


WORK PLANNED FOR PERIOD: FROM 14/06/10 TO 20/06/10

Description: (subject to weather conditions)
14/06/10: Normand Mermaid Cable Repairs, UR101 Jetting at Cable Crossings & MPI Resolution Installing WTG's
15/06/10: Normand Mermaid Cable Repairs, UR101 Jetting at Cable Crossings & MPI Resolution Installing WTG's
16/06/10: Normand Mermaid Cable Repairs, UR101 Jetting at Cable Crossings & MPI Resolution Installing WTG's
17/06/10: Normand Mermaid Cable Repairs, UR101 Jetting at Cable Crossings & MPI Resolution Installing WTG's
18/06/10: Normand Mermaid Cable Repairs, UR101 Jetting at Cable Crossings & MPI Resolution Installing WTG's
19/06/10: Normand Mermaid Cable Repairs, UR101 Jetting at Cable Crossings & MPI Resolution Installing WTG's
20/06/10: Normand Mermaid Cable Repairs, UR101 Jetting at Cable Crossings & MPI Resolution Installing WTG's
<ul style="list-style-type: none"> • MPI Resolution installing WTG's G07, G09, G08, G05, G04, F05 & E06(100th) • Multratug 18 to assist the non-propelled barge UR101 as required. • DP Ship Normand Mermaid conducting cable Repairs at mid point joints. • Barge UR101 shall be Jetting at cable crossings assisted by the tug Multra tug 18 and multicats Maggie M & Northern Kestrel. • DP ship Sia – second end cable pulling. • Crew boat OP3 for TOW terminators. • Crew boat Wildcat1 conducting crew changes for Forth jouter & Ocean Cat. • Crew boat Waterfall out for TOWSAPS and TOW Port Technicians. • Crew boat Sea Beaver assists Normand Mermaid. • Crew boats Lesley Jay, Wildcat 1, Ocean Cat & MPI Rucio servicing Forth Jouter & Sia. • Crew boats Endeavour, Enterprise, Windcat 12, Moidart and Wind Crew 1 for WTG access (Vestas) • M/S Sander performing post laid cable surveys. • Multicat Forth Jouter engaged in diving operations, diving surveys, messenger wire installations & cable remedial works. • Guard boats Ann Scott and Reliance in field for monitoring vessel movements and collision avoidance. • Strider, Sea Badger & Norfolk Swift assisting with Subocean termination works.

WORK COMPLETED FROM 07/05/10 TO 13/06/10

Date	Description
07/06/10	<ul style="list-style-type: none"> Resolution loading at Dunkirk, Normand Mermaid at B05 and Transit to Great Yarmouth, UR101 Laying concrete mattresses & Sia at F01 for 2nd end pull's.
08/07/10	<ul style="list-style-type: none"> Resolution loading at Dunkirk, Normand Mermaid at Great Yarmouth, UR101 Laying concrete mattresses & Sia at G02 2nd end pull.
09/07/10	<ul style="list-style-type: none"> Resolution loading at Dunkirk, Normand Mermaid at Great Yarmouth, UR101 Laying concrete mattresses & Sia at G07 & F03 2nd end pull's.
10/06/10	<ul style="list-style-type: none"> Resolution at WTG G11, Normand Mermaid at mid point cable repair location, UR101 Matting at Tangerine crossing & Sia at F03 / F13 2nd end pulls.
11/06/10	<ul style="list-style-type: none"> Resolution WTG G11, Normand Mermaid at mid point cable repair location, UR101 Matting at Tangerine crossing & Sia at F13 & F03 2nd end pulls.
12/06/10	<ul style="list-style-type: none"> Resolution at WTG G10, Normand Mermaid at mid point cable repair location, UR101 Matting/Jetting at Tangerine crossing, Sia at F13 for 2nd end pull.
13/06/10	<ul style="list-style-type: none"> Resolution at WTG C10 blade repair, Normand Mermaid at mid point cable repair location, UR101 Jetting at Tangerine & PEC crossings, Sia F03/G04 2nd end pulls.

Field Status Report 13th June 2010

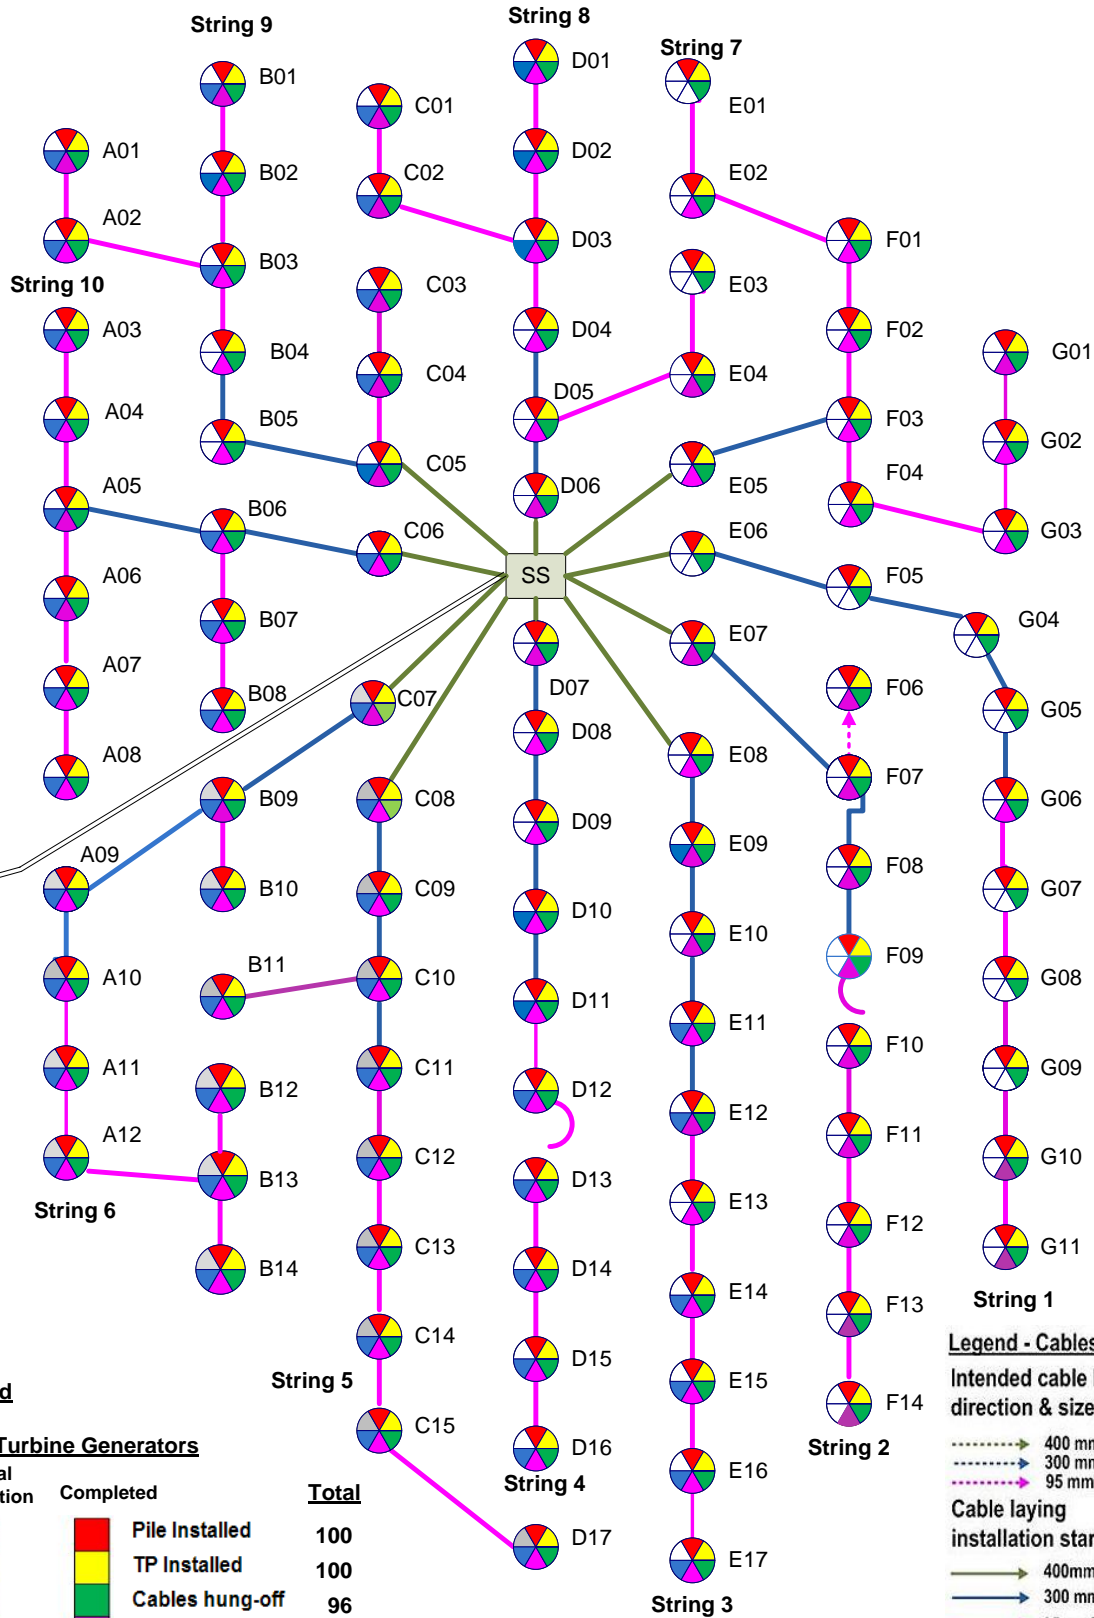

Legend

Wind Turbine Generators

Partial completion	Completed	Total
	Pile Installed	100
	TP Installed	100
	Cables hung-off	96
	WTG Installed	93
	Cables terminated	124
	Energised	10

Legend - Cables

Intended cable laying direction & size:

- 400 mm²
- 300 mm²
- 95 mm²

Cable laying installation started:

- 400mm²
- 300 mm²
- 95 mm²

Cable laying completed:

-

ON PROJECT VESSEL LIST:

Name	Type
Offshore Performer(OP3)	Crew vessel
Waterfall	Crew vessel
Wildcat 1	Crew Vessel
Sea Beaver	Crew vessel
Sea Badger	Crew vessel
Endeavour	Crew vessel
Enterprise	Crew vessel
Lesley Jay	Crew vessel
MPI Rucio	Crew vessel
Windcat 12	Crew vessel
Wind Crew 1	Crew vessel
Strider	Crew Vessel
Moidart	Crew vessel
Norfolk Swift	Crew vessel
MPI Resolution	Jack Up (DP) Installation v/l
Sia	DP cable installation ship
Normand Mermaid	Cable lay (DP) v/l
UR101	Cable lay barge
Multatug 18	Tug
Ocean Cat	Dive Support
Forth Joustier	Multicat Dive vessel
Maggie M	Multicat
Reliance	Guard Vessel
M/S Sander	Survey
Ann Scott	Guard vessel

NOTES

This document will be issued every Monday and will describe the planned activities for the next 7 days. Normal liaison for offshore operations is between the TOW Marine Coordinator and:

- Captain Rob Brown – Interim Harbour Master Port of Ramsgate; and
- Kaimes Beasley – CNIS Manager Dover MCA

This weekly report will be distributed to those recipients listed on the email address header on a weekly basis and is intended to inform those recipients of TOW's planned activities over the forthcoming week.

For further information or comments, please contact:

The Duty Marine Coordinator:

Office: +44 (0) 1843 572130

Mobile: +44 (0) 7825880528

Fax: +44 (0) 1843 572131

Email: marinecoordinator@thanetoffshorewind.com
