


Thanet Offshore Wind Limited
Weekly Notice of Operations to Stakeholders

Date of Notice 08/08/2010

Notice No.73

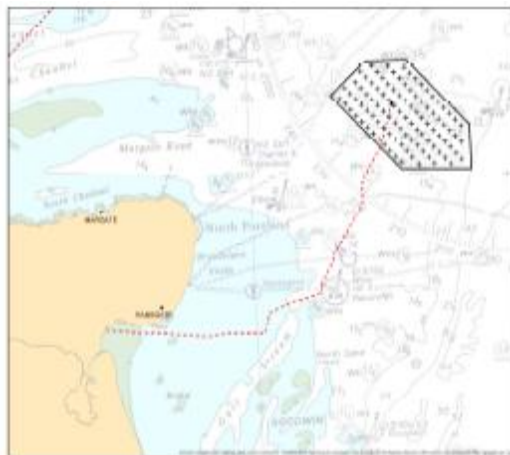

Distribution

See e-mail address header

WORK PLANNED FOR PERIOD: FROM 09/08/10 TO 15/08/10

Description: (subject to weather conditions)
09/08/10 - Forth Jouster engaged in diving operations. MS Nico cable trenching within boundaries of the windfarm. The Sia cable trenching within boundaries of windfarm.
10/08/10 - Forth Jouster engaged in diving operations. MS Nico and Sia cable trenching within boundaries of the windfarm.
11/08/10 - Forth Jouster engaged in diving operations. MS Nico and Sia cable trenching within boundaries of the windfarm.
12/08/10 - Forth Jouster engaged in diving operations, MS Nico and Sia cable trenching within boundaries of the windfarm.
13/08/10 - Forth Jouster engaged in diving operations, MS Nico and Sia cable trenching within boundaries of the windfarm.
14/08/10 - Forth Jouster engaged in diving operations, MS Nico and Sia cable trenching within boundaries of the windfarm.
15/08/10 - Forth Jouster engaged in diving operations, MS Nico and Sia cable trenching within boundaries of the windfarm.
<ul style="list-style-type: none"> • DP ship Sia – array cable operations
<ul style="list-style-type: none"> • Crew boat Waterfall and OP3 out for TOWSAPS and TOW Port Technicians
<ul style="list-style-type: none"> • Crew boats Waterfall and OP3 servicing Forth Jouster
<ul style="list-style-type: none"> • Crew boats Endeavour, Enterprise, Windcat 12 and Moidart for WTG access (Vestas)
<ul style="list-style-type: none"> • M/S Line performing post laid cable surveys.
<ul style="list-style-type: none"> • Multicat Forth Jouster engaged in diving operations, diving surveys, messenger wire installations & cable remedial works.
<ul style="list-style-type: none"> • Guard boats Ann Scott and Reliance in field for monitoring vessel movements and collision avoidance.
<ul style="list-style-type: none"> • Sea Badger assisting with Subocean cable termination works.
<ul style="list-style-type: none"> • MS Nico Carrying out cable trenching operations


WORK COMPLETED FROM 01/08/10 TO 07/08/10

Date	Description
01/08/10	<ul style="list-style-type: none"> • Contractors continue to Terminate, test and energise turbines. • Sia transpooling in Great Yarmouth. • Nico Trench jetting in pre-laid array cable.
02/08/10	<ul style="list-style-type: none"> • Contractors continue to Terminate, test and energise turbines. • Sia replacing D-14-D13. • Nico Trench jetting in pre-laid array cable.
03/08/10	<ul style="list-style-type: none"> • Contractors continue to Terminate, test and energise turbines. • Sia trenching array cables • Nico Trench jetting in pre-laid array cable.
04/08/10	<ul style="list-style-type: none"> • Contractors continue to Terminate, test and energise turbines. • Sia trenching array cables • Nico Trench jetting in pre-laid array cable
05/08/10	<ul style="list-style-type: none"> • Contractors continue to Terminate, test and energise turbines. • Sia trenching array cables • Nico Trench jetting in pre-laid array cable.
06/08/10	<ul style="list-style-type: none"> • Contractors continue to Terminate, test and energise turbines. • Sia trenching array cables • Nico Trench jetting in pre-laid array cable.
07/08/10	<ul style="list-style-type: none"> • Contractors continue to Terminate, test and energise turbines. • Sia trenching array cables • Nico Trench jetting in pre-laid array cable

ON PROJECT VESSEL LIST:






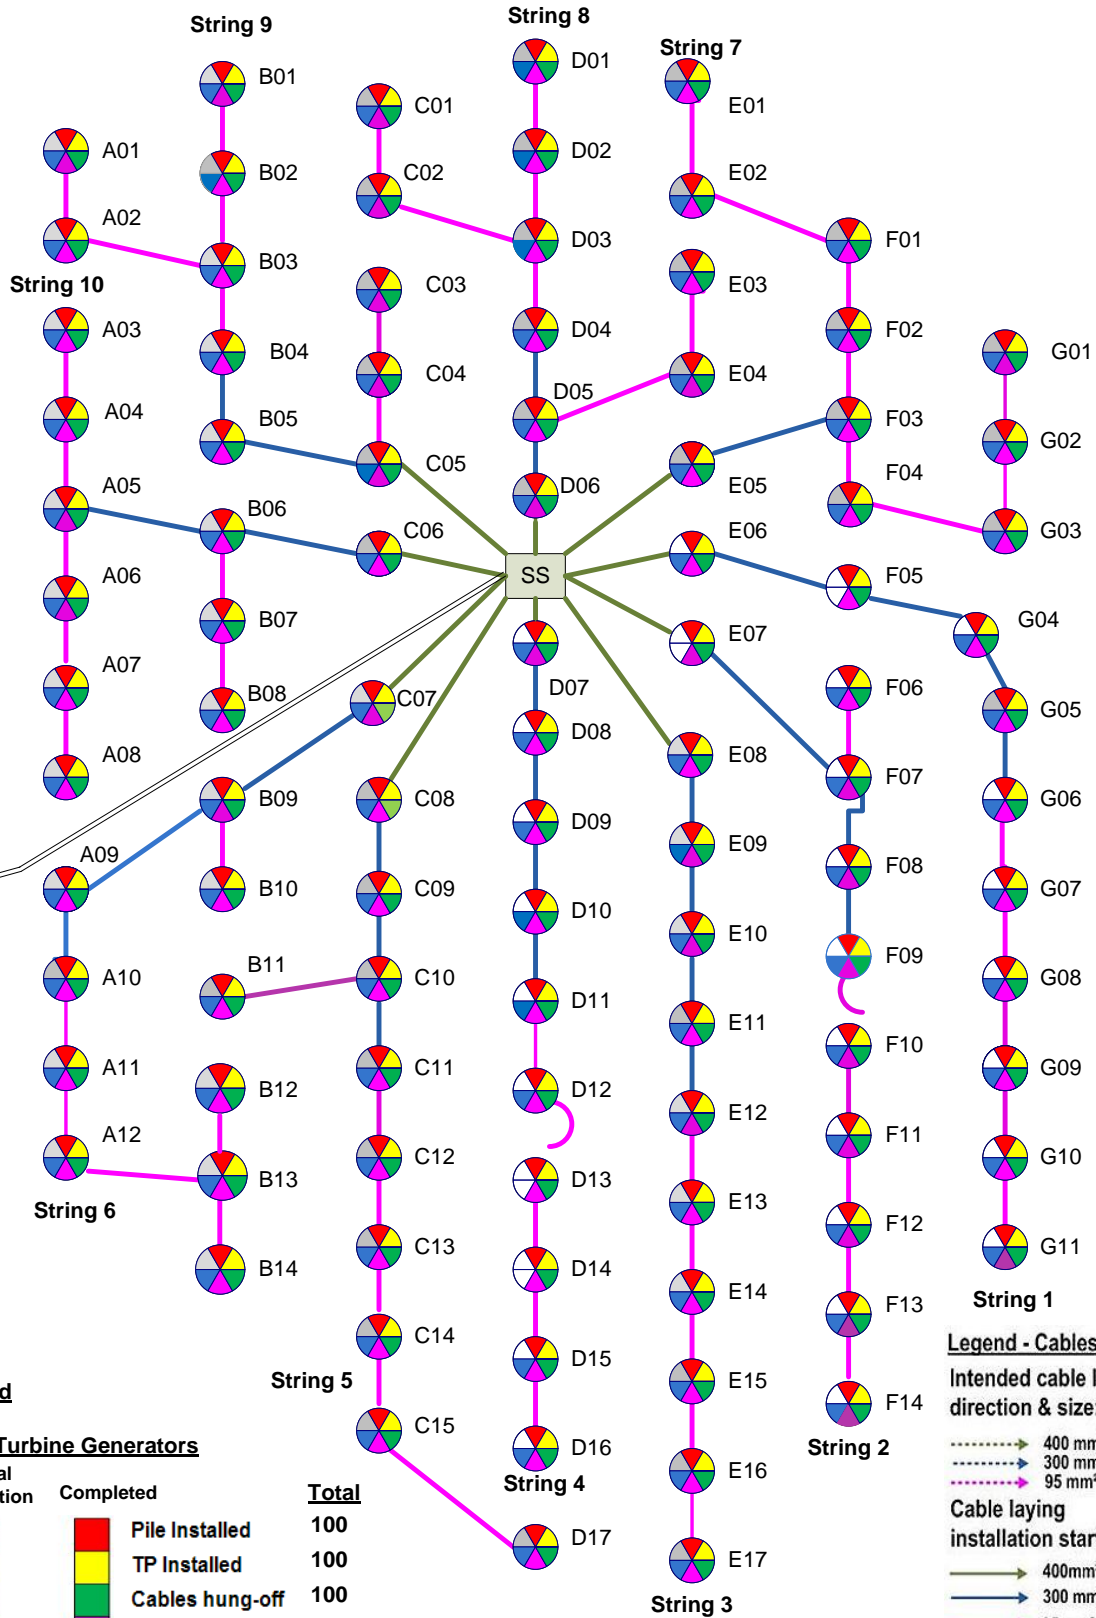






Name	Type
Offshore Performer(OP3)	Crew vessel
Waterfall	Crew vessel
Sea Badger	Crew vessel
Endeavour	Crew vessel
Enterprise	Crew vessel
Lesley Jay	Crew vessel
Windcat 12	Crew vessel
Moidart	Crew vessel
Forth Joustier	Multicat Dive vessel
Reliance	Guard Vessel
M/S Line	Survey
Ann Scott	Guard vessel
MS Nico	Trenching vessel
Sia	Cable vessel

Field Status Report 8th August 2010



Legend

Wind Turbine Generators

Partial completion	Completed	Total
	 Pile Installed	100
	 TP Installed	100
	 Cables hung-off	100
	 WTG Installed	100
	 Cables terminated	98
	 Energised	71

Legend - Cables

Intended cable laying direction & size:

-  400 mm²
-  300 mm²
-  95 mm²

Cable laying installation started:

-  400mm²
-  300 mm²
-  95 mm²

Cable laying completed:

- 

NOTES

This document will be issued every Monday and will describe the planned activities for the next 7 days. Normal liaison for offshore operations is between the TOW Marine Coordinator and:

- Captain Rob Brown – Interim Harbour Master Port of Ramsgate; and
- Kaimes Beasley – CNIS Manager Dover MCA

This weekly report will be distributed to those recipients listed on the email address header on a weekly basis and is intended to inform those recipients of TOW's planned activities over the forthcoming week.

For further information or comments, please contact:

The Duty Marine Coordinator:

Office: +44 (0) 1843 572130

Mobile: +44 (0) 7825880528

Fax: +44 (0) 1843 572131

Email: marinecoordinator@thanetoffshorewind.com
