


Thanet Offshore Wind Limited
Weekly Notice of Operations to Stakeholders

Date of Notice 12/09/2010

Notice No.78

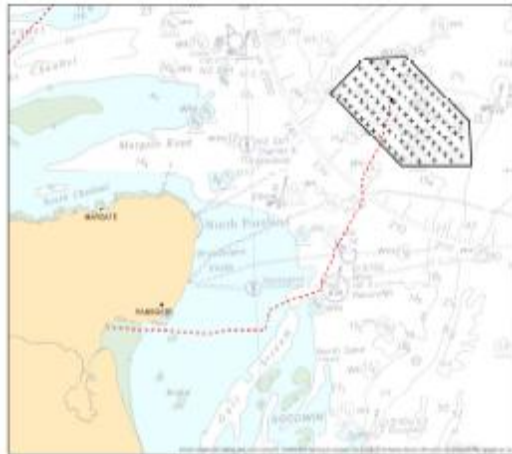

Distribution

See e-mail address header

WORK PLANNED FOR PERIOD: FROM 13/09/10 TO 19/09/10

Description: (subject to weather conditions)
13/09/10 - MS Nico and Sia cable trenching within boundaries of the windfarm.
14/09/10 - MS Nico and Sia cable trenching within boundaries of the windfarm.
15/09/10 - MS Nico and Sia cable trenching within boundaries of the windfarm.
16/09/10 - MS Nico and Sia cable trenching within boundaries of the windfarm.
17/09/10 - MS Nico and Sia cable trenching within boundaries of the windfarm.
18/09/10 - MS Nico and Sia cable trenching within boundaries of the windfarm.
19/09/10 - MS Nico and Sia cable trenching within boundaries of the windfarm.
<ul style="list-style-type: none"> • DP ship Sia – cable trenching operations.
<ul style="list-style-type: none"> • Crew boat Norfolk swift and OP3 out for TOWSAPS, TOW Port Technicians and remedial works.
<ul style="list-style-type: none"> • Crew boats Endeavour, Enterprise and Moidart for WTG access (Vestas)
<ul style="list-style-type: none"> • M/S Sander performing post laid cable surveys.
<ul style="list-style-type: none"> • Guard boats Brockelsby and Reliance in field for monitoring vessel movements and collision avoidance.
<ul style="list-style-type: none"> • MS Nico - cable trenching operations


WORK COMPLETED FROM 06/09/10 TO 12/09/10

Date	Description
06/09/10	<ul style="list-style-type: none"> • Contractors continue to Terminate, test and energise turbines. • Nico Trench jetting in pre-laid array cable.
07/09/10	<ul style="list-style-type: none"> • Contractors continue to Terminate, test and energise turbines. • Nico Trench jetting in pre-laid array cable.
08/09/10	<ul style="list-style-type: none"> • Contractors continue to Terminate, test and energise turbines. • Nico and Sia trench jetting in pre-laid array cable.
09/09/10	<ul style="list-style-type: none"> • Contractors performing snagging list items on turbines. • Nico and Sia trench jetting in pre-laid array cable.
10/09/10	<ul style="list-style-type: none"> • Contractors performing snagging list items on turbines. • Nico trench jetting in pre-laid array cable.
11/09/10	<ul style="list-style-type: none"> • Contractors performing snagging list items on turbines. • Nico trench jetting in pre-laid array cable.
12/09/10	<ul style="list-style-type: none"> • Contractors performing snagging list items on turbines. • Nico trench jetting in pre-laid array cable.

ON PROJECT VESSEL LIST:

Name	Type
Offshore Performer(OP3)	Crew vessel
Norfolk Swift	Crew vessel
Endeavour	Crew vessel
Enterprise	Crew vessel
Moidart	Crew vessel
Reliance	Guard Vessel
M/S Line	Survey
Brockelsby	Guard vessel
MS Nico	Cable trenching vessel
Sia	Cable trenching vessel

Field Status Report 12th September 2010

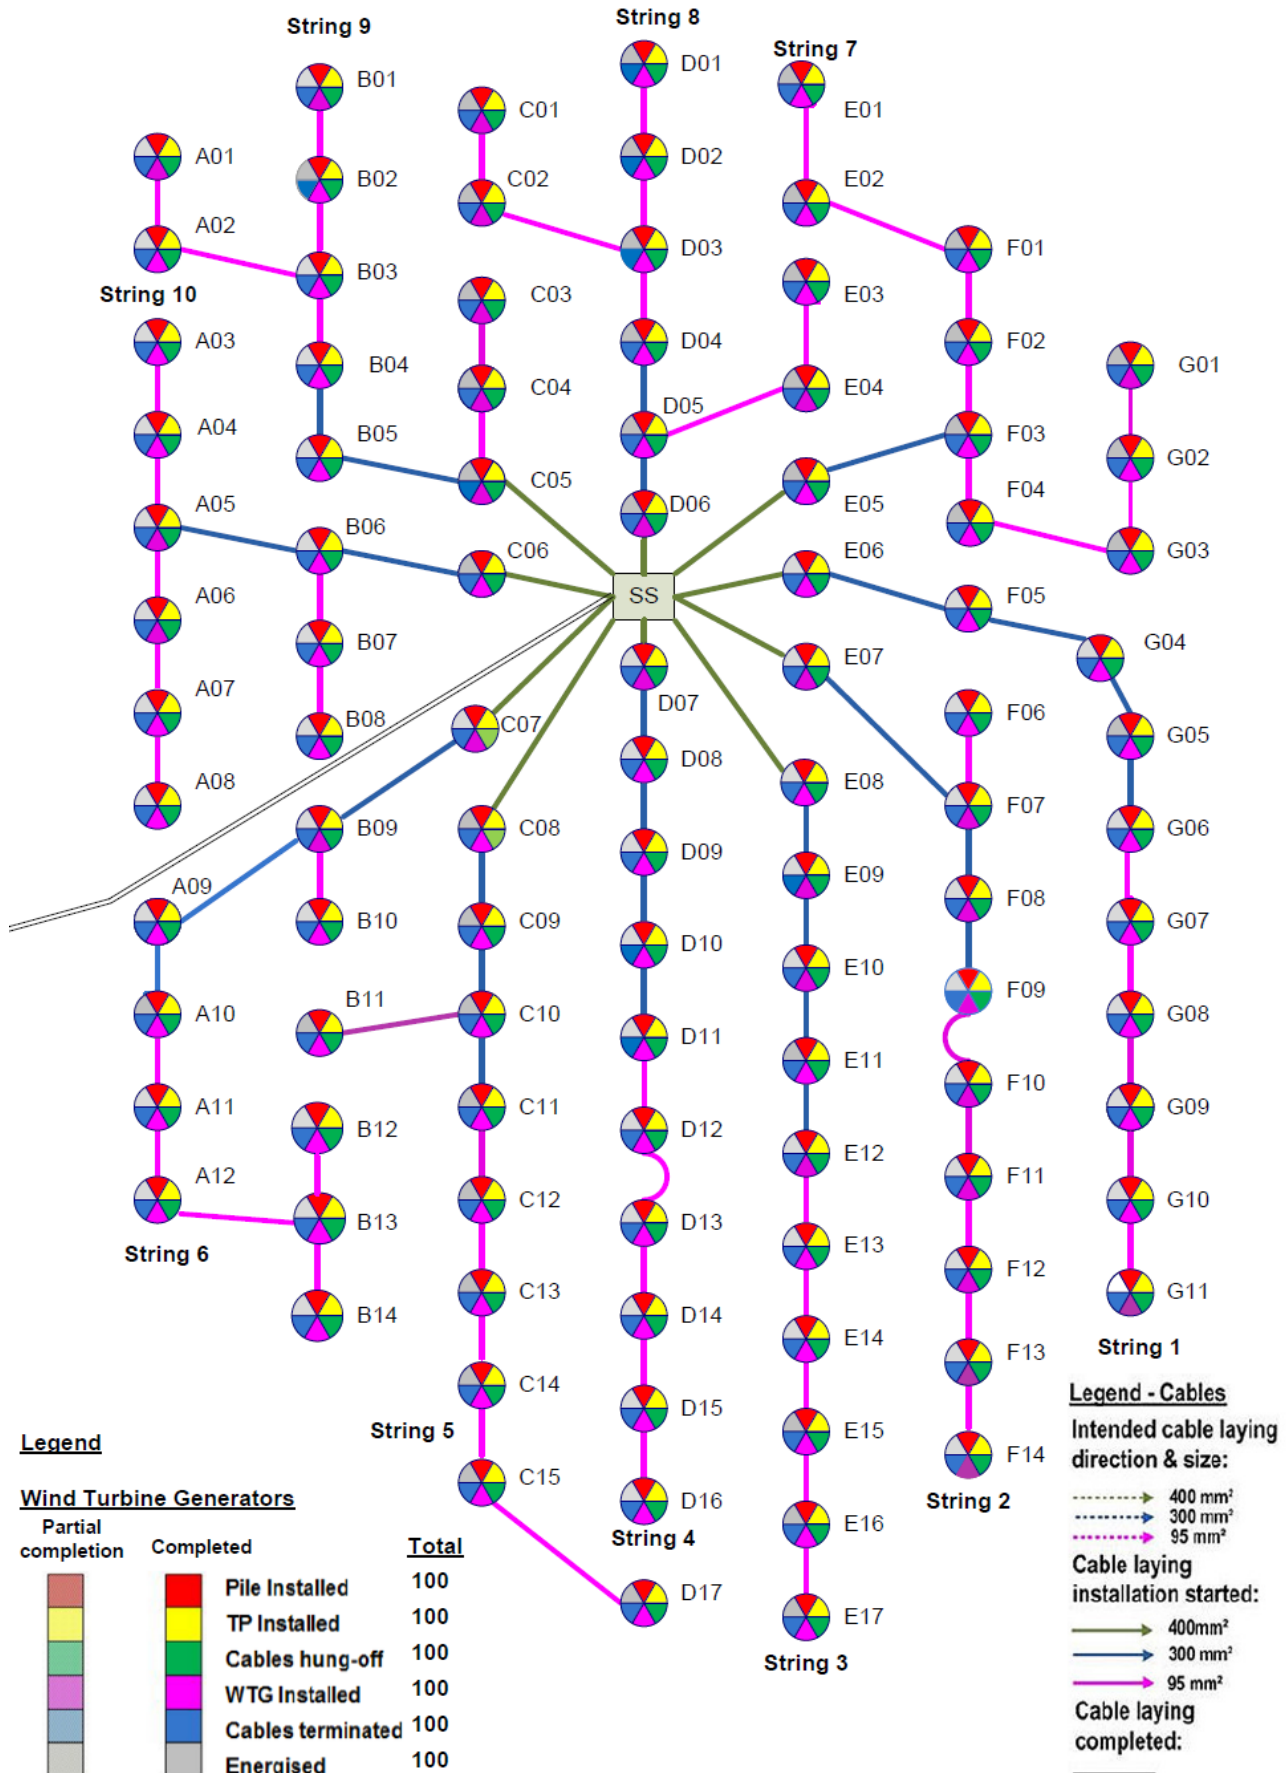

NOTES

This document will be issued every Monday and will describe the planned activities for the next 7 days. Normal liaison for offshore operations is between the TOW Marine Coordinator and:

- Captain Rob Brown – Interim Harbour Master Port of Ramsgate; and
- Kaimes Beasley – CNIS Manager Dover MCA

This weekly report will be distributed to those recipients listed on the email address header on a weekly basis and is intended to inform those recipients of TOW's planned activities over the forthcoming week.

For further information or comments, please contact:

The Duty Marine Coordinator:

Office: +44 (0) 1843 572130

Mobile: +44 (0) 7825880528

Fax: +44 (0) 1843 572131

Email: marinecoordinator@thanetoffshorewind.com
