


Thanet Offshore Wind Limited  
**Weekly Notice of Operations to Stakeholders**

---

**Date of Notice 19/09/2010**

**Notice No.79**

---

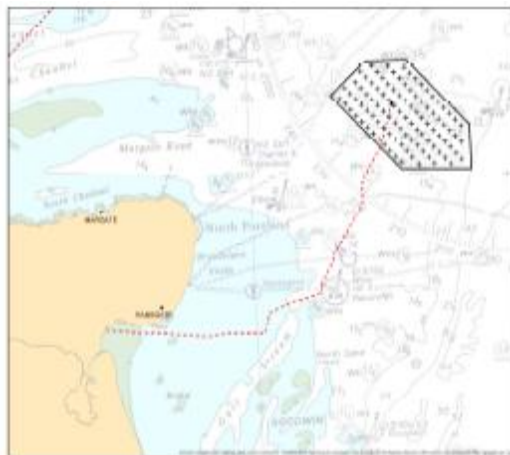

**Distribution**

See e-mail address header

**WORK PLANNED FOR PERIOD: FROM 20/09/10 TO 26/09/10**

<b>Description:</b> (subject to weather conditions)
20/09/10 - MS Nico and Sia cable trenching within boundaries of the windfarm.
21/09/10 - MS Nico and Sia cable trenching within boundaries of the windfarm.
22/09/10 - MS Nico and Sia cable trenching within boundaries of the windfarm.
23/09/10 - MS Nico and Sia cable trenching within boundaries of the windfarm.
24/09/10 - MS Nico and Sia cable trenching within boundaries of the windfarm.
25/09/10 - MS Nico and Sia cable trenching within boundaries of the windfarm.
26/09/10 - MS Nico and Sia cable trenching within boundaries of the windfarm.
<ul style="list-style-type: none"> <li>• DP ship Sia – cable trenching operations.</li> </ul>
<ul style="list-style-type: none"> <li>• Crew boat Norfolk swift and OP3 out for TOWSAPS, TOW Port Technicians and remedial works.</li> </ul>
<ul style="list-style-type: none"> <li>• Crew boats Endeavour, Enterprise and Moidart for WTG access (Vestas)</li> </ul>
<ul style="list-style-type: none"> <li>• M/S Sander performing post laid cable surveys.</li> </ul>
<ul style="list-style-type: none"> <li>• Guard boats Brockelsby and Anne Scott in field for monitoring vessel movements and collision avoidance.</li> </ul>
<ul style="list-style-type: none"> <li>• MS Nico and Sia - cable trenching operations</li> </ul>


**WORK COMPLETED FROM 13/09/10 TO 19/09/10**

<b>Date</b>	<b>Description</b>
13/09/10	<ul style="list-style-type: none"> <li>• Contractors performing snagging list items on turbines.</li> <li>• Nico and Sia trench jetting in pre-laid array cable.</li> </ul>
14/09/10	<ul style="list-style-type: none"> <li>• Contractors performing snagging list items on turbines.</li> <li>• Nico and Sia trench jetting in pre-laid array cable.</li> </ul>
15/09/10	<ul style="list-style-type: none"> <li>• Contractors performing snagging list items on turbines.</li> <li>• Nico and Sia trench jetting in pre-laid array cable.</li> </ul>
16/09/10	<ul style="list-style-type: none"> <li>• Contractors performing snagging list items on turbines.</li> <li>• Nico and Sia trench jetting in pre-laid array cable.</li> </ul>
17/09/10	<ul style="list-style-type: none"> <li>• Contractors performing snagging list items on turbines.</li> <li>• Nico and Sia trench jetting in pre-laid array cable.</li> </ul>
18/09/10	<ul style="list-style-type: none"> <li>• Contractors performing snagging list items on turbines.</li> <li>• Nico and Sia trench jetting in pre-laid array cable.</li> </ul>
19/09/10	<ul style="list-style-type: none"> <li>• Contractors performing snagging list items on turbines.</li> <li>• Nico and Sia trench jetting in pre-laid array cable.</li> </ul>

**ON PROJECT VESSEL LIST:**





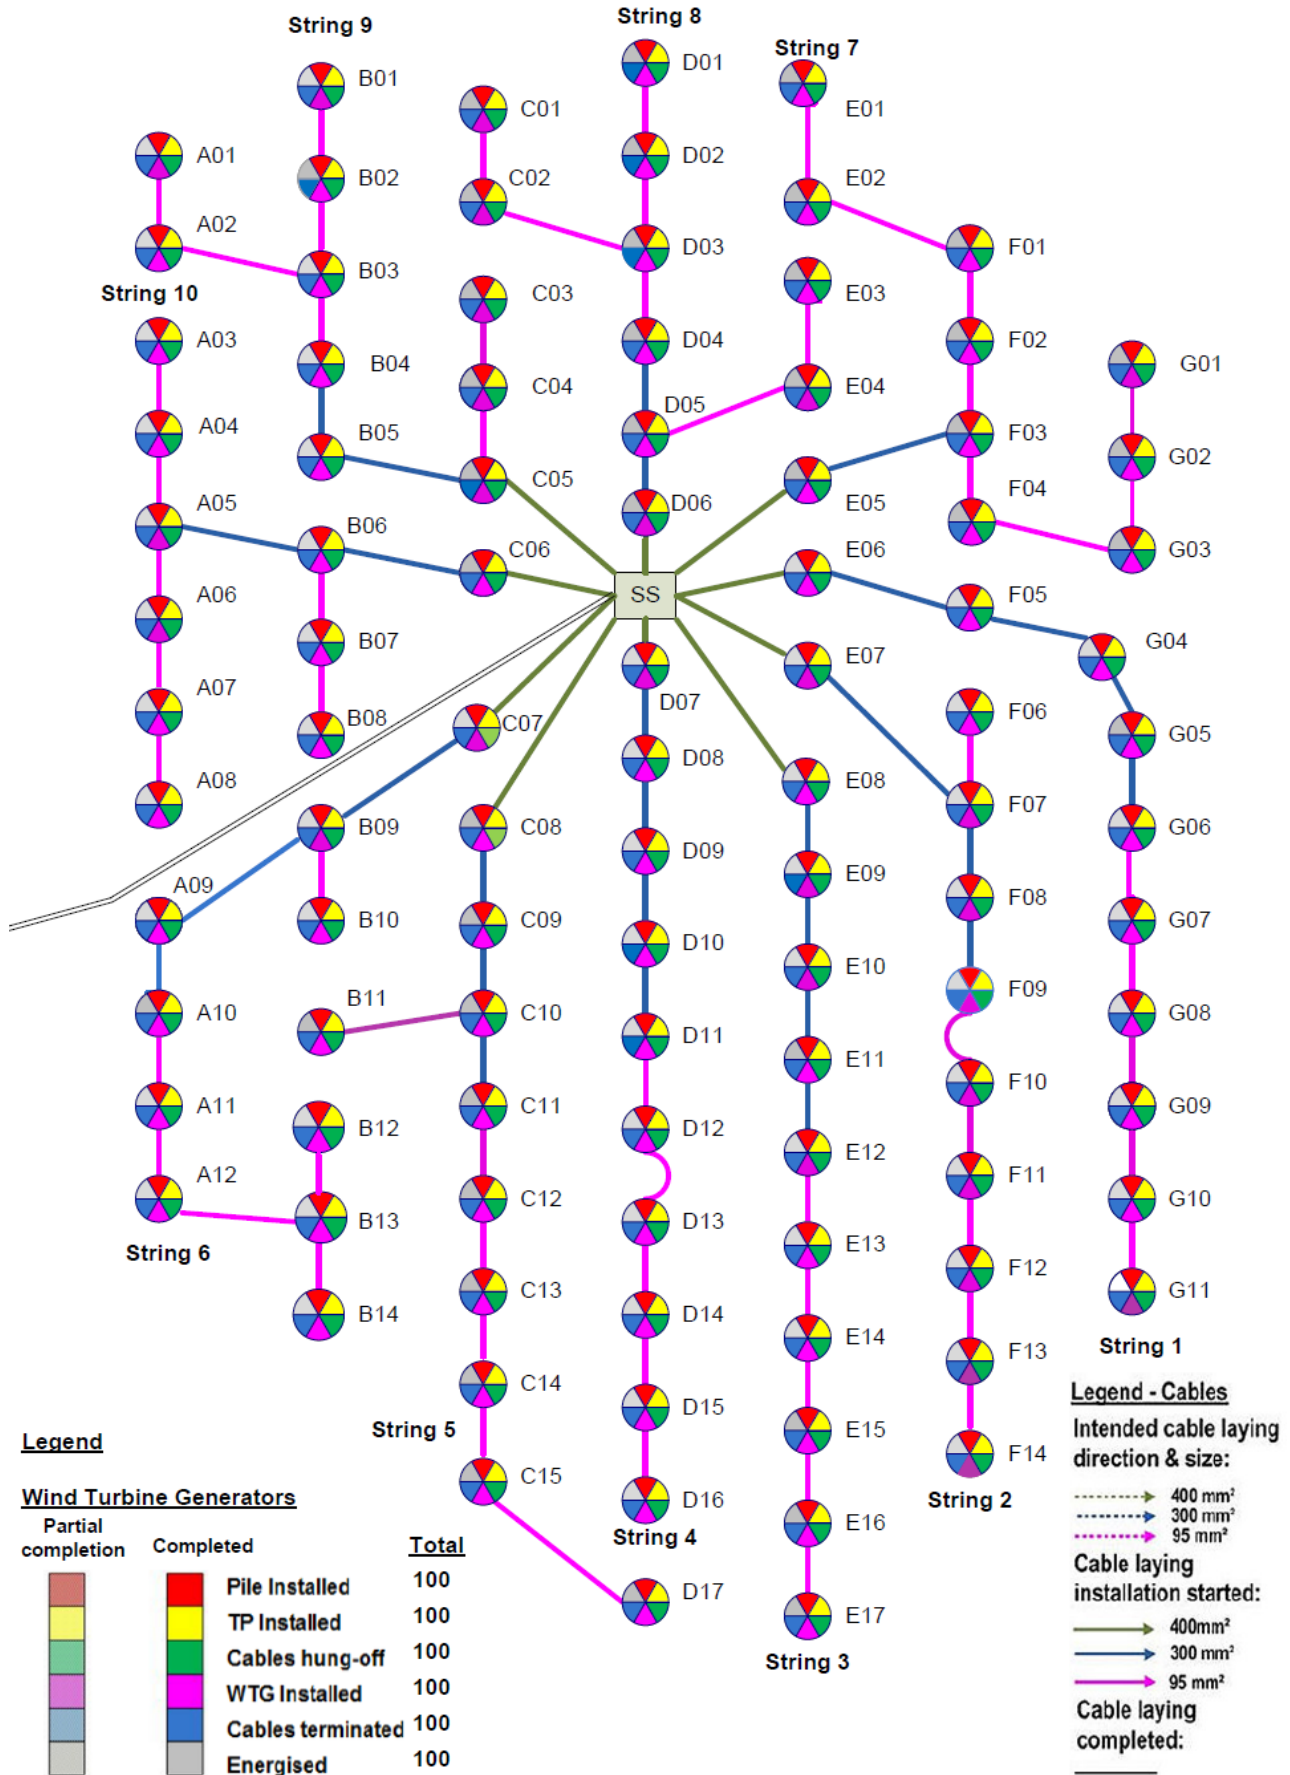





Name	Type
Offshore Performer (OP3)	Crew vessel
Norfolk Swift	Crew vessel
Endeavour	Crew vessel
Enterprise	Crew vessel
Moidart	Crew vessel
Anne Scott	Guard Vessel
Sander	Survey
Brockelsby	Guard vessel
MS Nico	Cable trenching vessel
Sia	Cable trenching vessel

**Field Status Report 19th September 2010**






**Legend**

**Wind Turbine Generators**




Partial completion	Completed	Total
	 <b>WTG Installed</b>	100
	 <b>TP Installed</b>	100
	 <b>Cables hung-off</b>	100
	 <b>Cables terminated</b>	100
	 <b>Energised</b>	100

**Legend - Cables**

Intended cable laying direction & size:

-  400 mm<sup>2</sup>
-  300 mm<sup>2</sup>
-  95 mm<sup>2</sup>

Cable laying installation started:

-  400mm<sup>2</sup>
-  300 mm<sup>2</sup>
-  95 mm<sup>2</sup>

Cable laying completed:

- 

## **NOTES**

This document will be issued every Monday and will describe the planned activities for the next 7 days. Normal liaison for offshore operations is between the TOW Marine Coordinator and:

- Captain Rob Brown – Interim Harbour Master Port of Ramsgate; and
- Kaimes Beasley – CNIS Manager Dover MCA

This weekly report will be distributed to those recipients listed on the email address header on a weekly basis and is intended to inform those recipients of TOW's planned activities over the forthcoming week.

For further information or comments, please contact:

### **The Duty Marine Coordinator:**

**Office:** +44 (0) 1843 572130

**Mobile:** +44 (0) 7825880528

**Fax:** +44 (0) 1843 572131

**Email:** [marinecoordinator@thanetoffshorewind.com](mailto:marinecoordinator@thanetoffshorewind.com)
