


Thanet Offshore Wind Limited

Weekly Notice of Operations to Stakeholders

Date of Notice 28/11/2010

Notice No.89

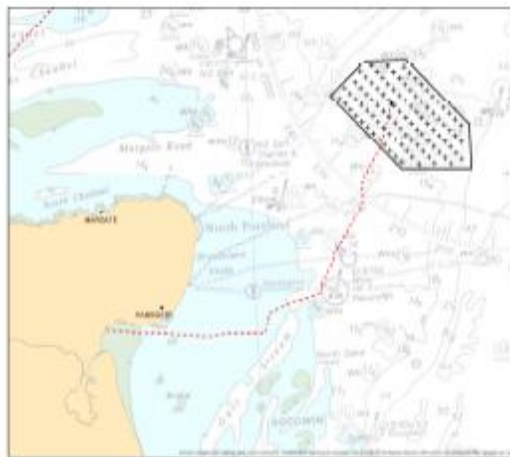

Distribution

See e-mail address header

WORK PLANNED FOR PERIOD: FROM 29/11/10 TO 05/12/10

Description: (subject to weather conditions)
29/11/10 - MS Nico and Sia cable trenching within boundaries of the windfarm.
30/11/10 - MS Nico and Sia cable trenching within boundaries of the windfarm.
01/12/10 - MS Nico and Sia cable trenching within boundaries of the windfarm.
02/12/10 - MS Nico and Sia cable trenching within boundaries of the windfarm.
03/12/10 - MS Nico and Sia cable trenching within boundaries of the windfarm.
04/12/10 - MS Nico and Sia cable trenching within boundaries of the windfarm.
05/12/10 - MS Nico and Sia cable trenching within boundaries of the windfarm.
<ul style="list-style-type: none"> • DP ship Sia – cable-trenching operations.
<ul style="list-style-type: none"> • Crew boat, OP3 out for TOW SAPS, TOW Port Technicians and remedial works.
<ul style="list-style-type: none"> • Crew boats Endeavour, Enterprise & Windcat 25 for WTG access (Vestas)
<ul style="list-style-type: none"> • M/S Sander performing post laid cable surveys.
<ul style="list-style-type: none"> • Guard boats Brockelsby and Anne Scott in field for monitoring vessel movements and collision avoidance.
<ul style="list-style-type: none"> • MS Nico - cable trenching operations
<ul style="list-style-type: none"> • Valkyrie – Confined space teams


WORK COMPLETED FROM 22/11/10 TO 28/11/10

Date	Description
22/11/10	<ul style="list-style-type: none"> • Contractors performing snagging list items on turbines. • Nico and Sia trench jetting in pre-laid array cable.
23/11/10	<ul style="list-style-type: none"> • Contractors performing snagging list items on turbines. • Nico and Sia trench jetting in pre-laid array cable.
24/11/10	<ul style="list-style-type: none"> • Contractors performing snagging list items on turbines. • Nico and Sia trench jetting in pre-laid array cable.
25/11/10	<ul style="list-style-type: none"> • Contractors performing snagging list items on turbines. • Nico and Sia trench jetting in pre-laid array cable.
26/11/10	<ul style="list-style-type: none"> • Contractors performing snagging list items on turbines. • Nico and Sia trench jetting in pre-laid array cable.
27/11/10	<ul style="list-style-type: none"> • Contractors performing snagging list items on turbines. • Nico and Sia trench jetting in pre-laid array cable.
28/11/10	<ul style="list-style-type: none"> • Contractors performing snagging list items on turbines. • Nico and Sia trench jetting in pre-laid array cable.

ON PROJECT VESSEL LIST:

Name	Type
Offshore Performer (OP3)	Crew vessel
Valkyrie	Crew vessel
Endeavour	Crew vessel
Enterprise	Crew vessel
Windcat 25	Crew vessel
Anne Scott	Guard Vessel
Brocklesby	Guard Vessel
Sander	Survey
MS Nico	Cable trenching vessel
Sia	Cable trenching vessel

Field Status Report 28th November 2010

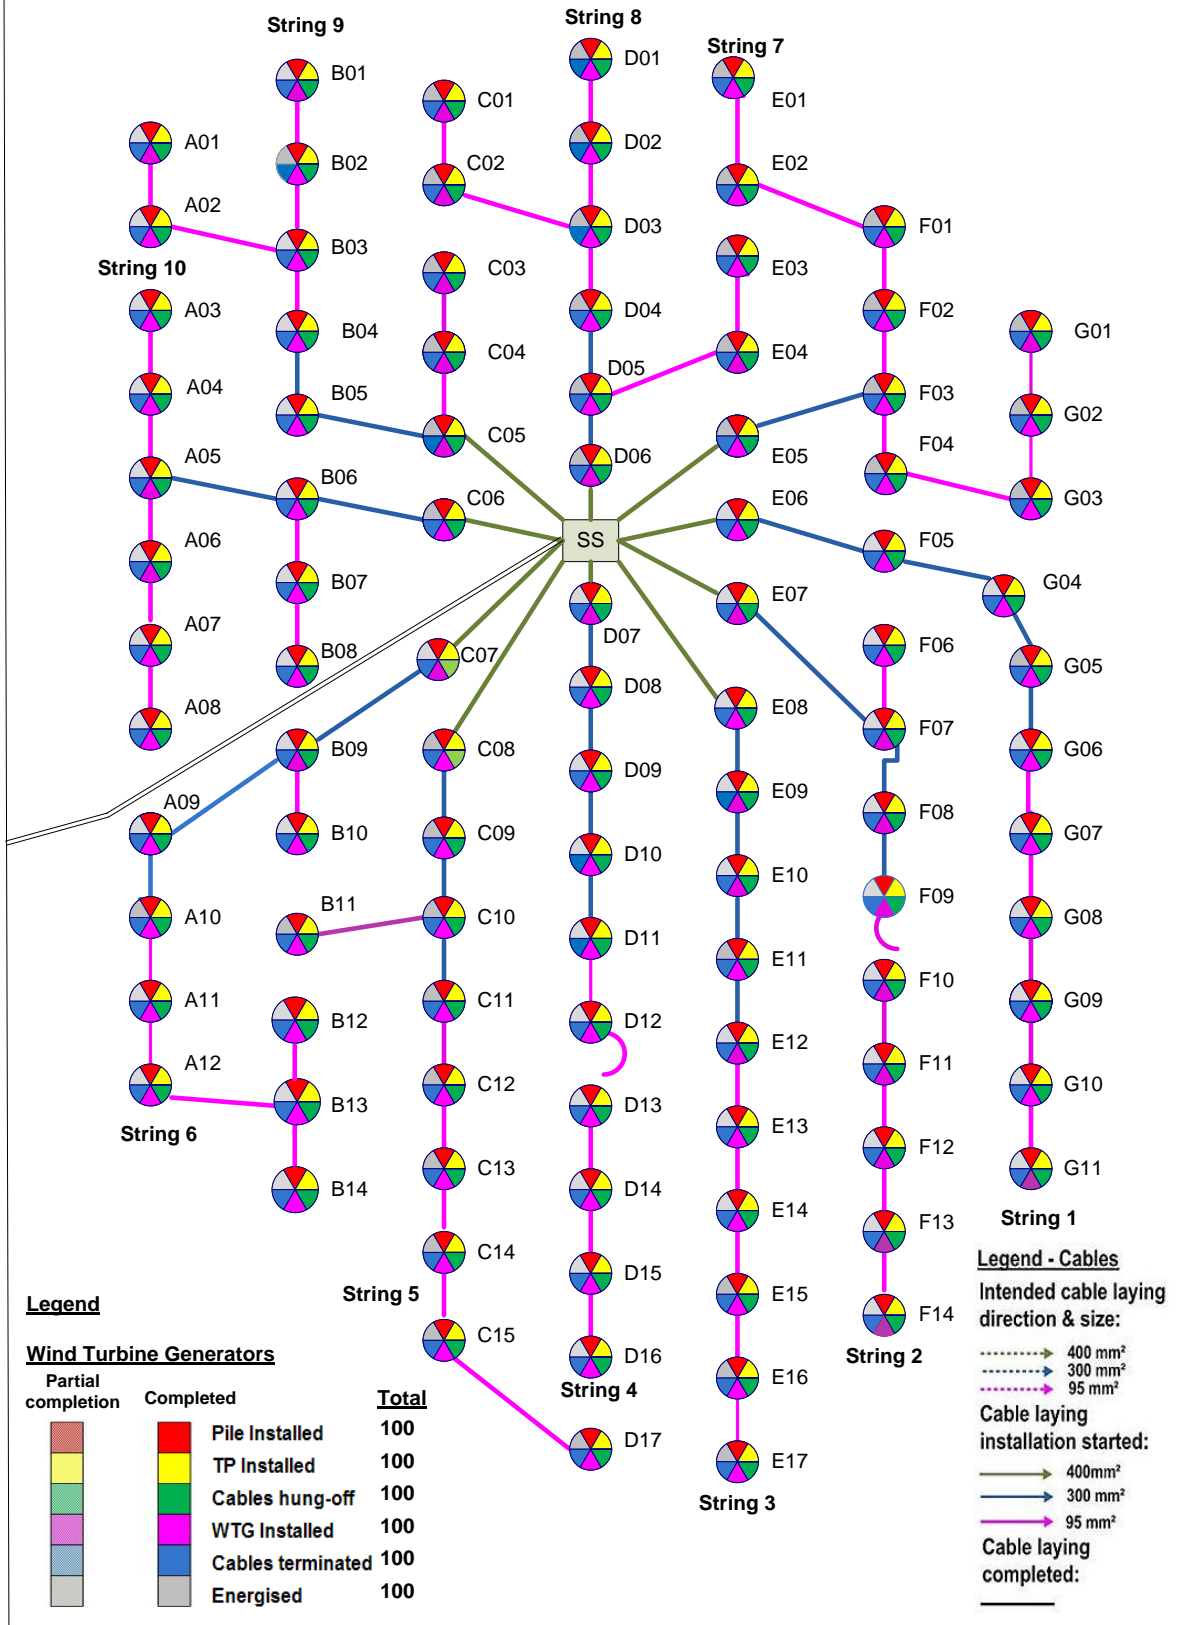

NOTES

This document will be issued every Monday and will describe the planned activities for the next 7 days. Normal liaison for offshore operations is between the TOW Marine Coordinator and:

- Captain Rob Brown – Interim Harbour Master Port of Ramsgate; and
- Kaimes Beasley – CNIS Manager Dover MCA

This weekly report will be distributed to those recipients listed on the email address header on a weekly basis and is intended to inform those recipients of TOW's planned activities over the forthcoming week.

For further information or comments, please contact:

The Duty Marine Coordinator:

Office: +44 (0) 1843 572130

Mobile: +44 (0) 7825880528

Fax: +44 (0) 1843 572131

Email: marinecoordinator@thanetoffshorewind.com
