

# Thanet Offshore Wind Limited


## Weekly Notice of Operations to Stakeholders

---

Date of Notice 08/03/2010

Notice No.51

---

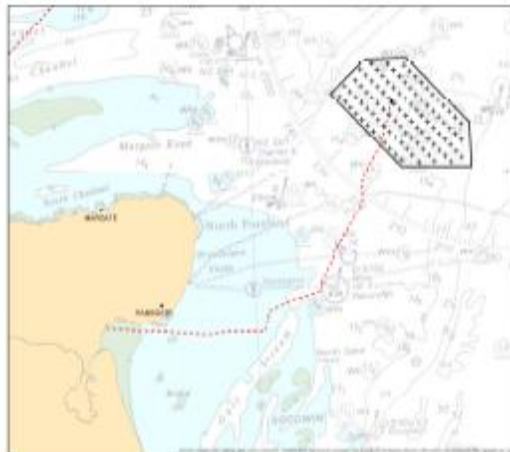

### Distribution

See e-mail address header

**WORK PLANNED FOR PERIOD: FROM 08/03/10 TO 14/03/10**


<b>Description:</b> (subject to weather conditions)
08/03/10 – Resolution install WTG at A06.UR101 cable lay from Pegwell Bay towards substn. Sea Jack install TP at F10. Polar Prince lay cable at D06-D05. Normand Mermaid lay cable at F03-F02.
09/03/10 - Resolution install WTG at A06. UR101 cable lay from Pegwell Bay towards substn. Sea Jack in Ramsgate for load-out. Polar Prince lay cable at D06-D05. Normand Mermaid lay cable at F03-F02.
10/03/10 - Resolution install WTG at B09 WOW. UR101 cable lay from Pegwell Bay towards substn. Sea Jack in Ramsgate for load-out. Polar Prince lay cable at E10-E09. Normand Mermaid lay cable at F02-F01.
11/03/10 - Resolution install WTG at B09 WOW. UR101 cable lay from Pegwell Bay towards substn. Sea Jack at D07. Polar Prince lay cable at E11-E10. Normand Mermaid lay cable at C04-C03
12/03/10 – Resolution install WTG at B09. UR101 cable lay from Pegwell Bay towards substn. Sea Jack install TP at D07. Polar Prince lay cable at D05-D04. Normand Mermaid lay cable at C04-C03.
13/03/10 – Resolution install WTG at B09. UR101 cable lay from Pegwell Bay towards substn. Sea Jack install TP at E05. Polar Prince lay cable at D05-D04. Normand Mermaid lay cable at C05-C04.
14/03/10 - Resolution completed B09 and depart for Dunkirk. UR101 cable lay from Pegwell Bay towards substn. Sea Jack install TP at E05. Polar Prince lay cable at D05-D04. Normand Mermaid lay cable at C05-C04.
<ul style="list-style-type: none"> <li>• Tugs Stevns Arctic and Bever tow tugs and field support for Sea Jack.</li> <li>• Tug Osprey Boxer towing transition piece supply barges to / from Ramsgate &amp; Vlissingen.</li> <li>• Tug Meander assisting Sea Jack and Osprey Fighter as required.</li> <li>• Multratug 18 to assist the non-propelled barge UR101 as required.</li> <li>• DP Ship Polar Prince cable laying – Inter array cables between turbine foundations.</li> <li>• DP Ship Normand Mermaid cable laying – Inter array cables between turbine foundations</li> <li>• Barge UR101 cable laying - export cables from Pegwell Bay.</li> <li>• Crew boat Waterfall performing crew changes and diving ops.</li> <li>• Crew boat Offshore Performer (OP3) assisting with crew changes, &amp; TP maintenance</li> <li>• Crew boats Sea Weasel, Sea Beaver &amp; Sea Badger for crew changes to Polar Prince &amp; Normand Mermaid (Subocean).</li> <li>• Crew boats Strider, Lesley Jay, Supporter, Voyageur &amp; Distributor servicing Multicats Forth Jouster and Forth Fighter</li> <li>• Crew boats Endeavour, Enterprise &amp; George D for WTG access (Vestas)</li> <li>• M/S Line performing post laid cable surveys.</li> <li>• Multicat Forth Jouster &amp; Forth Fighter assisting with TP maintenance and diving</li> </ul>

operations, diving surveys & 2 <sup>nd</sup> end cable pull-ins
<ul style="list-style-type: none"> <li>• Guard boat Gitte in field for monitoring vessel movements and collision avoidance.</li> </ul>
<ul style="list-style-type: none"> <li>• Fishing vessel Arie Dirk used for environmental surveys.</li> </ul>
<ul style="list-style-type: none"> <li>• Tug DMS Global supporting Oil Express with cable cross pre-lay cable mattress installation</li> </ul>

**WORK COMPLETED FROM: 01/03/10 TO 07/03/10**

<b>Date</b>	<b>Description</b>
01/03/10	<ul style="list-style-type: none"> <li>• Laid cable B06-C06. Installed WTG at A03</li> </ul>
02/03/10	<ul style="list-style-type: none"> <li>• Laid cable B05-C05. Installed WTG at B04.</li> </ul>
03/03/10	<ul style="list-style-type: none"> <li>• WOW</li> </ul>
04/03/10	<ul style="list-style-type: none"> <li>• WOW</li> </ul>
05/03/10	<ul style="list-style-type: none"> <li>• Laid cable C09-C08. Installed WTG at A04</li> </ul>
06/03/10	<ul style="list-style-type: none"> <li>• WOW.</li> </ul>
07/03/10	<ul style="list-style-type: none"> <li>• Installed TP at G08.</li> </ul>

**Field Status Report 7th March 2010**

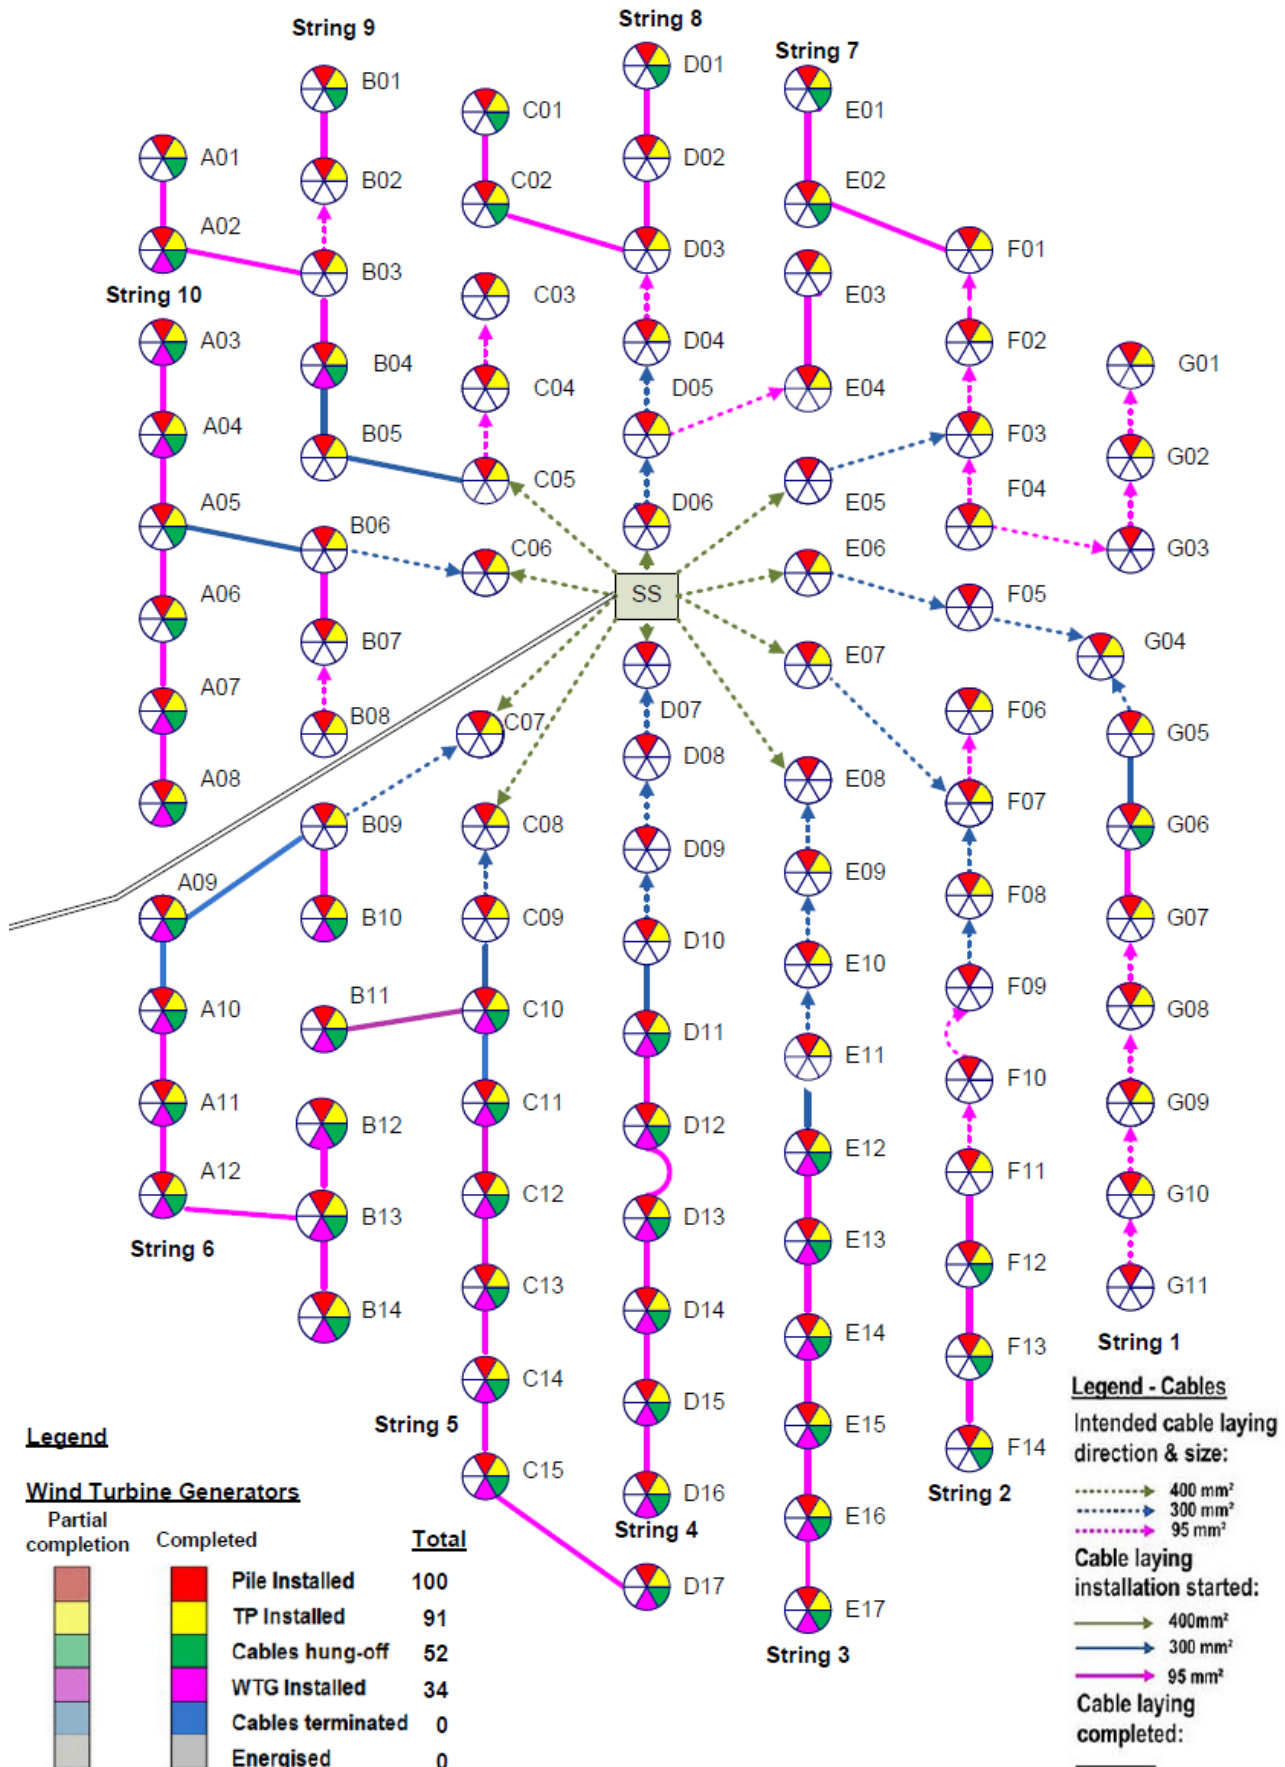

## ON PROJECT VESSEL LIST :

Name	Type
Offshore Performer(OP3)	Crew vessel
Waterfall	Crew/diving vessel
Sea Weasel	Crew vessel
Sea Beaver	Crew vessel
Sea Badger	Crew vessel
Endeavour	Crew vessel
Enterprise	Crew vessel
Meriel D	Crew vessel
Strider & Lesley Jay	Crew vessel
Distributor	Crew vessel
Supporter	Crew vessel
Windcat 12	Crew vessel
Gitte	Guard vessel
Bever	Tug
Stevns Arctic	Tug
Meander	Tug
Osprey Boxer	Tug
Multatug 18	Tug
Sea Jack	Jack Up
MPI Resolution	Jack Up (DP)
Polar Prince	Cable lay (DP)
Normand Mermaid	Cable lay (DP)
UR101	Cable lay barge
M/S Line	Survey
Arie Dirk	Environmental (Birds)
Forth Joust & Forth Fighter	Multicat
Voe Viking	Multicat
Oil Express	Diving Support Vessel
George D	Crew vessel
Ocean Cat	Crew vessel

## NOTES

This document will be issued every Monday and will describe the planned activities for the next 7 days. Normal liaison for offshore operations is between the TOW Marine Coordinator and:

- Captain Rob Brown – Interim Harbour Master Port of Ramsgate; and
- Kaimes Beasley – CNIS Manager Dover MCA

This weekly report will be distributed to those recipients listed on the email address header on a weekly basis and is intended to inform those recipients of TOW's planned activities over the forthcoming week.

For further information or comments please contact:

**The Duty Marine Coordinator:**

**Office:** +44 (0) 1843 572130

**Mobile:** +44 (0) 7825880528

**Fax:** +44 (0) 1843 572131

**Email:** [marinecoordinator@thanetoffshorewind.com](mailto:marinecoordinator@thanetoffshorewind.com)
