

# Thanet Offshore Wind Limited


## Weekly Notice of Operations to Stakeholders

---

Date of Notice 28/09/09

Notice No.28

---

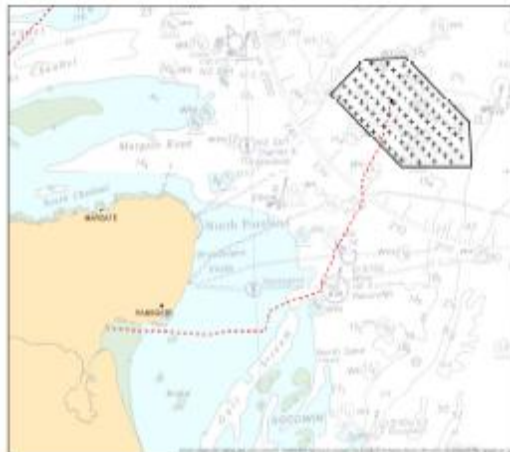

### Distribution

See e-mail address header

## WORK PLANNED FOR PERIOD: FROM 28/09/09 TO 04/10/09


Description: (subject to weather conditions)
<ul style="list-style-type: none"> <li>28/09/09 – Sea Jack departs Ramsgate to B02. Resolution installing TP F13. Voe Jarl continues with prelay grapnel run operations in field. Polar Prince arrives to conduct DP trials and commence cable installation programme at C11</li> </ul>
<ul style="list-style-type: none"> <li>29/09/09 – Sea Jack relocates to B03. Resolution installs TP G07. Voe Jarl continues with prelay grapnel run operations in field. Polar Prince installing cable between C11 &amp; C10</li> </ul>
<ul style="list-style-type: none"> <li>30/09/09 – Sea Jack in Ramsgate to load out. Resolution installing TP F06. Voe Jarl continues with prelay grapnel run operations in field. Polar Prince installing cable between C10 &amp; C09</li> </ul>
<ul style="list-style-type: none"> <li>01/10/09 – Sea Jack installing B01. Resolution installing TP C06. Voe Jarl continues with prelay grapnel run operations in field. Polar Prince installing cable between C10, C09 &amp; A09</li> </ul>
<ul style="list-style-type: none"> <li>02/10/09 – Sea Jack installing D06. Resolution installing TP D04. Voe Jarl continues with prelay grapnel run operations in field. Polar Prince installing cable between A09 &amp; A10</li> </ul>
<ul style="list-style-type: none"> <li>03/10/09 – Sea Jack in Ramsgate to load out. Resolution installing TP D01. Voe Jarl continues with prelay grapnel run operations in field. Polar Prince continues with cable installation programme</li> </ul>
<ul style="list-style-type: none"> <li>04/10/09 – Sea Jack installing D09. Resolution to Vlissingen for load out. Voe Jarl continues with prelay grapnel run operations in field. Polar Prince continues with cable installation programme</li> </ul>
<ul style="list-style-type: none"> <li>Tugs Stevns Arctic and Bever tow tugs and field support for Sea Jack.</li> </ul>
<ul style="list-style-type: none"> <li>Tug Osprey Fighter towing monopile supply barges to / from Ramsgate &amp; Vlissingen.</li> </ul>
<ul style="list-style-type: none"> <li>Tug Meander assisting Sea Jack and Osprey Fighter as required.</li> </ul>
<ul style="list-style-type: none"> <li>Multicat Voe Jarl performing Prelay grapnel run operations in field.</li> </ul>
<ul style="list-style-type: none"> <li>DP Ship Polar Prince cable laying – Inter array cables between turbine foundations.</li> </ul>
<ul style="list-style-type: none"> <li>Crew boat Waterfall performing Marine Mammal Observations and various crew changes and transfers.</li> </ul>
<ul style="list-style-type: none"> <li>Crew boat Offshore Performer (OP3) assisting with crew changes / transfers &amp; TP maintenance.</li> </ul>
<ul style="list-style-type: none"> <li>Crew boat Sea Weasel for crew changes to Polar Princes &amp; barges (Subocean).</li> </ul>
<ul style="list-style-type: none"> <li>Guard boat Brocklesby in field for monitoring vessel movements and collision avoidance.</li> </ul>

## WORK COMPLETED FROM: 21/09/09 TO 27/09/09

Date	Description
21/09/09	<ul style="list-style-type: none"> <li>Resolution installed TP A01</li> </ul>

22/09/09	<ul style="list-style-type: none"> <li>• Sea Jack installed MP F06. Resolution installed TP B05</li> </ul>
23/09/09	<ul style="list-style-type: none"> <li>• Sea Jack installed MP F13. Resolution installed TP C02</li> </ul>
24/09/09	<ul style="list-style-type: none"> <li>• Sea Jack installed MP G09. Resolution installed TP C03</li> <li>• Voe Jarl completes String 3 grapnel run</li> </ul>
25/09/09	<ul style="list-style-type: none"> <li>• Sea Jack installed MP G10. Resolution installed TP C04</li> <li>• Voe Jarl completes String 4 grapnel run</li> </ul>
26/09/09	<ul style="list-style-type: none"> <li>• Sea Jack installed MP G05. Resolution installed TP D03</li> <li>• Voe Jarl starts String 5 grapnel run. Not complete</li> </ul>
27/09/09	<ul style="list-style-type: none"> <li>• Sea Jack installed MP A03. Resolution in Vlissingen</li> </ul>

Field Status Report 28th September 2009

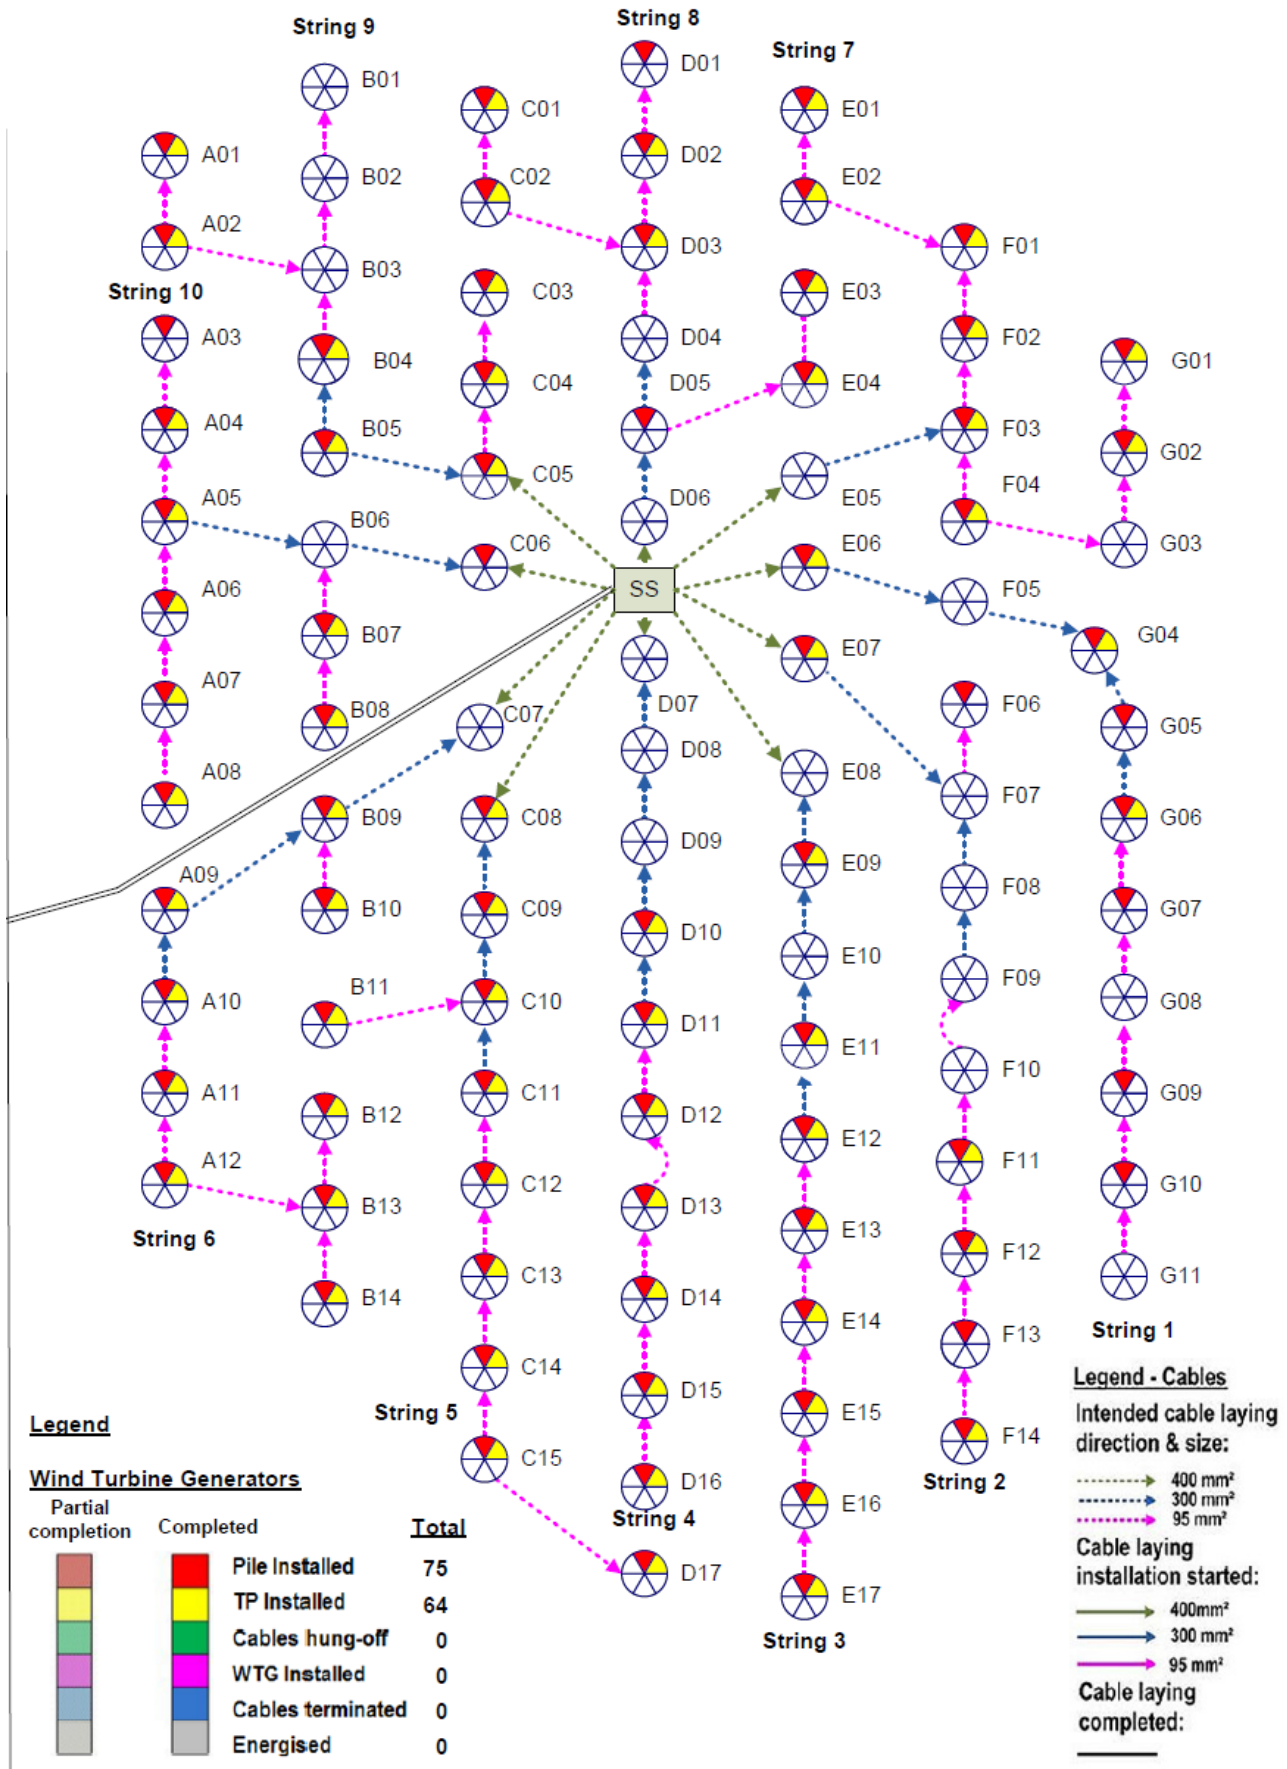

**ON PROJECT VESSEL LIST :**

Name	Type
Offshore Performer(OP3)	Crew vessel
Waterfall	Crew vessel
Sea Weasel	Crew vessel
Bever	Tug
Sea Jack	Jack Up
Stevns Arctic	Tug
MPI Resolution	Jack Up (DP)
Brocklesby	Guard vessel
Meander	Tug
Osprey Fighter	Tug
Polar Prince	Survey (DP)
Voel Jarl	Multicat

**NOTES**

This document will be issued every Monday and will describe the planned activities for the next 7 days. Normal liaison for offshore operations is between the TOW Marine Coordinator and:

- Captain Rob Brown – Interim Harbour Master Port of Ramsgate; and
- Kaimes Beasley – CNIS Manager Dover MCA

This weekly report will be distributed to those recipients listed on the email address header on a weekly basis and is intended to inform those recipients of TOW's planned activities over the forthcoming week.

For further information or comments please contact:

**The Duty Marine Coordinator:**

**Office:** +44 (0) 1843 572130

**Mobile:** +44 (0) 7825880528

**Fax:** +44 (0) 1843 572131

**Email:** [marinecoordinator@thanetoffshorewind.com](mailto:marinecoordinator@thanetoffshorewind.com)
