


Thanet Offshore Wind Limited

Weekly Notice of Operations to Stakeholders

Date of Notice 21/12/09

Notice No.40

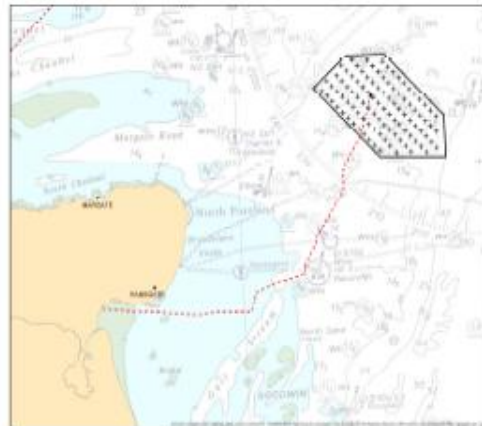

Distribution

See e-mail address header


WORK PLANNED FOR PERIOD: FROM 20/12/09 TO 27/12/09

Description: (subject to weather conditions)
21/12/09 – Sea Jack on location E08 to install MP. Resolution completes installation of WTG D15. Polar Prince working on cable installation guides at A05, A04 & A03. UR101 installs cable between A06 & A05
22/12/09 - Sea Jack on location E08 to install MP. Polar Prince - magnetometer survey and installing cable A11 to A10. UR101 complete cable A06 to A05. Resolution commences installation of WTG D16
23/12/09 - Sea Jack in Ramsgate. Polar Prince - magnetometer survey and installing cable B10 to B09. UR101 installing cable A05 to A04. Resolution installs WTG on D16 & moves to C11
24/12/09 - Sea Jack in Ramsgate WOW. Polar Prince - magnetometer survey and installing cable B13 to B12. UR101 May seek shelter due to weather. Resolution installs WTG at C11. Weather delays expected.
25/12/09 - Sea Jack leaves Ramsgate for F05. Polar Prince - installing cable B13 to B12. UR101 resumes installing cable A05 to A04. Resolution installs WTG on B11
26/12/09 - Sea Jack at G03 to install MP. Polar Prince - installing cable C14 to C13. UR101 installing cable A04 to A03. Resolution to install WTG at A12.
27/12/09 - Sea Jack in Ramsgate for loadout. Polar Prince - installing cable C15 to C14. UR101 completes installing cable A04 to A03. Resolution to install WTG at A11.
<ul style="list-style-type: none"> • Tugs Stevns Arctic and Bever tow tugs and field support for Sea Jack. • Tug Osprey Fighter towing monopile supply barges to / from Ramsgate & Vlissingen. • Tug Meander assisting Sea Jack and Osprey Fighter as required. • Tug Multratug 18 & Maggie M to assist the non-propelled barge UR101 as required. • Multicat Voe Viking performing Prelay grapnel run operations in field. • DP Ship Polar Prince cable laying – Inter array cables between turbine foundations. • Barge UR101 cable laying - Inter array cables between turbine foundations. • Crew boat Waterfall performing Marine Mammal Observations and various crew changes, transfers & TP maintenance. • Crew boat Offshore Performer (OP3) assisting with crew changes, transfers & TP maintenance. • Crew boat Sea Weasel & Ocean Cat for crew changes to Polar Princes & barges (Subocean). • Crew boats Endeavour & Ocean Wind 3 for WTG access (Vestas) • Sander performing post laid cable surveys. Replaced by MS Line • Guard boat Brockelsby in field for monitoring vessel movements and collision avoidance.

WORK COMPLETED FROM: 14/11/09 TO 20/12/09

Date	Description
14/12/09	<ul style="list-style-type: none">• Polar Prince installed cable B14 to B13. UR101 installed cable E17 to E16. Resolution installed WTG A09.
15/12/09	<ul style="list-style-type: none">• Sea jack installed MP E05
16/12/09	<ul style="list-style-type: none">• Sea Jack attempting to install MP D08.
17/12/09	<ul style="list-style-type: none">• Sea Jack in Ramsgate. Waiting on Weather
18/12/09	<ul style="list-style-type: none">• Waiting on weather
19/12/09	<ul style="list-style-type: none">• Resolution installed nacelle on D15
20/12/09	<ul style="list-style-type: none">• Sea Jack left Ramsgate for E08

Field Status Report 20th December 2009

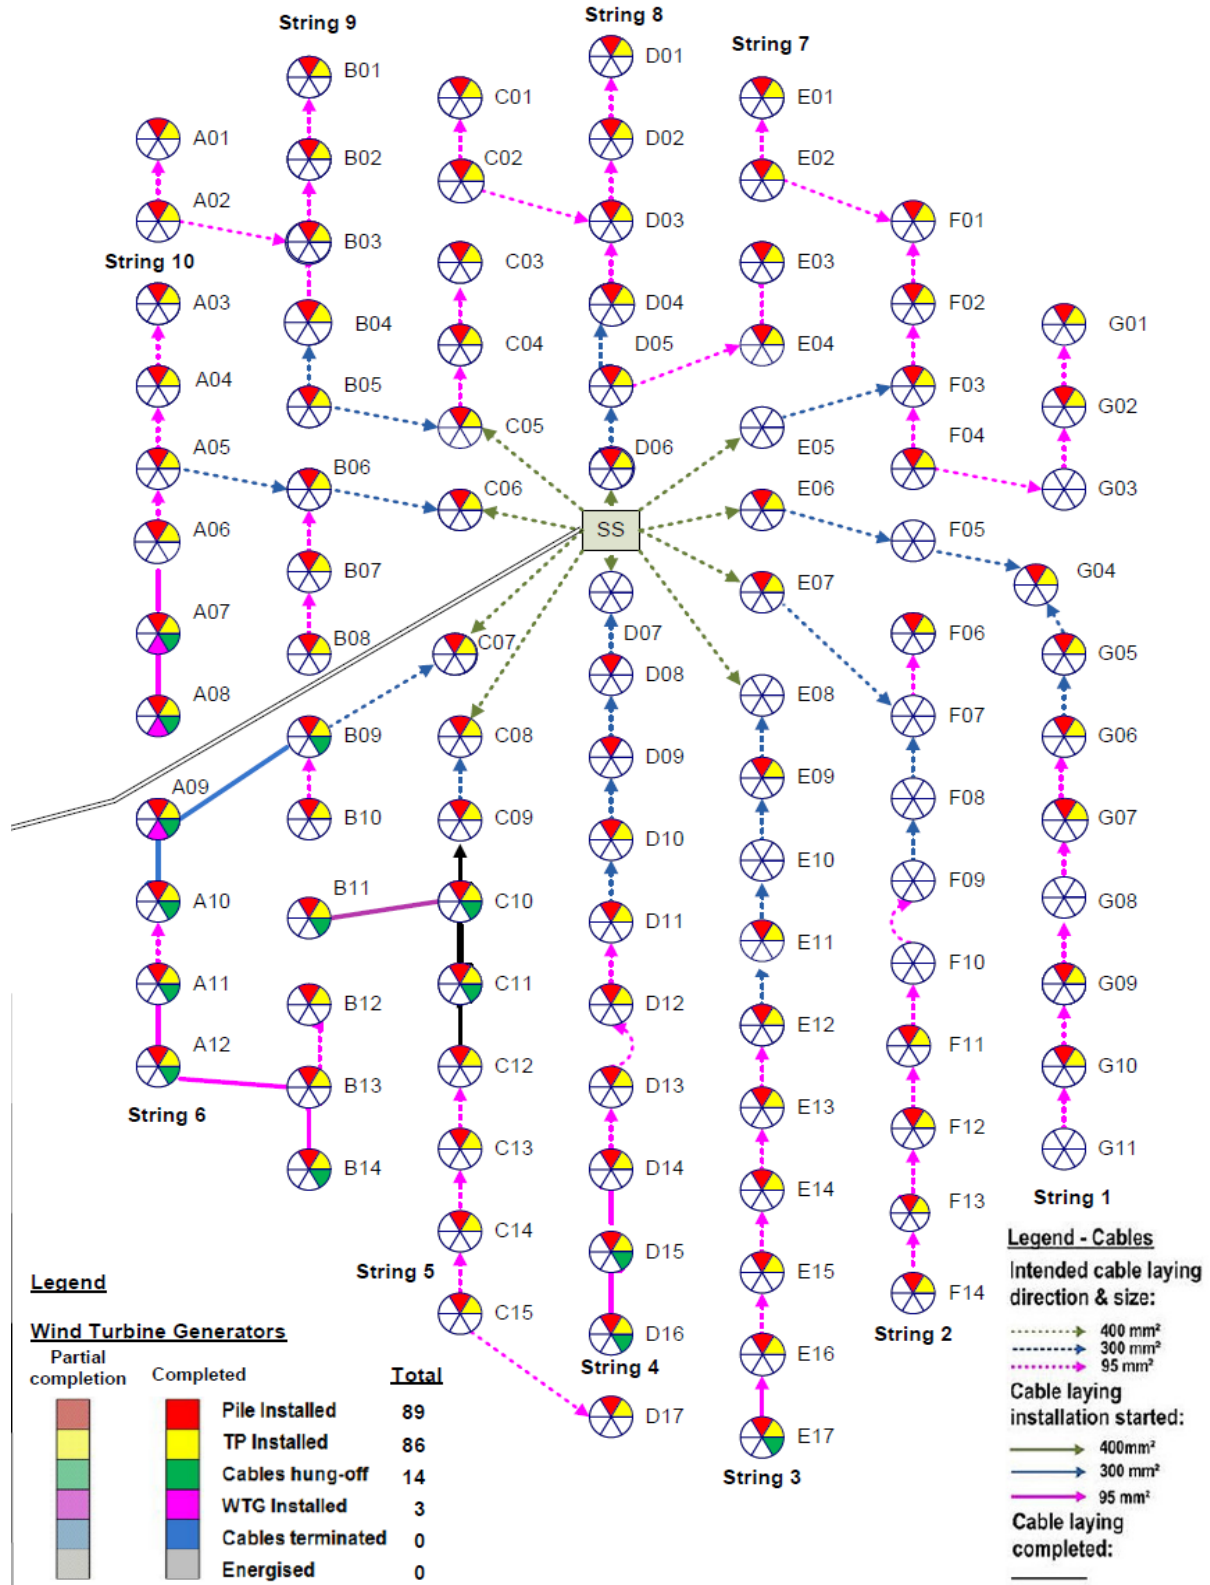

ON PROJECT VESSEL LIST :

Name	Type
Offshore Performer(OP3)	Crew vessel
Waterfall	Crew vessel
Sea Weasel	Crew vessel
Endeavour	Crew vessel
Ocean Wind 3	Crew vessel
Ocean Cat	Crew vessel
Brockelsby	Guard vessel
Bever	Tug
Stevns Arctic	Tug
Meander	Tug
Osprey Fighter	Tug
Multratug 18	Tug
Sea Jack	Jack Up
MPI Resolution	Jack Up (DP)
Polar Prince	Cable lay (DP)
UR101	Cable lay barge
Voe Viking	Multicat
Voe Jarl	Multicat
Maggie M	Multicat
Sander / M/S Line	Survey
Arie Dirk	Environmental (Birds)

NOTES

This document will be issued every Monday and will describe the planned activities for the next 7 days. Normal liaison for offshore operations is between the TOW Marine Coordinator and:

- Captain Rob Brown – Interim Harbour Master Port of Ramsgate; and
- Kaimes Beasley – CNIS Manager Dover MCA

This weekly report will be distributed to those recipients listed on the email address header on a weekly basis and is intended to inform those recipients of TOW's planned activities over the forthcoming week.

For further information or comments please contact:

The Duty Marine Coordinator:

Office: +44 (0) 1843 572130

Mobile: +44 (0) 7825880528

Fax: +44 (0) 1843 572131

Email: marinecoordinator@thanetoffshorewind.com
