


Thanet Offshore Wind Limited

Weekly Notice of Operations to Stakeholders

Date of Notice 11/01/2010

Notice No.43

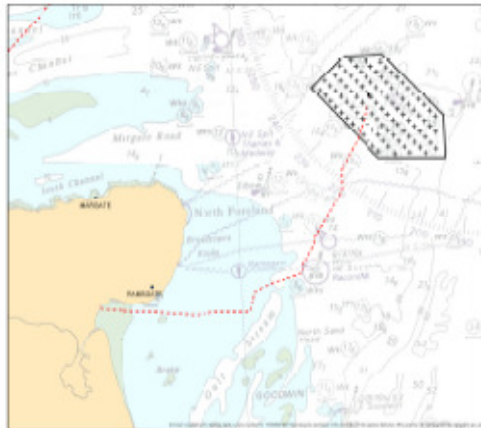

Distribution

See e-mail address header


WORK PLANNED FOR PERIOD: FROM 11/01/10 TO 17/01/10

Description: (subject to weather conditions)
11/01/10 – Waiting on weather
12/01/10 – Sea Jack to location F10, Polar Prince installing cable C13 to C12. Resolution on site at B14 to install WTG.
13/01/10 – Sea Jack at F10, Polar Prince installing cable C13 to C12, Resolution at B14 to install WTG. Expect delays due to weather.
14/01/10 - Sea Jack install MP at F10, Polar Prince installing cable C13 to C12, Resolution at B14 to install WTG.
15/01/10 – Sea Jack in Ramsgate, Polar Prince install cable B13 to B12. Resolution install WTG on C10.
16/01/10 – Sea Jack to D07, Polar Prince install cable B13 to B12. Resolution install WTG at C10.
17/01/10 – Sea Jack install MP at D07. Polar Prince install cable at B10 to B09. Resolution install WTG at E17.
<ul style="list-style-type: none"> • Tugs Stevns Arctic and Bever tow tugs and field support for Sea Jack. • Tug Osprey Fighter towing monopile supply barges to / from Ramsgate & Vlissingen. • Tug Meander assisting Sea Jack and Osprey Fighter as required. • Tug Multratug 18 & Maggie M to assist the non-propelled barge UR101 as required. • DP Ship Polar Prince cable laying – Inter array cables between turbine foundations. • Barge UR101 cable laying - export cables from Pegwell Bay. • Crew boat Waterfall performing Marine Mammal Observations and various crew changes, transfers & TP maintenance. • Crew boat Offshore Performer (OP3) assisting with crew changes, transfers & TP maintenance. • Crew boat Sea Weasel for crew changes to Polar Princes & barges (Subocean). • Crew boats Endeavour & Enterprise for WTG access (Vestas) • M/S Line performing post laid cable surveys. • Guard boat Brockelsby in field for monitoring vessel movements and collision avoidance.

WORK COMPLETED FROM: 04/01/10 TO 10/01/10

Date	Description
04/01/10	<ul style="list-style-type: none">• Resolution install WTG at A10
05/01/10	<ul style="list-style-type: none">• Resolution install WTG at B11. Sea Jack installs MP G11.
06/01/10	<ul style="list-style-type: none">• Polar Prince installed array cable from C14 to C13.
07/01/10	<ul style="list-style-type: none">• Waiting on weather
08/01/10	<ul style="list-style-type: none">• Waiting on weather
09/01/10	<ul style="list-style-type: none">• Waiting on weather
10/01/10	<ul style="list-style-type: none">• Waiting on weather

Field Status Report 10th January 2010

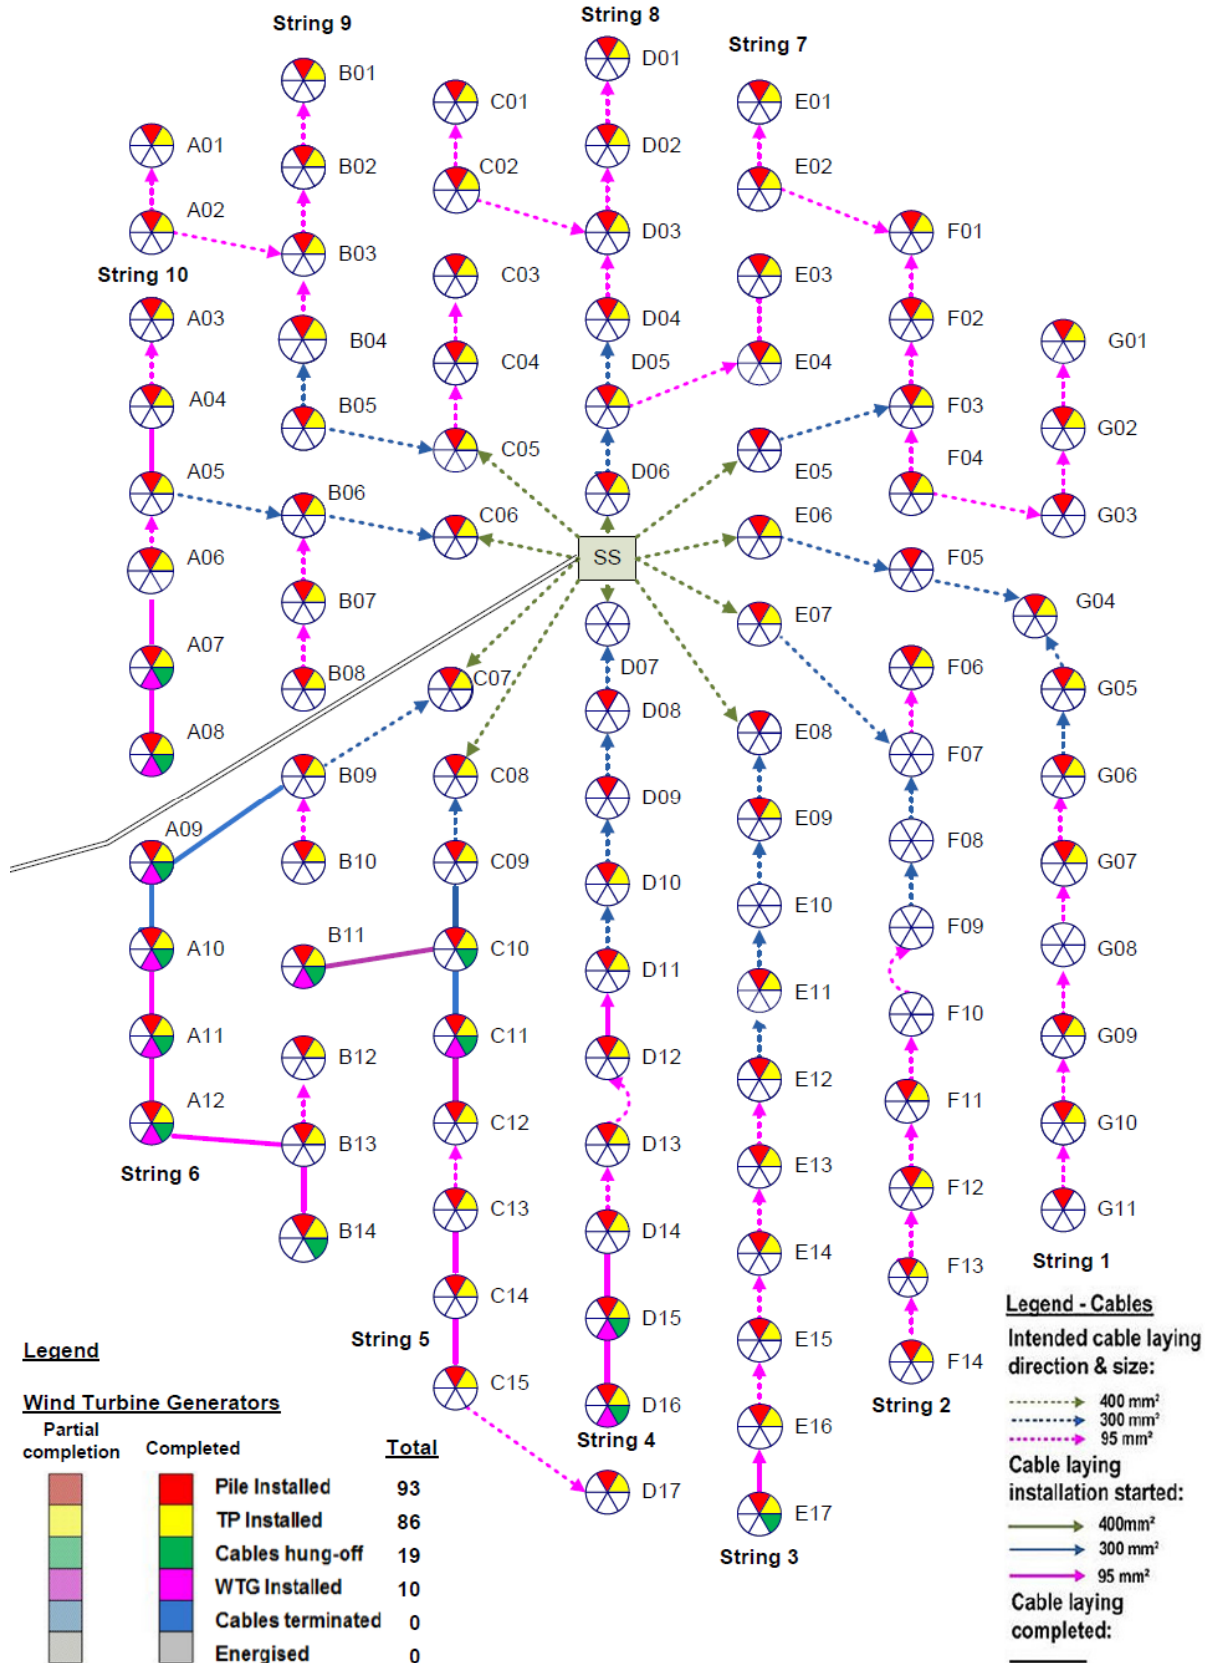

ON PROJECT VESSEL LIST :

Name	Type
Offshore Performer(OP3)	Crew vessel
Waterfall	Crew vessel
Sea Weasel	Crew vessel
Endeavour	Crew vessel
Enterprise	Crew vessel
Brockelsby	Guard vessel
Bever	Tug
Stevns Arctic	Tug
Meander	Tug
Osprey Fighter	Tug
Multratug 18	Tug
Sea Jack	Jack Up
MPI Resolution	Jack Up (DP)
Polar Prince	Cable lay (DP)
UR101	Cable lay barge
Maggie M	Multicat
M/S Line	Survey
Arie Dirk	Environmental (Birds)

NOTES

This document will be issued every Monday and will describe the planned activities for the next 7 days. Normal liaison for offshore operations is between the TOW Marine Coordinator and:

- Captain Rob Brown – Interim Harbour Master Port of Ramsgate; and
- Kaimes Beasley – CNIS Manager Dover MCA

This weekly report will be distributed to those recipients listed on the email address header on a weekly basis and is intended to inform those recipients of TOW's planned activities over the forthcoming week.

For further information or comments please contact:

The Duty Marine Coordinator:

Office: +44 (0) 1843 572130

Mobile: +44 (0) 7825880528

Fax: +44 (0) 1843 572131

Email: marinecoordinator@thanetoffshorewind.com
