


Thanet Offshore Wind Limited

Weekly Notice of Operations to Stakeholders

Date of Notice 01/02/2010

Notice No.46

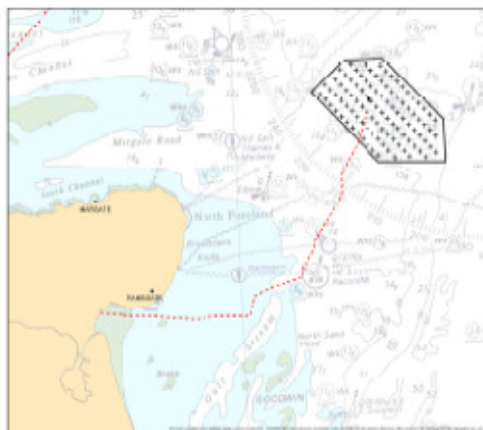

Distribution

See e-mail address header

WORK PLANNED FOR PERIOD: FROM 01/02/10 TO 07/02/10


Description: (subject to weather conditions)
01/02/10 – Resolution at D14 installing WTG. Polar Prince install cable D11-D10. Normand Mermaid install cable E13-E12.
02/02/10 – Resolution at D13 installing WTG. Polar Prince install cable D11-D10. Normand Mermaid install cable E13-E12.
03/02/10 – Resolution at D13 installing WTG. Polar Prince install cable E16-E15. Normand Mermaid install cable E14-E13.
04/02/10 – Resolution at D12 installing WTG. Stanislav Yudin on site and setting up at Sub-station location. Polar Prince install cable E16-E15. Normand Mermaid install cable E14-E13.
05/02/10 – Resolution at D11 installing WTG. Stanislav Yudin preparing to install Sub-station jacket. Polar Prince install cable E16-E15. Normand Mermaid install cable E15-E14. Sea Jack in Ramsgate to load TPs.
06/02/10 – Resolution at D15 installing WTG. Stanislav Yudin preparing to install Sub-station jacket. Polar Prince install cable F13-F12. Normand Mermaid install cable A04-A03. Sea Jack out to site to install TP on D07.
07/02/10 - Resolution at D17 installing WTG. Stanislav Yudin preparing to install sub-station topsides module. Polar Prince install cable F13-F12. Normand Mermaid install cable A04-A03. Sea Jack on site to install TP on D07.
<ul style="list-style-type: none"> • Tugs Stevns Arctic and Bever tow tugs and field support for Sea Jack. • Tug Osprey Fighter towing monopile supply barges to / from Ramsgate & Vlissingen. • Tug Meander assisting Sea Jack and Osprey Fighter as required. • Tug Multratug 18 & Maggie M to assist the non-propelled barge UR101 as required. • DP Ship Polar Prince cable laying – Inter array cables between turbine foundations. • DP Ship Normand Mermaid cable laying – Inter array cables between turbine foundations • Barge UR101 cable laying - export cables from Pegwell Bay. • Crew boat Waterfall performing Marine Mammal Observations and various crew changes, transfers & TP maintenance. • Crew boat Offshore Performer (OP3) assisting with crew changes, transfers & TP maintenance. • Crew boat Sea Weasel for crew changes to Polar Princes & barges (Subocean). • Crew boat Strider servicing Multicats Joustler and Fighter. • Crew boats Endeavour & Enterprise for WTG access (Vestas) • Survey boat Channel Chieftain and Sir Claude Inglis for UXO survey work. • M/S Line performing post laid cable surveys. • Diving boat Xplorer surveying seabed anomalies near sub-station location • Multicat Forth Joustler & Forth Fighter assisting with TP maintenance and diving operations

- Guard boat Brockelsby in field for monitoring vessel movements and collision avoidance.

WORK COMPLETED FROM: 25/01/10 TO 31/01/10

Date	Description
25/01/10	<ul style="list-style-type: none"> • Resolution installed WTG at C14
26/01/10	<ul style="list-style-type: none"> • Waiting on weather.
27/01/10	<ul style="list-style-type: none"> • Polar Prince installed cable D12 to D13.
28/01/10	<ul style="list-style-type: none"> • UR101 pulling cable to beach landing
29/01/10	<ul style="list-style-type: none"> • UR101 pulling cable to beach landing
30/01/10	<ul style="list-style-type: none"> • UR101 pulling cable to beach landing
31/01/10	<ul style="list-style-type: none"> • UR101 pulling cable to beach landing

Field Status Report 31st January 2010

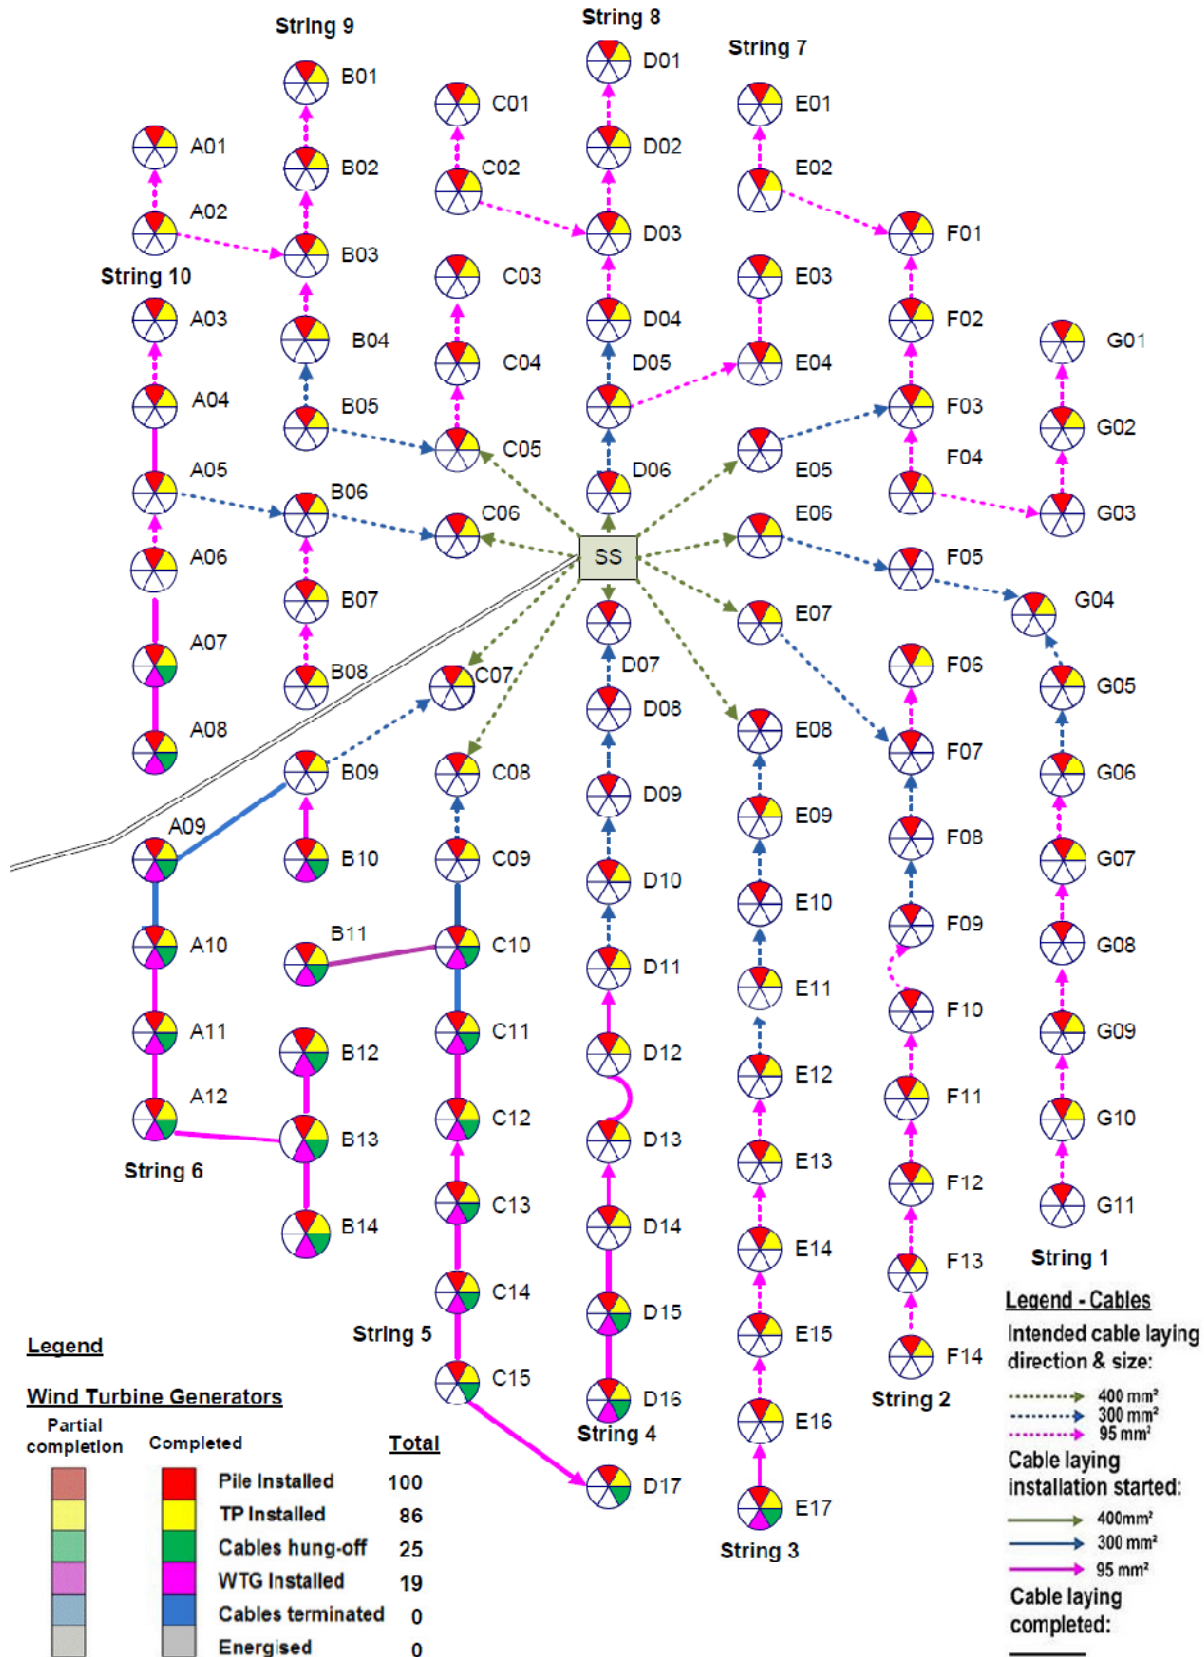

ON PROJECT VESSEL LIST :

Name	Type
Offshore Performer(OP3)	Crew vessel
Waterfall	Crew vessel
Sea Weasel	Crew vessel
Endeavour	Crew vessel
Enterprise	Crew vessel
Channel Chieftain	Survey vessel
Brockelsby	Guard vessel
Bever	Tug
Stevns Arctic	Tug
Meander	Tug
Osprey Fighter	Tug
Multratug 18	Tug
Sea Jack	Jack Up
MPI Resolution	Jack Up (DP)
Polar Prince	Cable lay (DP)
Normand Mermaid	Cable lay (DP)
UR101	Cable lay barge
Maggie M	Multicat
M/S Line	Survey
Arie Dirk	Environmental (Birds)
Forth Jouser	Multicat
Voe Viking	Multicat
Xplorer	Diving Vessel

NOTES

This document will be issued every Monday and will describe the planned activities for the next 7 days. Normal liaison for offshore operations is between the TOW Marine Coordinator and:

- Captain Rob Brown – Interim Harbour Master Port of Ramsgate; and
- Kaimes Beasley – CNIS Manager Dover MCA

This weekly report will be distributed to those recipients listed on the email address header on a weekly basis and is intended to inform those recipients of TOW's planned activities over the forthcoming week.

For further information or comments please contact:

The Duty Marine Coordinator:

Office: +44 (0) 1843 572130

Mobile: +44 (0) 7825880528

Fax: +44 (0) 1843 572131

Email: marinecoordinator@thanetoffshorewind.com
