


Thanet Offshore Wind Limited

Weekly Notice of Operations to Stakeholders

Date of Notice 30/11/09

Notice No.37

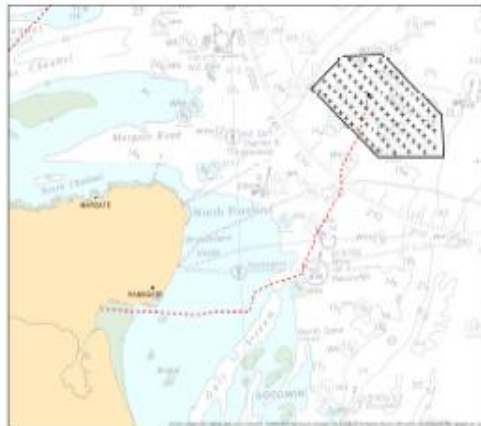

Distribution

See e-mail address header


WORK PLANNED FOR PERIOD: FROM 30/11/09 TO 06/12/09

Description: (subject to weather conditions)
30/11/09 – Polar Prince installing cable from A12 to B13. Voe Viking to continue with grapnel run sequence if weather permits. Sea Jack transits from Rotterdam to Ramsgate
01/12/09 – Polar Prince installing cable from A11 to A10. Voe Viking to continue with grapnel run sequence if weather permits. Sea Jack arrives in Ramsgate
02/12/09 – Polar Prince installing cable from B10 to B09. UR101 installing cable from A06 to A05. Voe Viking to continue with grapnel run sequence if weather permits. Sea Jack Installs MP D08
03/12/09 – Polar Prince installing cable from B09 to C07. UR101 installing cable from A06 to A05. Voe Viking to continue with grapnel run sequence if weather permits. Sea Jack Installs MP D09.
04/12/09 – Polar Prince installing cable from C09 to C08. UR101 installing cable from A05 to A04. Voe Viking to continue with grapnel run sequence if weather permits. Sea Jack in Ramsgate for MP loadout.
05/12/09 – Polar Prince installing cable from B14 to B13. UR101 installing cable from A05 to A05. Voe Viking to continue with grapnel run sequence if weather permits. Sea Jack Installs MP D07
06/12/09 – Polar Prince installing cable from B13 to B12. UR101 installing cable from A04 to A03. Voe Viking to continue with grapnel run sequence if weather permits. Sea Jack Installs MP E05
<ul style="list-style-type: none"> • Tugs Stevns Arctic and Bever tow tugs and field support for Sea Jack. • Tug Osprey Fighter towing monopile supply barges to / from Ramsgate & Vlissingen. • Tug Meander assisting Sea Jack and Osprey Fighter as required. • Tug Multratug 18 to assist the non-propelled barge UR101 as required. • Multicat Voe Viking performing Prelay grapnel run operations in field. • DP Ship Polar Prince cable laying – Inter array cables between turbine foundations. • Barge UR101 cable laying - Inter array cables between turbine foundations. • Crew boat Waterfall performing Marine Mammal Observations and various crew changes, transfers & TP maintenance. • Crew boat Offshore Performer (OP3) assisting with crew changes, transfers & TP maintenance. • Crew boat Sea Weasel & Sea Beaver for crew changes to Polar Princes & barges (Subocean). • Crew boat Endeavour for WTG access (Vestas) • Sander performing post laid cable surveys. • Guard boat Brockelsby in field for monitoring vessel movements and collision avoidance.

WORK COMPLETED FROM: 23/11/09 TO 29/11/09

Date	Description
23/11/09	<ul style="list-style-type: none"> • Polar Prince conducts ROV free-span survey of A08
24/11/09	<ul style="list-style-type: none"> • Polar Prince conducts ROV free-span survey of A10, C10 & C09. Voe Viking conducted grapnel runs between B9-C7, C07-SS & A04-A03
25/11/09	<ul style="list-style-type: none"> • Polar Prince conducts ROV survey of D16 & D16
26/11/09	<ul style="list-style-type: none"> • Polar Prince conducts ROV survey of D14 & A05
27/11/09	<ul style="list-style-type: none"> • Polar Prince deploys alignment frames at A05
28/11/09	<ul style="list-style-type: none"> • Polar Prince conducts ROV survey at A07
29/11/09	<ul style="list-style-type: none"> • Polar Prince conducts ROV survey of A03, A04 & A06

Field Status Report 30th. November 2009

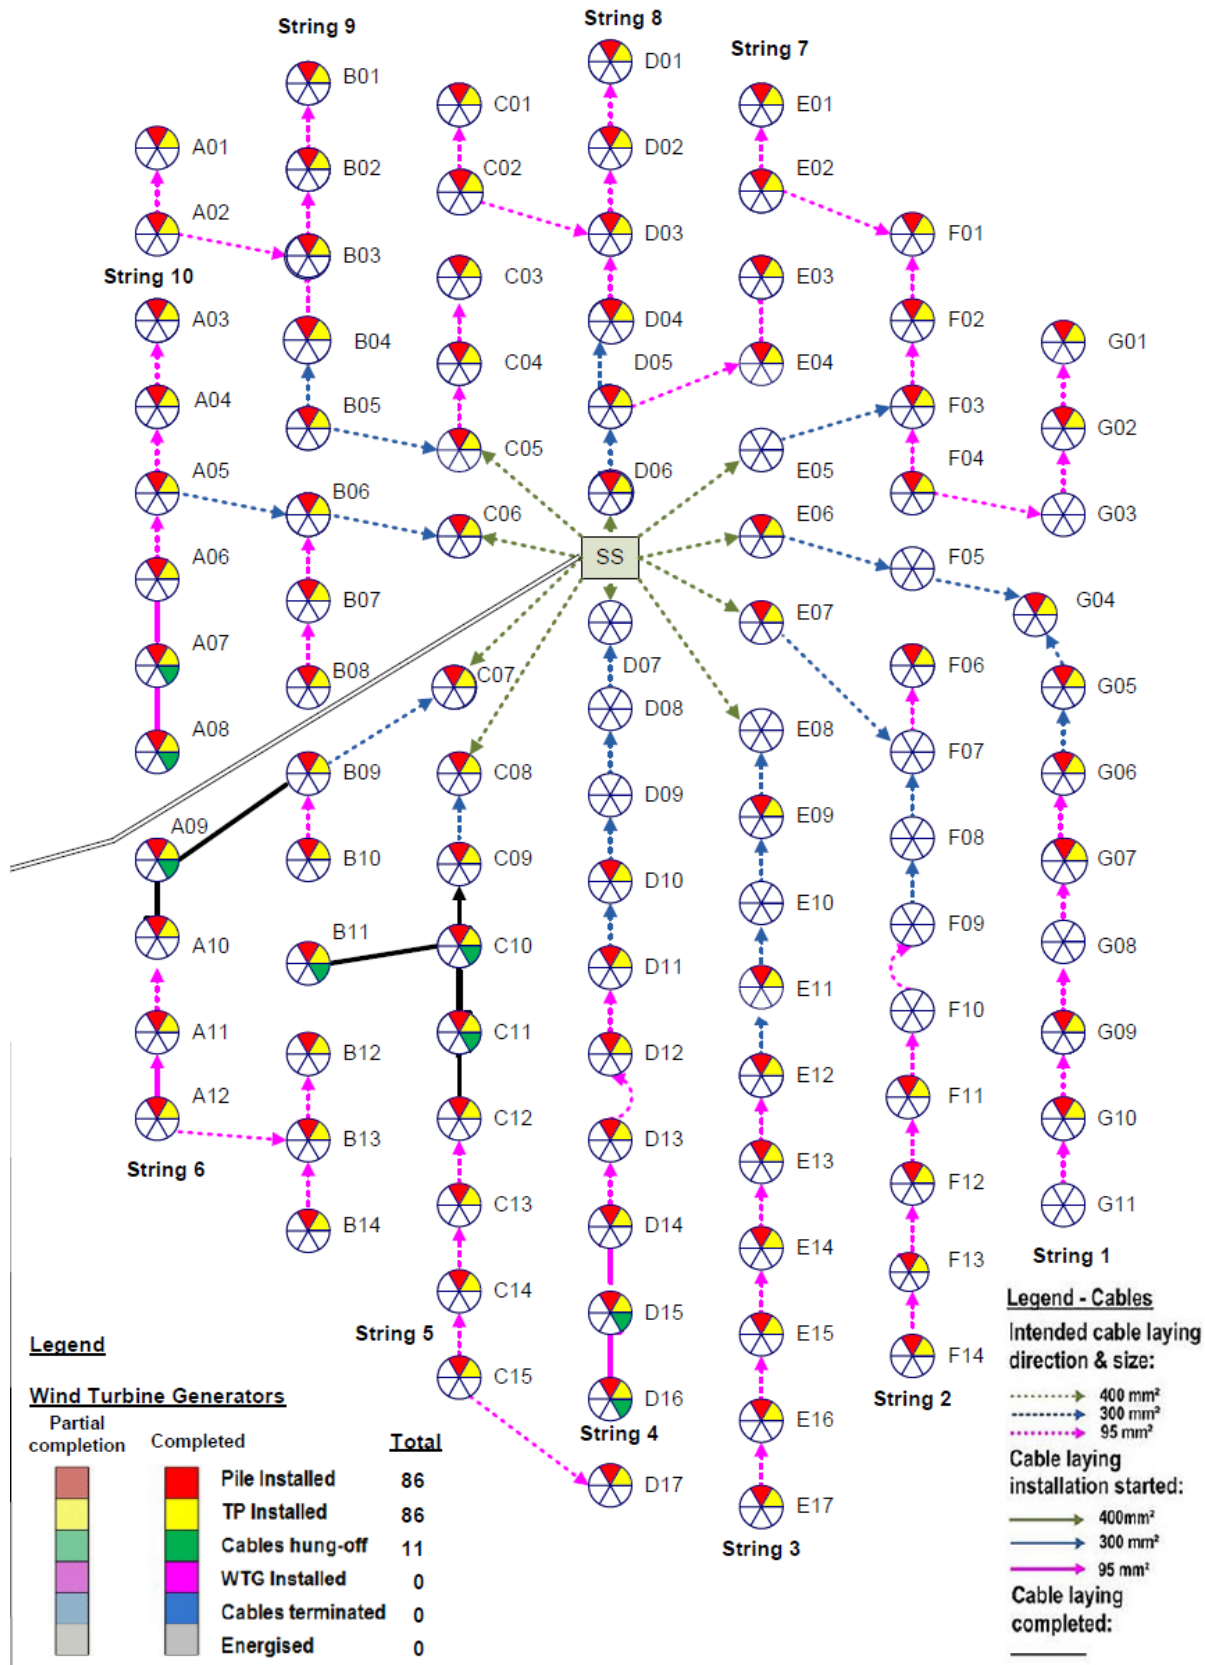

ON PROJECT VESSEL LIST :

Name	Type
Offshore Performer(OP3)	Crew vessel
Waterfall	Crew vessel
Sea Weasel	Crew vessel
Sea Beaver	Crew vessel
Endeavour	Crew vessel
Brockelsby	Guard vessel
Bever	Tug
Stevns Arctic	Tug
Meander	Tug
Osprey Fighter	Tug
Multratug 18	Tug
Sea Jack	Jack Up
MPI Resolution	Jack Up (DP)
Polar Prince	Cable lay (DP)
UR101	Cable lay barge
Voe Jarl	Multicat
Voe Viking	Multicat
Maggie M	Multicat
Sander	Survey
Arie Dirk	Environmental (Birds)

NOTES

This document will be issued every Monday and will describe the planned activities for the next 7 days. Normal liaison for offshore operations is between the TOW Marine Coordinator and:

- Captain Rob Brown – Interim Harbour Master Port of Ramsgate; and
- Kaimes Beasley – CNIS Manager Dover MCA

This weekly report will be distributed to those recipients listed on the email address header on a weekly basis and is intended to inform those recipients of TOW's planned activities over the forthcoming week.

For further information or comments please contact:

The Duty Marine Coordinator:

Office: +44 (0) 1843 572130

Mobile: +44 (0) 7825880528

Fax: +44 (0) 1843 572131

Email: marinecoordinator@thanetoffshorewind.com
