


Thanet Offshore Wind Limited  
**Weekly Notice of Operations to Stakeholders**

---

Date of Notice 12/07/2010

Notice No.69

---

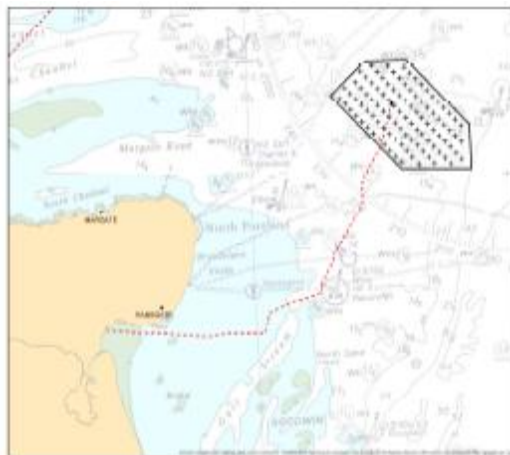

**Distribution**

See e-mail address header

**WORK PLANNED FOR PERIOD: FROM 12/07/10 TO 18/07/10**

Description: (subject to weather conditions)
12/07/10 - Forth Joustier engaged in diving operations, Normand Mermaid jointing the export cable & MS Nico Cable trenching within boundaries of the windfarm.
13/07/10 - Forth Joustier engaged in diving operations, Normand Mermaid jointing the export cable & MS Nico Cable trenching within boundaries of the windfarm.
14/07/10 - Forth Joustier engaged in diving operations, Normand Mermaid jointing the export cable & MS Nico Cable trenching within boundaries of the windfarm.
15/07/10 - Forth Joustier engaged in diving operations, Normand Mermaid jointing the export cable & MS Nico Cable trenching within boundaries of the windfarm.
16/07/10 - Forth Joustier engaged in diving operations, Normand Mermaid jointing the export cable & MS Nico Cable trenching within boundaries of the windfarm.
17/07/10 - Forth Joustier engaged in diving operations, Normand Mermaid jointing the export cable & MS Nico Cable trenching within boundaries of the windfarm.
18/07/10 - Forth Joustier engaged in diving operations, Normand Mermaid jointing the export cable & MS Nico Cable trenching within boundaries of the windfarm.
<ul style="list-style-type: none"> <li>• DP ship Normand Mermaid – export cable jointing.</li> </ul>
<ul style="list-style-type: none"> <li>• Crew boat OP3 for TOW cable terminators.</li> </ul>
<ul style="list-style-type: none"> <li>• Crew boat Wildcat1 conducting crew changes for Forth Joustier.</li> </ul>
<ul style="list-style-type: none"> <li>• Crew boat Waterfall out for TOWSAPS and TOW Port Technicians.</li> </ul>
<ul style="list-style-type: none"> <li>• Crew boats Lesley Jay, Wildcat 1, MPI Rucio servicing Forth Joustier</li> </ul>
<ul style="list-style-type: none"> <li>• Crew boats Endeavour, Enterprise, Windcat 12, Moidart and Wind Crew 1 for WTG access (Vestas)</li> </ul>
<ul style="list-style-type: none"> <li>• M/S Line performing post laid cable surveys.</li> </ul>
<ul style="list-style-type: none"> <li>• Multicat Forth Joustier engaged in diving operations, diving surveys, messenger wire installations &amp; cable remedial works.</li> </ul>
<ul style="list-style-type: none"> <li>• Guard boats Ann Scott and Reliance in field for monitoring vessel movements and collision avoidance.</li> </ul>
<ul style="list-style-type: none"> <li>• Strider, Sea Badger &amp; Norfolk Swift assisting with Subocean cable termination works.</li> </ul>
<ul style="list-style-type: none"> <li>• MS Nico Carrying out cable trenching operations</li> </ul>


**WORK COMPLETED FROM 05/07/10 TO 11/07/10**

Date	Description
05/07/10	<ul style="list-style-type: none"> <li>• Forth Jouster undertakes various diving operations within the windfarm. Various cable terminations have been completed and contractors continue to Terminate and test and energise turbines</li> </ul>
06/07/10	<ul style="list-style-type: none"> <li>• Forth Jouster undertakes various diving operations within the windfarm. Various cable terminations have been completed and contractors continue to Terminate and test and energise turbines</li> </ul>
07/07/10	<ul style="list-style-type: none"> <li>• Forth Jouster undertakes various diving operations within the windfarm. Various cable terminations have been completed and contractors continue to Terminate and test and energise turbines</li> </ul>
08/07/10	<ul style="list-style-type: none"> <li>• Forth Jouster undertakes various diving operations within the windfarm. Various cable terminations have been completed and contractors continue to Terminate and test and energise turbines</li> </ul>
09/07/10	<ul style="list-style-type: none"> <li>• Forth Jouster undertakes various diving operations within the windfarm.</li> <li>• Contractors continue to Terminate, test and energise turbines.</li> <li>• Normand Mermaid at South Export cable preparing for cable jointing</li> </ul>
10/07/10	<ul style="list-style-type: none"> <li>• Forth Jouster undertakes various diving operations within the windfarm.</li> <li>• Contractors continue to Terminate, test and energise turbines.</li> <li>• Normand Mermaid at South Export cable preparing for cable jointing then Great Yarmouth for equipment</li> </ul>
11/07/10	<ul style="list-style-type: none"> <li>• Forth Jouster undertakes various diving operations within the windfarm.</li> <li>• Contractors continue to Terminate, test and energise turbines.</li> <li>• Normand Mermaid at Great Yarmouth for equipment</li> <li>• MS Nico commences</li> </ul>

**ON PROJECT VESSEL LIST:**

Name	Type
Offshore Performer(OP3)	Crew vessel
Waterfall	Crew vessel
Wildcat 1	Crew Vessel
Sea Badger	Crew vessel
Endeavour	Crew vessel
Enterprise	Crew vessel
Lesley Jay	Crew vessel
MPI Rucio	Crew vessel
Windcat 12	Crew vessel
Wind Crew 1	Crew vessel
Strider	Crew Vessel
Moidart	Crew vessel
Norfolk Swift	Crew vessel
Forth Joustier	Multicat Dive vessel
Reliance	Guard Vessel
M/S Line	Survey
Ann Scott	Guard vessel
MS Nico	Trenching vessel
Normand Mermaid	Construction vessel

### Field Status Report 11<sup>th</sup> July 2010

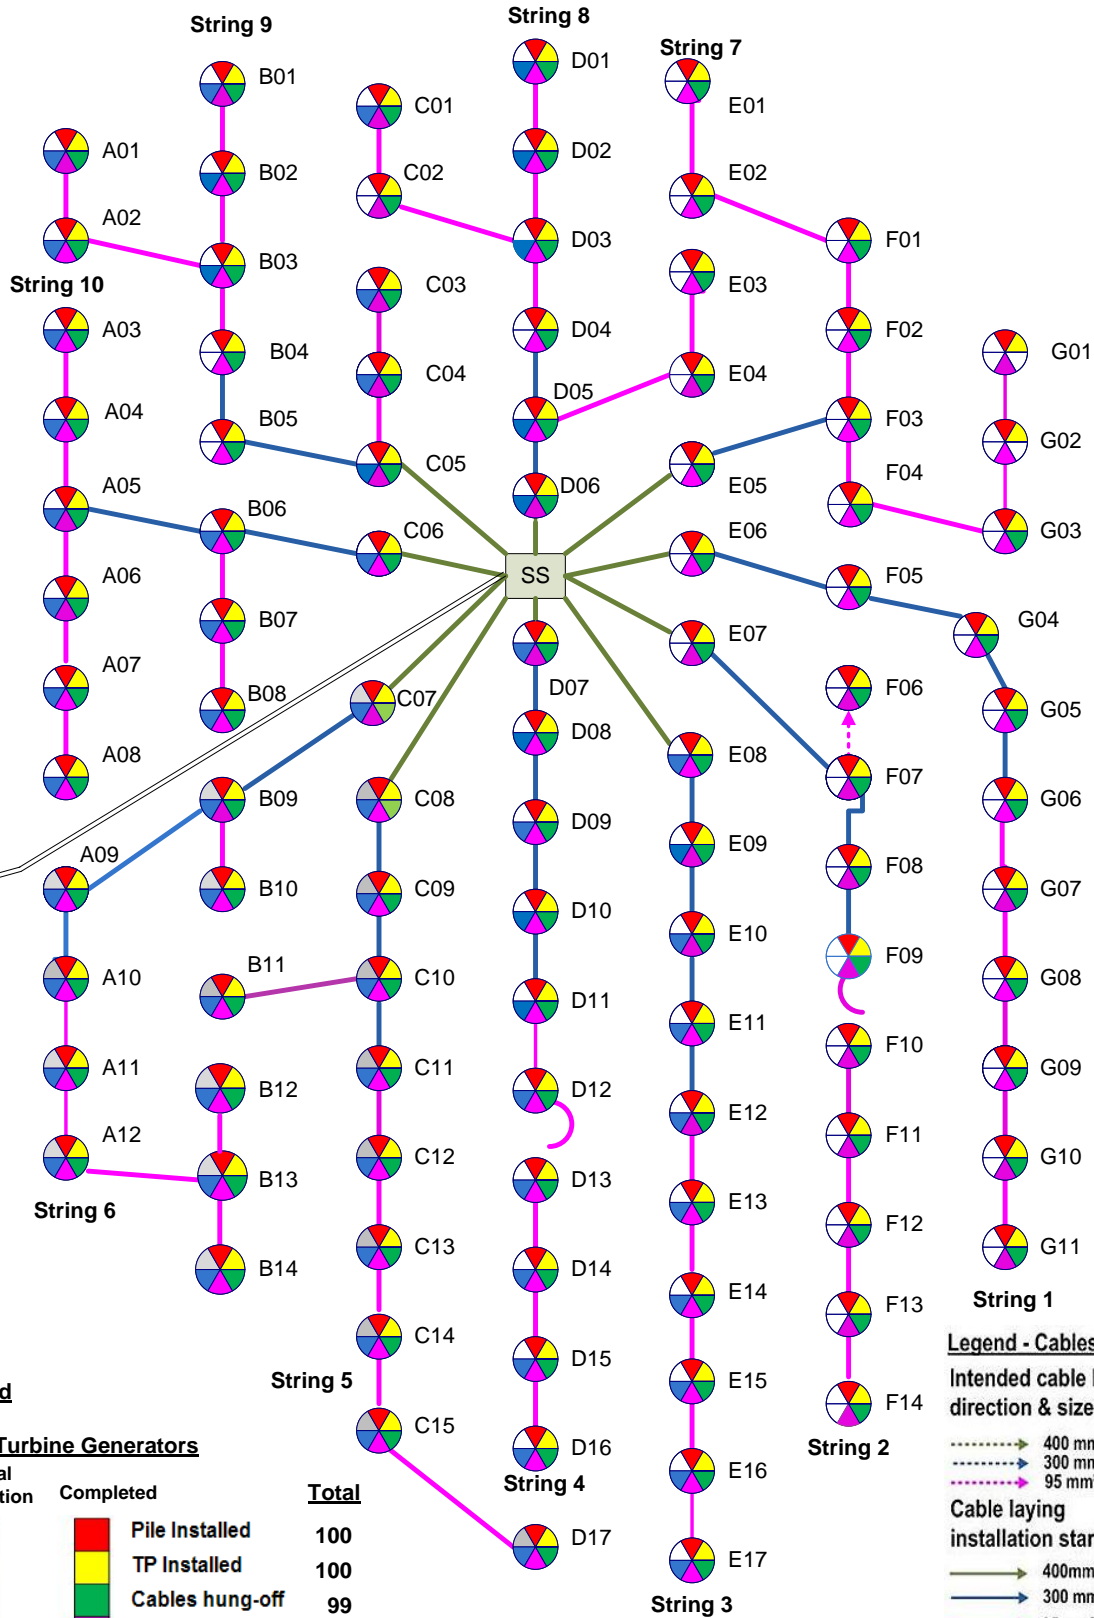

**Legend**

**Wind Turbine Generators**

Partial completion	Completed	Total
		100
		100
		99
		100
		172
		10

**Legend - Cables**

Intended cable laying direction & size:

- 400 mm<sup>2</sup>
- 300 mm<sup>2</sup>
- 95 mm<sup>2</sup>

Cable laying installation started:

- 400mm<sup>2</sup>
- 300 mm<sup>2</sup>
- 95 mm<sup>2</sup>

Cable laying completed:

-

## **NOTES**

This document will be issued every Monday and will describe the planned activities for the next 7 days. Normal liaison for offshore operations is between the TOW Marine Coordinator and:

- Captain Rob Brown – Interim Harbour Master Port of Ramsgate; and
- Kaimes Beasley – CNIS Manager Dover MCA

This weekly report will be distributed to those recipients listed on the email address header on a weekly basis and is intended to inform those recipients of TOW's planned activities over the forthcoming week.

For further information or comments, please contact:

### **The Duty Marine Coordinator:**

**Office:** +44 (0) 1843 572130

**Mobile:** +44 (0) 7825880528

**Fax:** +44 (0) 1843 572131

**Email:** [marinecoordinator@thanetoffshorewind.com](mailto:marinecoordinator@thanetoffshorewind.com)
