


Thanet Offshore Wind Limited

Weekly Notice of Operations to Stakeholders

Date of Notice 18/01/2010

Notice No.44

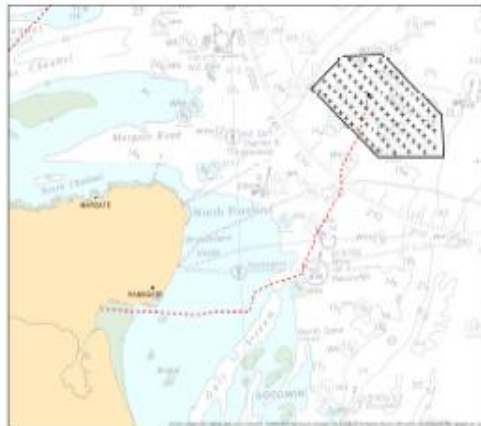

Distribution

See e-mail address header


WORK PLANNED FOR PERIOD: FROM 18/01/10 TO 24/01/10

Description: (subject to weather conditions)
18/01/10 – Sea Jack transits to F07 to install MP. Polar Prince installing cable B10 – B09. Resolution on site at B14 to install WTG.
19/01/10 – Sea Jack installing monopole at F08. Polar Prince installing cable B10 – B09. Resolution on site at C12 to install WTG.
20/01/10 – Sea Jack at Ramsgate for loadout, Polar Prince installing cable D14 ~ D13, Resolution at C13 to install WTG.
21/01/10 - Sea Jack transits to G08, Polar Prince installing cable D14 ~ D13, Resolution at B10 to install WTG.
22/01/10 – Sea Jack installing monopole at G08, Polar Prince installing cable D13 – D12 Resolution install WTG on B12.
23/01/10 – Sea Jack relocates to E10, Polar Prince install cable D11 - D10. Resolution install WTG at B13.
24/01/10 – Sea Jack install MP at E10. Polar Prince install cable at E16 – E15. Resolution install WTG at C14.
<ul style="list-style-type: none"> • Tugs Stevns Arctic and Bever tow tugs and field support for Sea Jack. • Tug Osprey Fighter towing monopile supply barges to / from Ramsgate & Vlissingen. • Tug Meander assisting Sea Jack and Osprey Fighter as required. • Tug Multratug 18 & Maggie M to assist the non-propelled barge UR101 as required. • DP Ship Polar Prince cable laying – Inter array cables between turbine foundations. • DP Ship Normand Mermaid cable laying – Inter array cables between turbine foundations • Barge UR101 cable laying - export cables from Pegwell Bay. • Crew boat Waterfall performing Marine Mammal Observations and various crew changes, transfers & TP maintenance. • Crew boat Offshore Performer (OP3) assisting with crew changes, transfers & TP maintenance. • Crew boat Sea Weasel for crew changes to Polar Princes & barges (Subocean). • Crew boats Endeavour & Enterprise for WTG access (Vestas) • Crew boat Channel Chieftain for survey work • M/S Line performing post laid cable surveys. • Guard boat Brockelsby in field for monitoring vessel movements and collision avoidance.

WORK COMPLETED FROM: 11/01/10 TO 17/01/10

Date	Description
11/01/10	<ul style="list-style-type: none"> • Sea Jack departs Ramsgate for F10. Polar Prince installed array cable from C13 to C12.
12/01/10	<ul style="list-style-type: none"> • Sea Jack installs monopole at F10
13/01/10	<ul style="list-style-type: none"> • Resolution departs Dunkirk for E17. Sea Jack enters Ramsgate
14/01/10	<ul style="list-style-type: none"> • Sea Jack installs monopole at D07. Resolution installs WGT at E17
15/01/10	<ul style="list-style-type: none"> • Sea Jack installs monopole at F09
16/01/10	<ul style="list-style-type: none"> • Waiting on weather
17/01/10	<ul style="list-style-type: none"> • Resolution installs WGT at C10

Field Status Report 17th January 2010

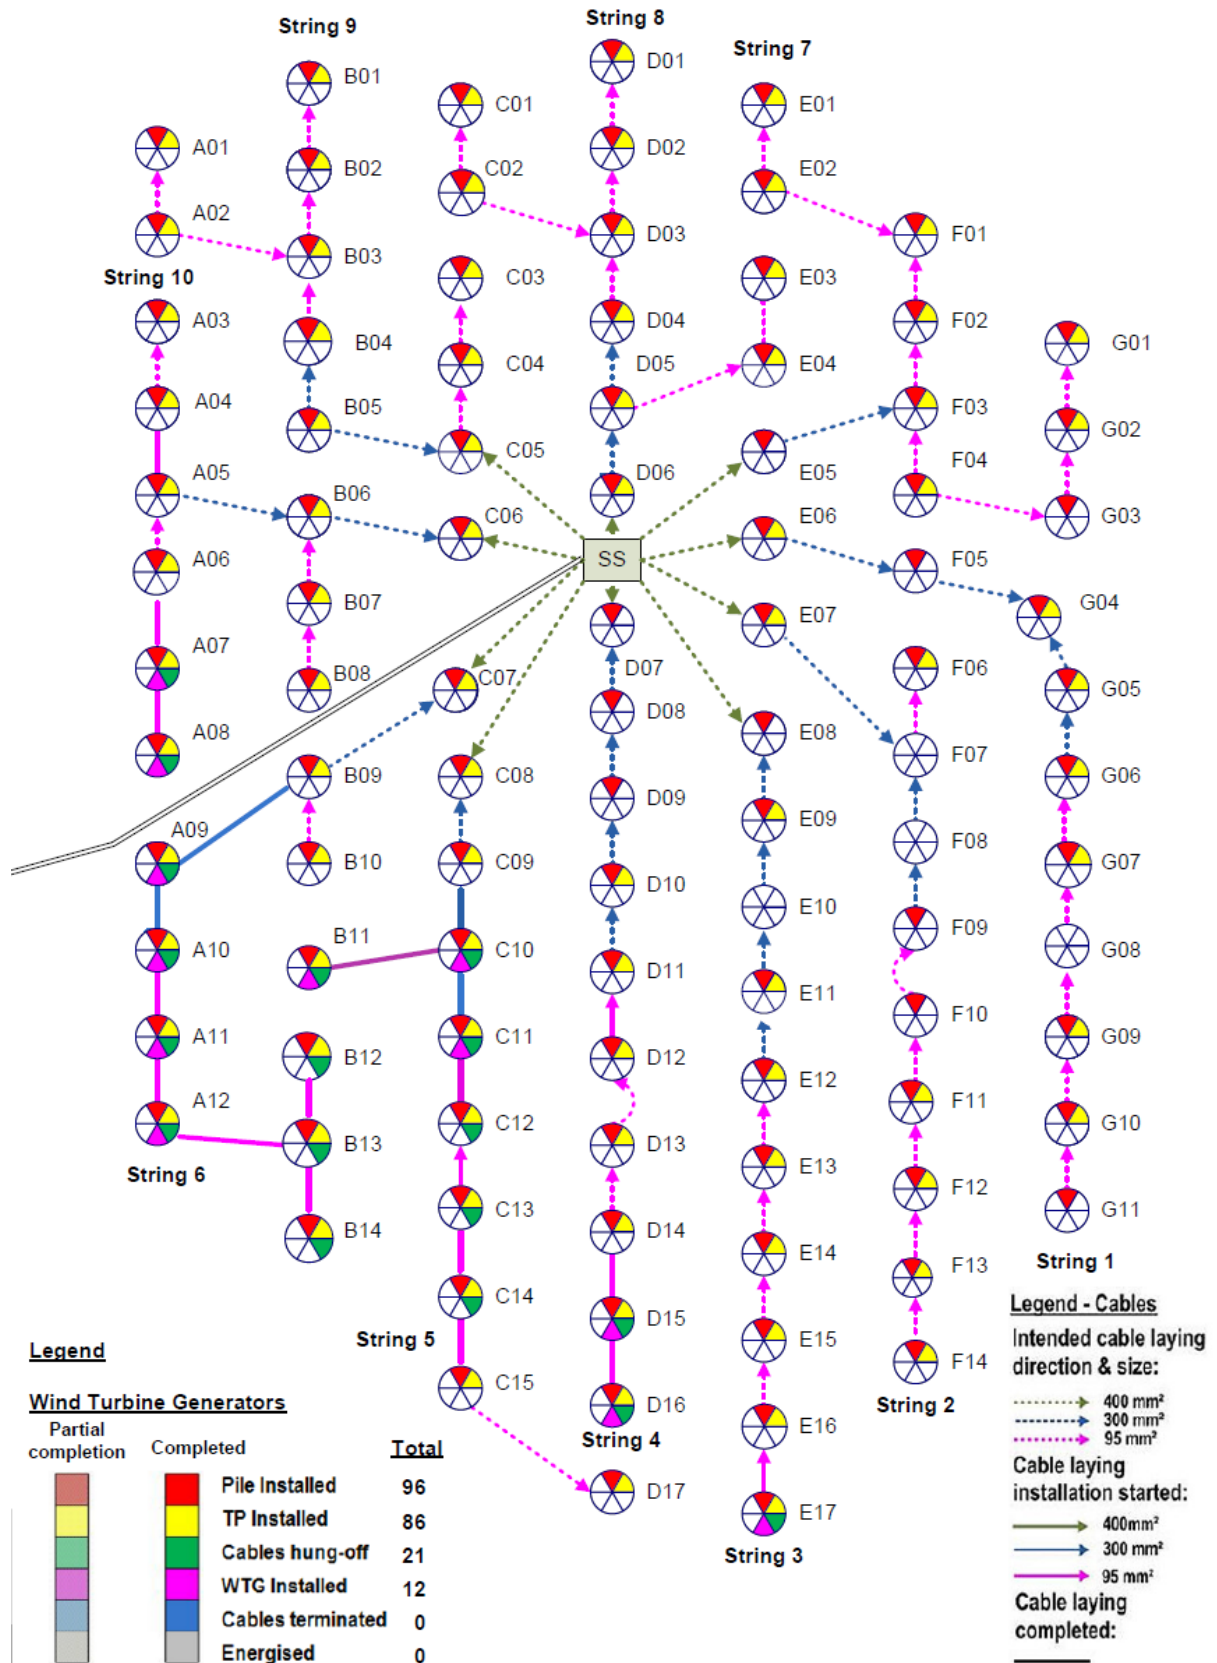

ON PROJECT VESSEL LIST :

Name	Type
Offshore Performer(OP3)	Crew vessel
Waterfall	Crew vessel
Sea Weasel	Crew vessel
Endeavour	Crew vessel
Enterprise	Crew vessel
Channel Chieftain	Survey vessel
Brockelsby	Guard vessel
Bever	Tug
Stevns Arctic	Tug
Meander	Tug
Osprey Fighter	Tug
Multratug 18	Tug
Sea Jack	Jack Up
MPI Resolution	Jack Up (DP)
Polar Prince	Cable lay (DP)
Normand Mermaid	Cable lay (DP)
UR101	Cable lay barge
Maggie M	Multicat
M/S Line	Survey
Arie Dirk	Environmental (Birds)

NOTES

This document will be issued every Monday and will describe the planned activities for the next 7 days. Normal liaison for offshore operations is between the TOW Marine Coordinator and:

- Captain Rob Brown – Interim Harbour Master Port of Ramsgate; and
- Kaimes Beasley – CNIS Manager Dover MCA

This weekly report will be distributed to those recipients listed on the email address header on a weekly basis and is intended to inform those recipients of TOW's planned activities over the forthcoming week.

For further information or comments please contact:

The Duty Marine Coordinator:

Office: +44 (0) 1843 572130

Mobile: +44 (0) 7825880528

Fax: +44 (0) 1843 572131

Email: marinecoordinator@thanetoffshorewind.com
