

# Thanet Offshore Wind Limited


## Weekly Notice of Operations to Stakeholders

---

Date of Notice 22/02/2010

Notice No.49

---

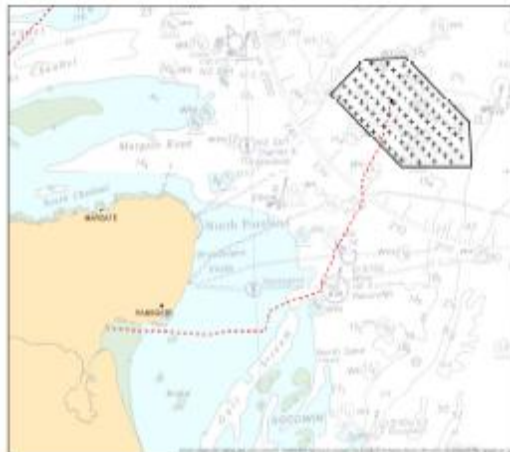

### Distribution

See e-mail address header


## WORK PLANNED FOR PERIOD: FROM 22/02/10 TO 28/02/10

<b>Description:</b> (subject to weather conditions)
22/02/10 Sea Jack install TP at E10. P.Prince cable A05-B06. N.Mermaid B07-B06. Resolution installs WTG at A02.
23/02/10 Sea Jack install TP at F08. P.Prince cable B05-B04. N.Mermaid B08-B07. Resolution installs WTG at A03
24/02/10 Sea Jack in Ramsgate for loadout. P.Prince installing cable B09-C07. N.Mermaid installing cable C04-C03. Resolution installs WTG at A04. Possible weather downtime
25/02/10 Sea Jack in Ramsgate for loadout. P.Prince installing cable B09-C07. N.Mermaid installing cable C04-C03. Resolution installs WTG at A04. Possible weather downtime
26/02/10 Sea Jack install TP at G08 . P.Prince installing cable B06-C06. N.Mermaid installing cable C05-C04. Resolution installs WTG at A05
27/02/10 Sea Jack install TP at F09 . P.Prince installing cable G05-G04. N.Mermaid installing cable F02-F01. Resolution installs WTG at A06
28/02/10 Sea Jack install TP at F10 . P.Prince installing cable G05-G04. N.Mermaid installing cable F02-F01. Resolution installs WTG at B04. Possible weather downtime
<ul style="list-style-type: none"> <li>• Tugs Stevns Arctic and Bever tow tugs and field support for Sea Jack.</li> <li>• Tug Osprey Boxer towing transition piece supply barges to / from Ramsgate &amp; Vlissingen.</li> <li>• Tug Meander assisting Sea Jack and Osprey Fighter as required.</li> <li>• Multratug 18 to assist the non-propelled barge UR101 as required.</li> <li>• DP Ship Polar Prince cable laying – Inter array cables between turbine foundations.</li> <li>• DP Ship Normand Mermaid cable laying – Inter array cables between turbine foundations</li> <li>• Barge UR101 cable laying - export cables from Pegwell Bay.</li> <li>• Crew boat Waterfall performing Marine Mammal Observations and diving ops.</li> <li>• Crew boat Offshore Performer (OP3) assisting with crew changes, &amp; TP maintenance</li> <li>• Crew boats Sea Weasel, Sea Beaver &amp; Sea Badger for crew changes to Polar Princes &amp; Normand Mermaid (Subocean).</li> <li>• Crew boats Strider, Lesley Jay, Supporter, Voyageur &amp; Distributor servicing Multicats Forth Jouster and Forth Fighter</li> <li>• Crew boats Endeavour, Enterprise &amp; George D for WTG access (Vestas)</li> <li>• M/S Line performing post laid cable surveys.</li> <li>• Multicat Forth Jouster &amp; Forth Fighter assisting with TP maintenance and diving operations, diving surveys &amp; 2<sup>nd</sup>. end cable pull-ins</li> <li>• Guard boat Gitte in field for monitoring vessel movements and collision avoidance.</li> <li>• Fishing vessel Arie Dirk used for environmental surveys.</li> <li>• Tug Shoalbaster supporting Oil Express with cable cross pre-lay cable mattress installation</li> </ul>

### WORK COMPLETED FROM: 15/02/10 TO 21/02/10

Date	Description
15/02/10	<ul style="list-style-type: none"><li>• WTG D11 completed. Cable installed F12-F11. Cable installed F14-F13</li></ul>
16/02/10	<ul style="list-style-type: none"><li>• Cable installed A06-A05.</li></ul>
17/02/10	<ul style="list-style-type: none"><li>• . Cable installed E02-E01</li></ul>
18/02/10	<ul style="list-style-type: none"><li>• Cable installed A04-A03. Cable installed C02-D03. Cable installed C02-C01</li></ul>
19/02/10	<ul style="list-style-type: none"><li>• Cable installed E02-F01</li></ul>
20/02/10	<ul style="list-style-type: none"><li>• Cable installed G07-G06. Cable installed C02-D01. TP 07 installed. Substation jacket &amp; topside installed</li></ul>
21/02/10	<ul style="list-style-type: none"><li>• Cable installed G06-G05. Cable installed D03-D02. WTG E13 completed.</li></ul>

Field Status Report 22<sup>nd</sup>. February 2010

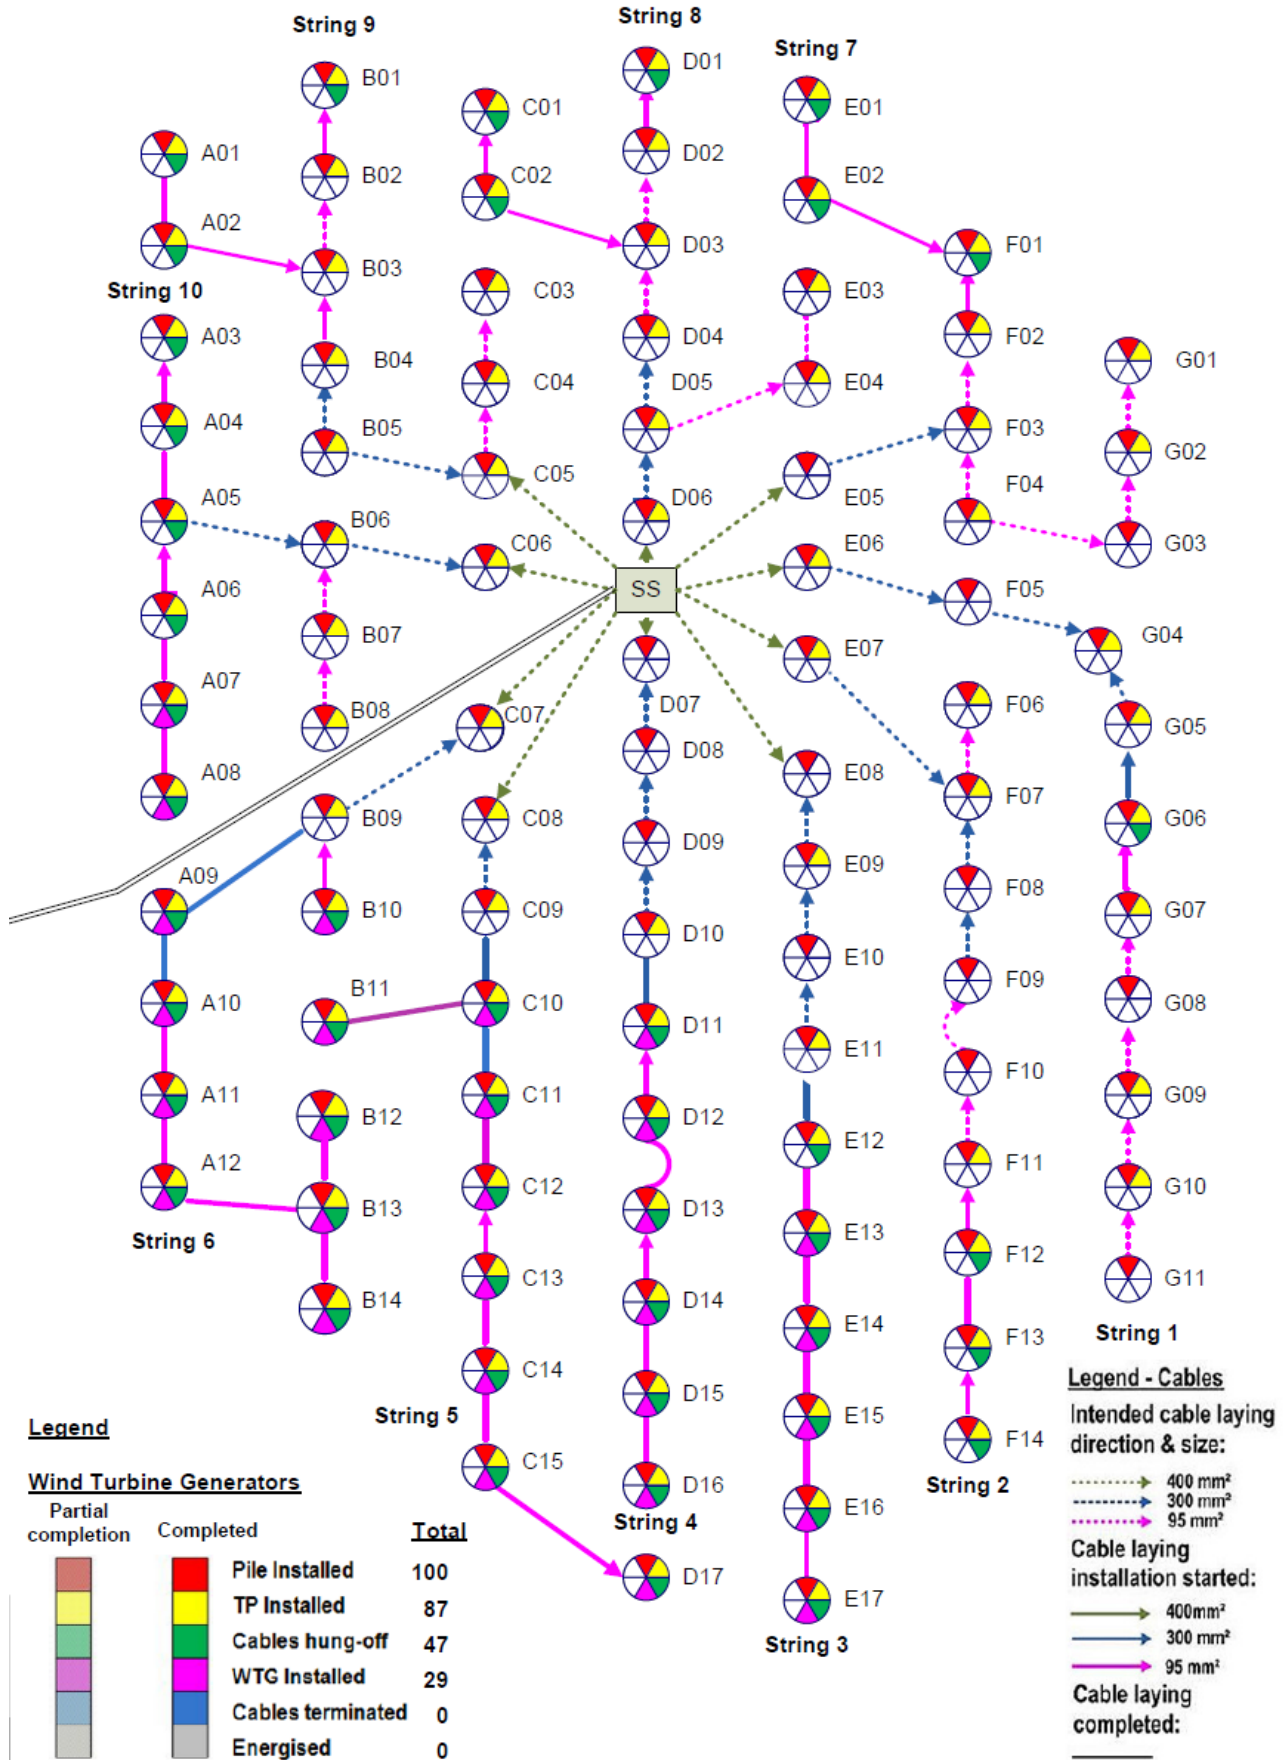

## ON PROJECT VESSEL LIST :

Name	Type
Offshore Performer(OP3)	Crew vessel
Waterfall	Crew/diving vessel
Sea Weasel	Crew vessel
Sea Beaver	Crew vessel
Sea Badger	Crew vessel
Endeavour	Crew vessel
Enterprise	Crew vessel
Meriel D	Crew vessel
Strider & Lesley Jay	Crew vessel
Distributor	Crew vessel
Supporter	Crew vessel
Voyageur	Crew vessel
Gitte	Guard vessel
Bever	Tug
Stevns Arctic	Tug
Meander	Tug
Osprey Boxer	Tug
Shaolbuster	Tug
Sea Jack	Jack Up
MPI Resolution	Jack Up (DP)
Polar Prince	Cable lay (DP)
Normand Mermaid	Cable lay (DP)
UR101	Cable lay barge
M/S Line	Survey
Arie Dirk	Environmental (Birds)
Forth Joust & Forth Fighter	Multicat
Voe Viking	Multicat
Oil Express	Diving Support Vessel
Strider	Crew vessel
George D	Crew vessel
Ocean Cat	Crew vessel
Lesley Jay	Crew vessel

### NOTES

This document will be issued every Monday and will describe the planned activities for the next 7 days. Normal liaison for offshore operations is between the TOW Marine Coordinator and:

- Captain Rob Brown – Interim Harbour Master Port of Ramsgate; and
- Kaimes Beasley – CNIS Manager Dover MCA

This weekly report will be distributed to those recipients listed on the email address header on a weekly basis and is intended to inform those recipients of TOW's planned activities over the forthcoming week.

For further information or comments please contact:

**The Duty Marine Coordinator:**

**Office:** +44 (0) 1843 572130

**Mobile:** +44 (0) 7825880528

**Fax:** +44 (0) 1843 572131

**Email:** [marinecoordinator@thanetoffshorewind.com](mailto:marinecoordinator@thanetoffshorewind.com)
