


Thanet Offshore Wind Limited  
**Weekly Notice of Operations to Stakeholders**

---

**Date of Notice 30/05/2010**

**Notice No.63**

---

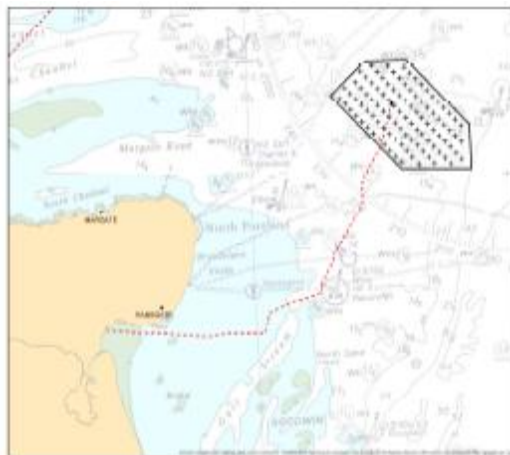

**Distribution**

See e-mail address header


**WORK PLANNED FOR PERIOD: FROM 31/05/10 TO 06/06/10**

<b>Description:</b> (subject to weather conditions)
31/05/10 – Resolution at E02, Normand Mermaid at E11, Sia at E01 – all WOW.
01/06/10 - Resolution at E02, Normand Mermaid at E11, Sia at E01 – all WOW.
02/06/10 – Resolution install WTG at E02, N.Mermaid lay cable E11 – E10, Sia 2 <sup>nd</sup> end pull at E01.
03/06/10 - Resolution install WTG at F01, N.Mermaid lay cable F07-F06, Sia 2 <sup>nd</sup> end pull at E01.
04/06/10 - Resolution install WTG at F02, N.Mermaid lay cable F07-E07, Sia 2 <sup>nd</sup> end pull at D07.
05/06/10 - Resolution install WTG at F03, N.Mermaid lay cable G02-G03, Sia 2 <sup>nd</sup> end pull at D08.
06/06/10 - Resolution install WTG at G03, N.Mermaid laid cable surveys, Sia 2 <sup>nd</sup> end pull at D09.
<ul style="list-style-type: none"> <li>• Multratug 18 to assist the non-propelled barge UR101 as required.</li> <li>• DP Ship Normand Mermaid cable laying – Inter array cables between turbine foundations and substation</li> <li>• Barge UR101 cable laying - export cables from shore to crossing, assisted by the tug Multra tug 18 and multicats Maggie M &amp; Northern Kestrel.</li> <li>• DP ship Sia – second end cable pulling.</li> <li>• Crew boat Waterfall for TOW terminators. Wildcat 1 crew changes for multicats.</li> <li>• Crew boat Offshore Performer (OP3) for use of cleaning access ladders and guano.</li> <li>• Crew boats Sea Beaver for crew changes to Normand Mermaid &amp; Sea Badger, dive support</li> <li>• Crew boats Lesley Jay, Wildcat 1, Deliverer &amp; MPI Rucio servicing Multicats Forth Jouster and Forth Fighter, Morag M, grey Mammoth</li> <li>• Crew boats Endeavour, Enterprise, Windcat 12, Wind Crew 1&amp; George D for WTG access (Vestas)</li> <li>• M/S Line performing post laid cable surveys.</li> <li>• Multicat Forth Jouster &amp; Forth Fighter diving operations, diving surveys &amp; 2<sup>nd</sup> end cable pull-ins</li> <li>• Guard boats Gitte and Reliance in field for monitoring vessel movements and collision avoidance.</li> <li>• Strider assisting with termination works</li> <li>• Morag M, Grey Mammoth, Norfolk Swift and Topline are working on remedial cable ops.</li> </ul>

**WORK COMPLETED FROM 24/05/10 TO 30/05/10**

Date	Description
24/05/10	<ul style="list-style-type: none"> <li>• Resolution installed WTG at E01,</li> </ul>
25/05/10	<ul style="list-style-type: none"> <li>• Resolution installed WTG at G01. Normand Mermaid installed cable at G01-G02.</li> </ul>
26/05/10	<ul style="list-style-type: none"> <li>• Resolution in Dunkirk, N.Mermaid survey of export cable.</li> </ul>
27/05/10	<ul style="list-style-type: none"> <li>• Resolution in Dunkirk, N.Mermaid survey of export cable.</li> </ul>
28/05/10	<ul style="list-style-type: none"> <li>• Resolution in Dunkirk, N.Mermaid survey of E03</li> </ul>
29/05/10	<ul style="list-style-type: none"> <li>• Resolution on site at E01. N.Mermaid survey of 2<sup>nd</sup> end B04-B05.</li> </ul>
30/05/10	<ul style="list-style-type: none"> <li>• Resolution &amp; Normand Mermaid – WOW. Sia arrived at site.</li> </ul>

Field Status Report 30<sup>th</sup> May 2010

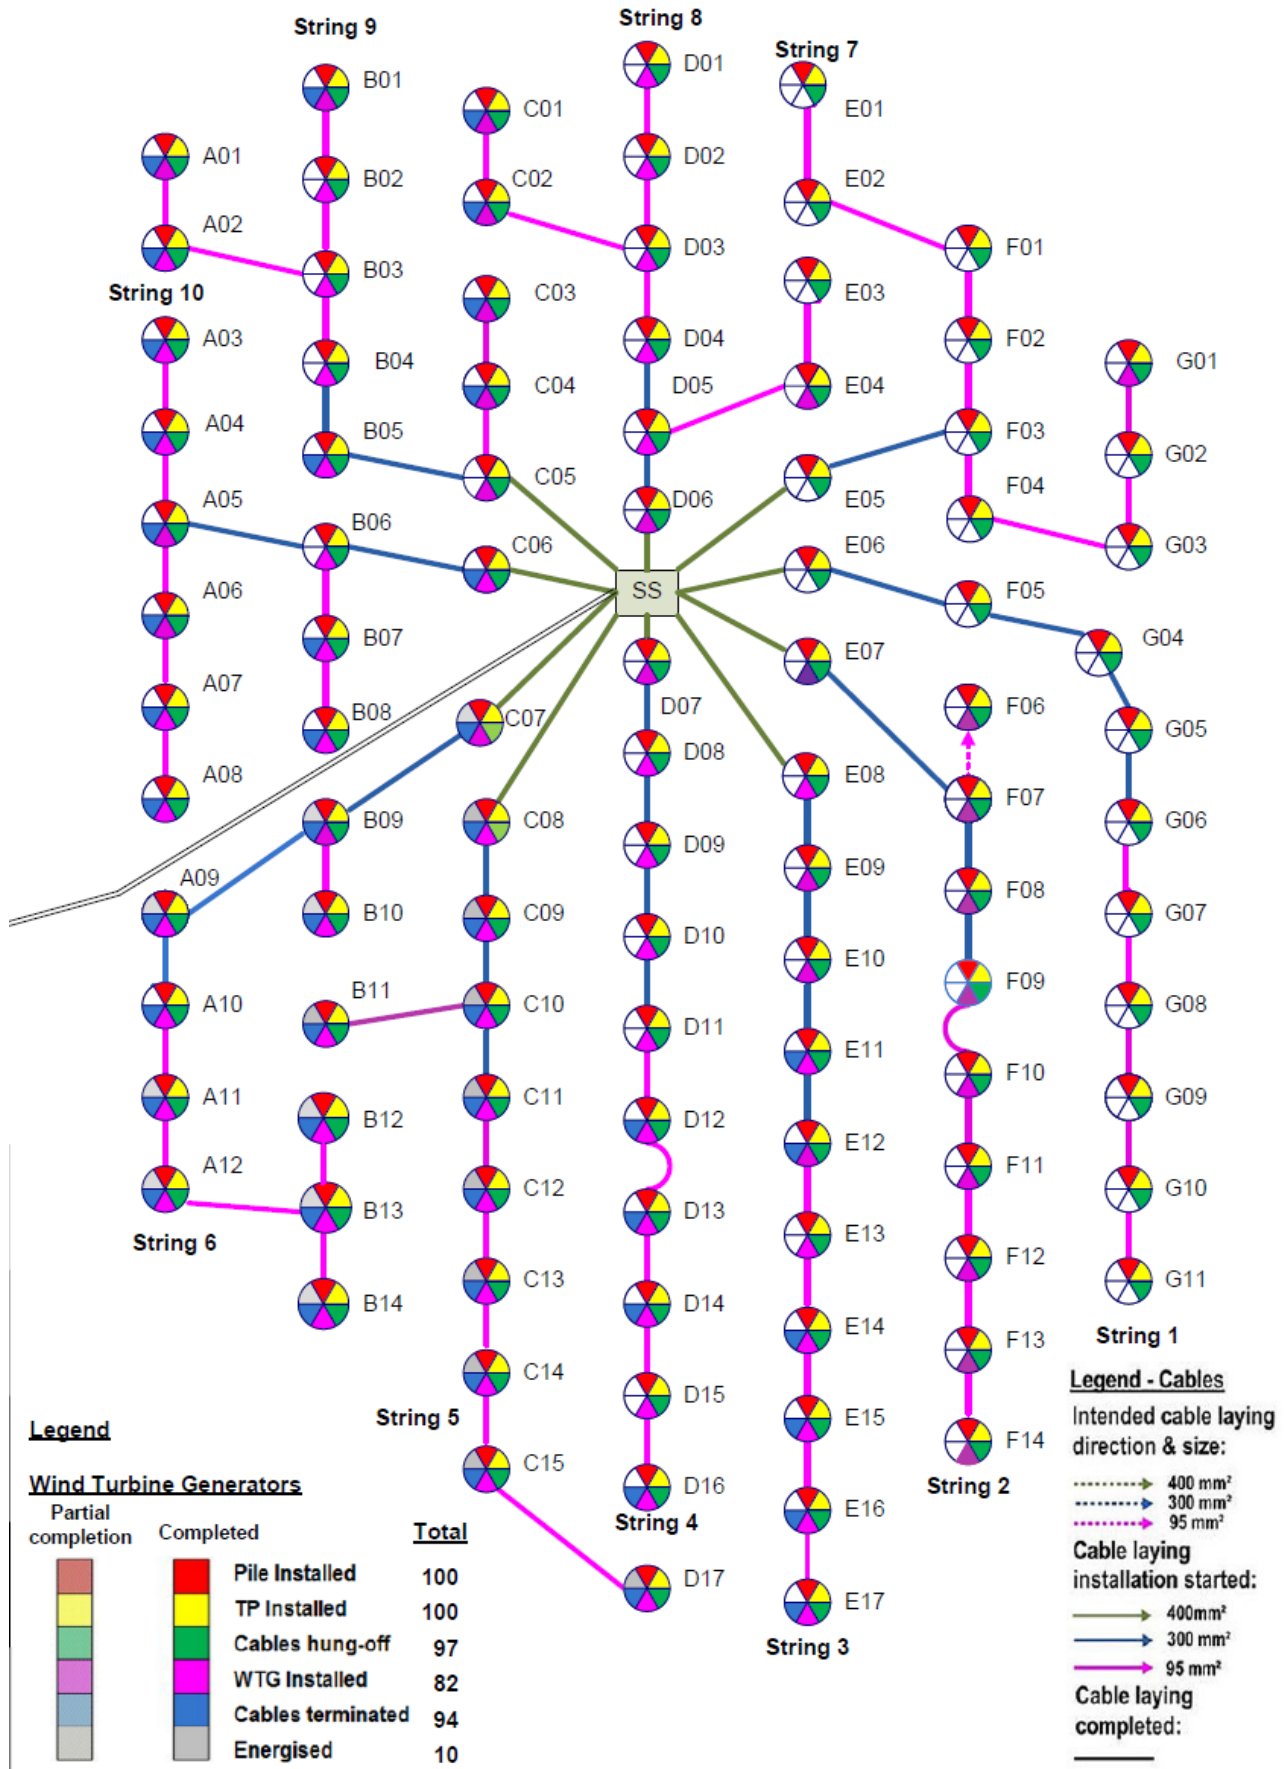

## ON PROJECT VESSEL LIST:

Name	Type
Offshore Performer(OP3)	Crew vessel
Waterfall	Crew vessel
Wildcat 1	Crew Vessel
Sea Beaver	Crew vessel
Sea Badger	Crew vessel
Endeavour	Crew vessel
Enterprise	Crew vessel
Lesley Jay	Crew vessel
MPI Rucio	Crew vessel
Deliverer	Crew vessel
Windcat 12	Crew vessel
Topline	Crew Vessel
Wind Crew 1	Crew vessel
Strider	Crew Vessel
Moidart	Crew vessel
Norfolk Swift	Crew vessel
MPI Resolution	Jack Up (DP) Installation v/l
Sia	DP cable installation ship
Normand Mermaid	Cable lay (DP) v/l
UR101	Cable lay barge
Multatug 18	Tug
Ocean Cat	Dive support v/l
Grey Mammoth	Multicat Dive support
Forth Jouster & Forth Fighter	Multicat Dive support
Maggie M	Multicat
Morag M	Multicat
Northern Kestrel	Multicat
M/S Line	Survey
Gitte	Guard vessel

## **NOTES**

This document will be issued every Monday and will describe the planned activities for the next 7 days. Normal liaison for offshore operations is between the TOW Marine Coordinator and:

- Captain Rob Brown – Interim Harbour Master Port of Ramsgate; and
- Kaimes Beasley – CNIS Manager Dover MCA

This weekly report will be distributed to those recipients listed on the email address header on a weekly basis and is intended to inform those recipients of TOW's planned activities over the forthcoming week.

For further information or comments please contact:

### **The Duty Marine Coordinator:**

**Office:** +44 (0) 1843 572130

**Mobile:** +44 (0) 7825880528

**Fax:** +44 (0) 1843 572131

**Email:** [marinecoordinator@thanetoffshorewind.com](mailto:marinecoordinator@thanetoffshorewind.com)
