


Thanet Offshore Wind Limited

Weekly Notice of Operations to Stakeholders

Date of Notice 02/11/09

Notice No.33

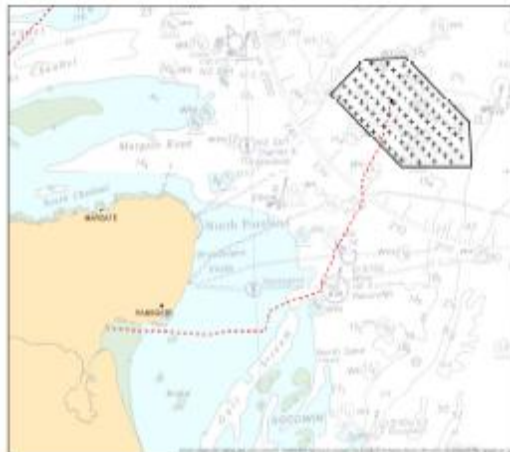

Distribution

See e-mail address header


WORK PLANNED FOR PERIOD: FROM 02/11/09 TO 08/11/09

Description: (subject to weather conditions)
02/11/09 – Resolution at A05 for snagging work. SeaJack at Ramsgate for loadout. Polar Prince laying cable D16 to C15. UR101 laying cable between A12 & B13. Sander continue ROV survey of as-laid cable routes.
03/11/09 – Resolution carrying out snagging work until D08 available for installing TP, Sea Jack installing MP at D08, Polar Prince cable lay D16 to D15. UR101 cable lay A12 – B13. Sander continue ROV survey of as-laid cable routes.
04/11/09 – Resolution on D08 installing TP, Sea Jack installs MP on D09. Polar Prince cable lay C15 to C14. UR101 cable lay A12 to B13. Sander continue ROV survey of as-laid cable routes.
05/11/09 – Resolution on D09 installing TP. Sea Jack in Ramsgate for loadout. Polar Prince cable lay D14 to D13. UR101 cable lay A12 to B13. Sander continue ROV survey of as-laid cable routes.
06/11/09 – Resolution on D07 installing TP. Sea Jack at D07 installing MP. Polar Prince cable lay D13 to D12. UR101 cable lay A12 to B13. Sander continue ROV survey of as-laid cable routes.
07/11/09 – Resolution continues with snagging list and/or returns to Vlissingen for cycle 19. Sea Jack in Ramsgate for loadout. Polar Prince continues cable lay. UR101 continues cable lay. Sander continue ROV survey of as-laid cable routes.
08/11/09 – Resolution continues with snagging list and/or returns to Vlissingen for cycle 19. Sea Jack installing next MP sequence. Polar Prince continues cable lay. UR101 continues cable lay. Sander continue ROV survey of as-laid cable routes.
<ul style="list-style-type: none"> • Tugs Stevns Arctic and Bever tow tugs and field support for Sea Jack. • Tug Osprey Fighter towing monopile supply barges to / from Ramsgate & Vlissingen. • Tug Meander assisting Sea Jack and Osprey Fighter as required. • Tug Keverne to assist the non-propelled barge UR101 as required. • Multicat Voe Jarl performing Prelay grapnel run operations in field. • DP Ship Polar Prince cable laying – Inter array cables between turbine foundations. • Crew boat Waterfall performing Marine Mammal Observations and various crew changes and transfers. • Crew boat Offshore Performer (OP3) assisting with crew changes / transfers & TP maintenance. • Crew boat Sea Weasel & Sea Beaver for crew changes to Polar Princes & barges (Subocean). • Sander performing post laid cable surveys. • Guard boat Brocklesby in field for monitoring vessel movements and collision avoidance.

WORK COMPLETED FROM: 26/10/09 TO 01/11/09

Date	Description
26/10/09	<ul style="list-style-type: none"> • Resolution at Safe Haven WOW then installing TP at B02. Sea Jack arrives Ramsgate. Polar Prince by B14
27/10/09	<ul style="list-style-type: none"> • Resolution installed TP at B02. Sea Jack installs MP at B01. Polar Prince laying cable between C12 – C11. UR101 arrives at TOW field at A12
28/10/09	<ul style="list-style-type: none"> • Resolution installed TP's on B03 and B01. Sea Jack installed MP at D06. Polar Prince cable lay C11 to C12. UR101 at A12.
29/10/09	<ul style="list-style-type: none"> • Resolution moves from B01 to D06. Sea Jack in Ramsgate. Polar Prince completed cable lay from C12 to C11. UR101 at A12. Sander working at Gunfleet Sands.
30/10/09	<ul style="list-style-type: none"> • Resolution installed TP on D06. Sea Jack left Ramsgate for B06. Polar Prince cable lay C10 to C09. UR101 at A12 Sander alongside in Ramsgate.
31/10/09	<ul style="list-style-type: none"> • Resolution moved from D06 to B06 . Sea Jack installed MP at B06. Polar Prince cable lay from C10 to C09. UR101 left A12/A11 for Ramsgate Roads Sander in Ramsgate
01/11/09	<ul style="list-style-type: none"> • Resolution installed TP on B06. Sea Jack installed MP at C07. Polar Prince continues cable lay from C10 to C09 before WOW off Margate. UR101 off Margate WOW. Sander in Ramsgate WOW.

Field Status Report 2nd November 2009

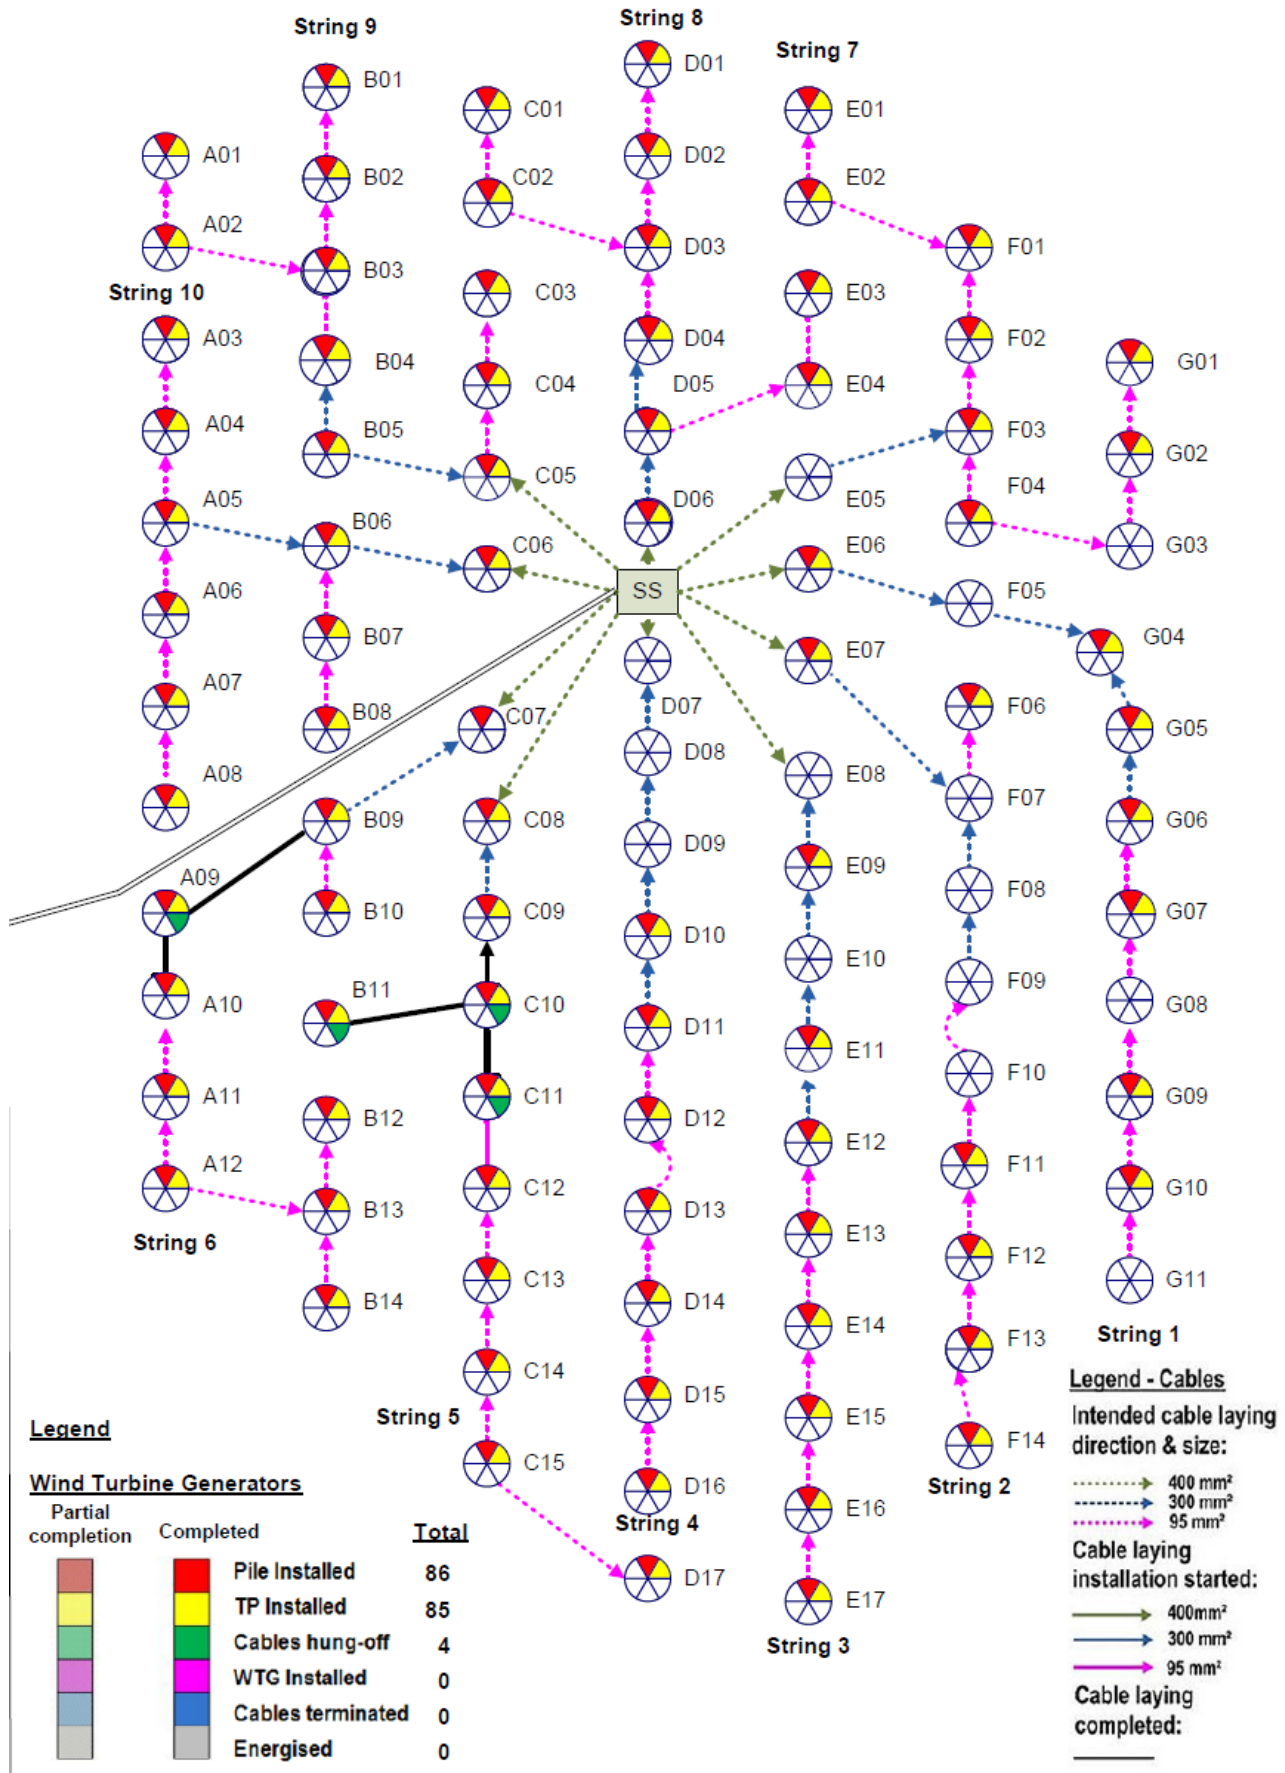

ON PROJECT VESSEL LIST :

Name	Type
Offshore Performer(OP3)	Crew vessel
Waterfall	Crew vessel
Sea Weasel	Crew vessel
Bever	Tug
Sea Jack	Jack Up
Stevns Arctic	Tug
MPI Resolution	Jack Up (DP)
Brocklesby	Guard vessel
Meander	Tug
Osprey Fighter	Tug
Polar Prince	Survey (DP)
Voe Jarl	Multicat
Sander	Survey
Arie Dirk	Environmental (Birds)

NOTES

This document will be issued every Monday and will describe the planned activities for the next 7 days. Normal liaison for offshore operations is between the TOW Marine Coordinator and:

- Captain Rob Brown – Interim Harbour Master Port of Ramsgate; and
- Kaimes Beasley – CNIS Manager Dover MCA

This weekly report will be distributed to those recipients listed on the email address header on a weekly basis and is intended to inform those recipients of TOW's planned activities over the forthcoming week.

For further information or comments please contact:

The Duty Marine Coordinator:

Office: +44 (0) 1843 572130

Mobile: +44 (0) 7825880528

Fax: +44 (0) 1843 572131

Email: marinecoordinator@thanetoffshorewind.com
