


Thanet Offshore Wind Limited

Weekly Notice of Operations to Stakeholders

Date of Notice 15/02/2010

Notice No.48

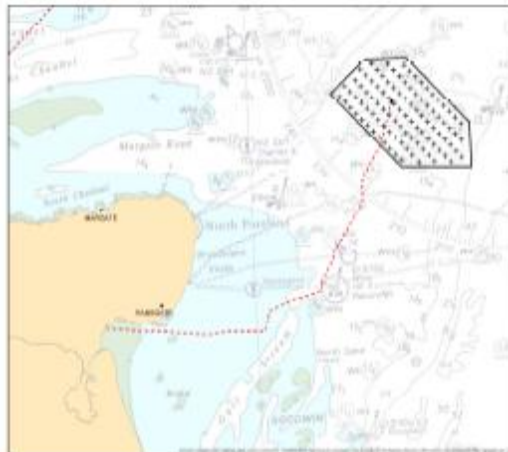

Distribution

See e-mail address header


WORK PLANNED FOR PERIOD: FROM 15/02/10 TO 21/02/10

Description: (subject to weather conditions)
15/02/10 Sea Jack install TP at F07. Stanislav installing SS jacket. P.Prince cable A04-A03. N.Mermaid F14-F13. Resolution WTG at D11.
16/02/10 Stanislav installing SS jacket. Sea Jack install TP at E10. P.Prince cable A04-A03. N.Mermaid C02-C01. Resolution departs for Dunkirk
17/02/10 Sea Jack install TP at E10 P.Prince cable A06-A05. N.Mermaid C02-C01. Stanislav Yudin install module on SS Jacket.
18/02/10 Sea Jack install TP at F08 N.Mermaid cable C02-D03. P.Prince installing cable & recovering SAFs Stanislav Yudin install module on SS Jacket.
19/02/10 Sea Jack sail to Ramsgate. N. Mermaid installing cable P.Prince installing cable & recovering SAFs
20/02/10 N. Mermaid installing cable P.Prince installing cable
21/02/10 Sea Jack sails for site. N. Mermaid installing cable P.Prince installing cable
<ul style="list-style-type: none"> • Tugs Stevns Arctic and Bever tow tugs and field support for Sea Jack. • Tug Osprey Boxer towing transition piece supply barges to / from Ramsgate & Vlissingen. • Tug Meander assisting Sea Jack and Osprey Fighter as required. • Tug Shoalbuster & Voe Viking to assist the non-propelled barge UR101 as required. • DP Ship Polar Prince cable laying – Inter array cables between turbine foundations. • DP Ship Normand Mermaid cable laying – Inter array cables between turbine foundations • Barge UR101 cable laying - export cables from Pegwell Bay. • Crew boat Waterfall performing Marine Mammal Observations and diving ops. • Crew boat Offshore Performer (OP3) assisting with crew changes, transfers & TP maintenance. • Crew boats Sea Weasel, Sea Beaver & Ocean Cat for crew changes to Polar Princes & Normand Mermaid (Subocean). • Crew boats Strider, Supporter, Voyageur & Distributor servicing Multcats Jouster and Fighter. • Crew boats Endeavour, Enterprise & Meriel D for WTG access (Vestas) • Heavy lift ship Stanislav Yudin for the installation of the Offshore sub-station assisted by tugs, Typhoon, Blizzard and Red Wolf. • M/S Line performing post laid cable surveys. • Multicat Forth Jouster & Forth Fighter assisting with TP maintenance and diving operations • Guard boat Brockelsby in field for monitoring vessel movements and collision avoidance. To be replaced by guard boat Gitte

WORK COMPLETED FROM: 08/02/10 TO 14/02/10

Date	Description
08/02/10	<ul style="list-style-type: none"><li data-bbox="571 593 903 622">• Cable installed B04-B03
09/02/10	<ul style="list-style-type: none"><li data-bbox="571 647 842 676">• Waiting on weather
10/02/10	<ul style="list-style-type: none"><li data-bbox="571 701 842 730">• Waiting on weather
11/02/10	<ul style="list-style-type: none"><li data-bbox="571 754 842 784">• Waiting on weather
12/02/10	<ul style="list-style-type: none"><li data-bbox="571 808 842 837">• Waiting on weather
13/02/10	<ul style="list-style-type: none"><li data-bbox="571 862 868 891">• WTG E16 completed.
14/02/10	<ul style="list-style-type: none"><li data-bbox="571 916 868 945">• WTG E15 completed.

Field Status Report 15th February 2010

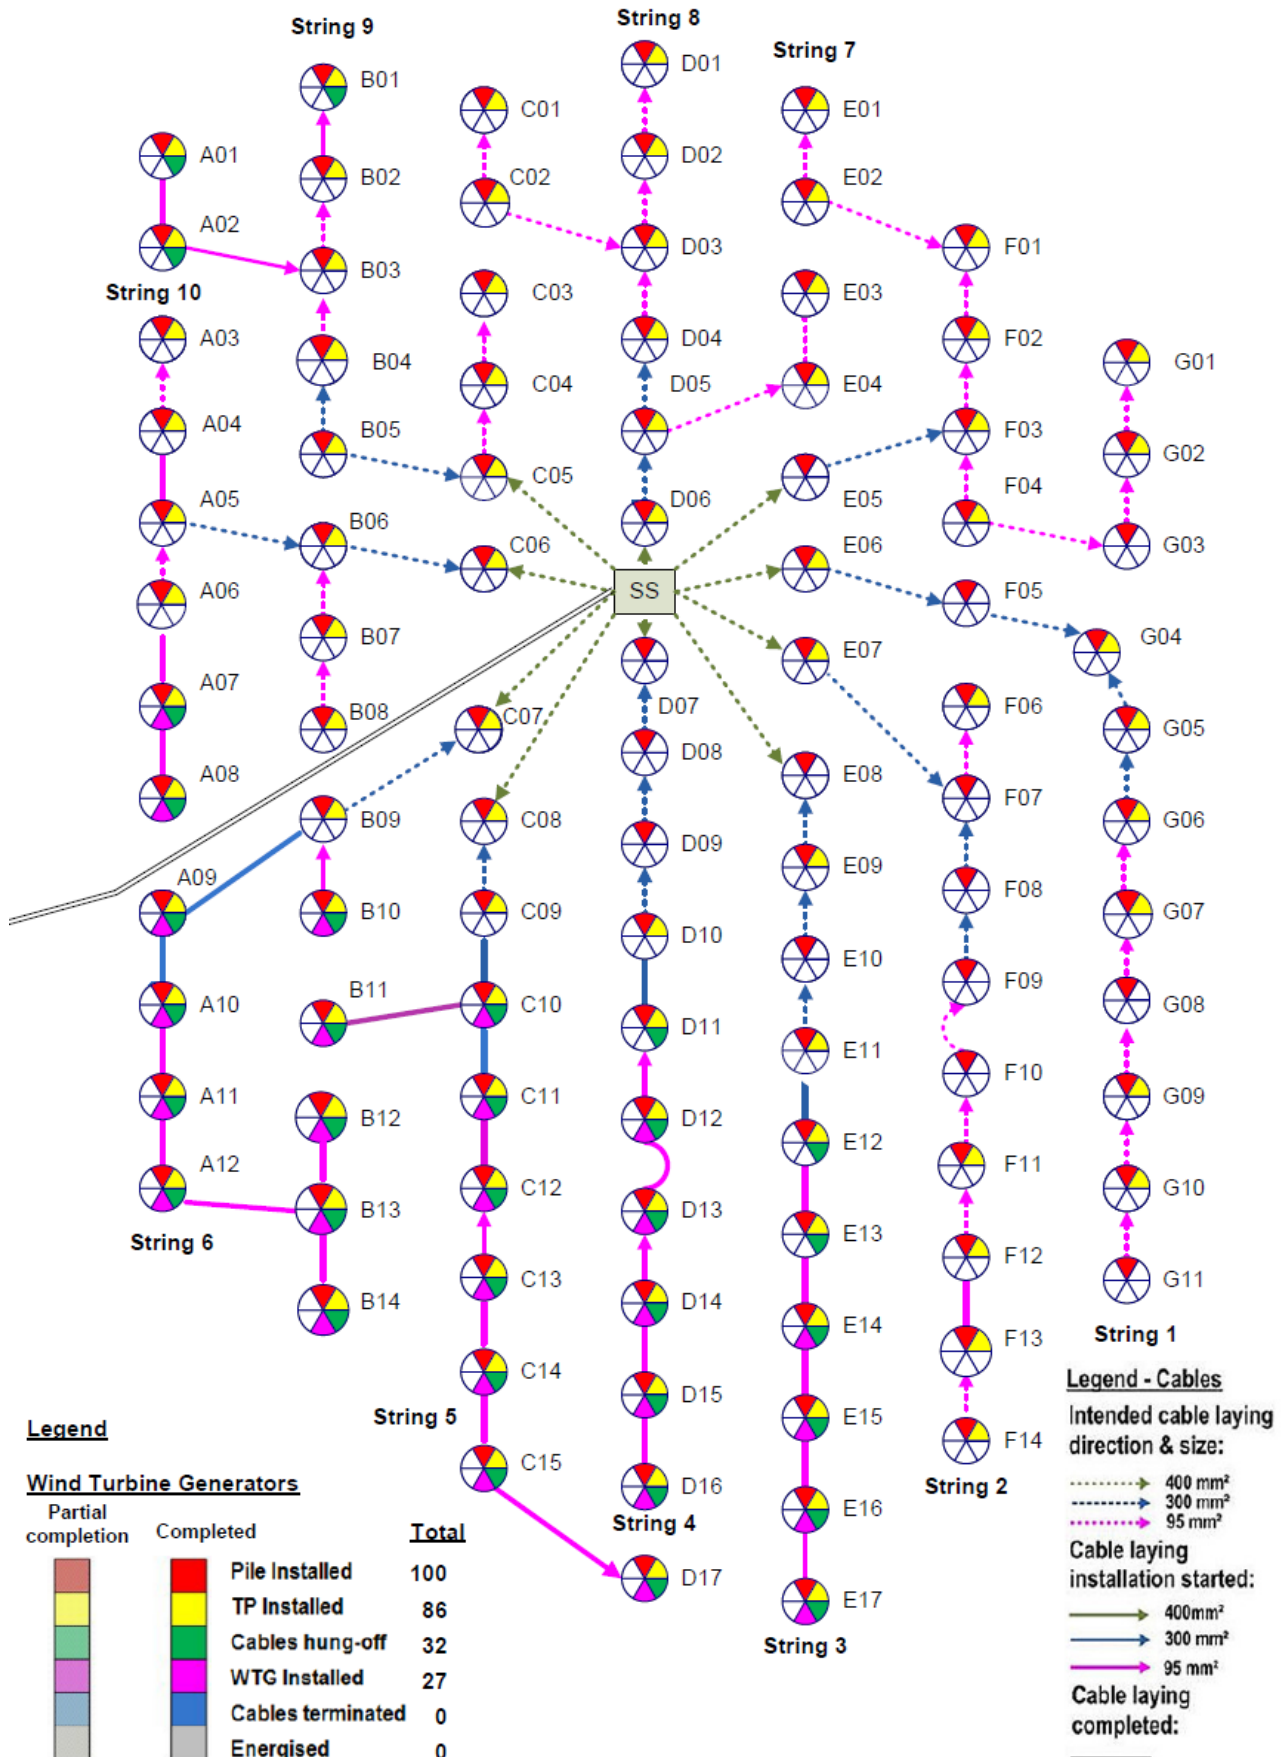

ON PROJECT VESSEL LIST :

Name	Type
Offshore Performer(OP3)	Crew vessel
Waterfall	Crew/diving vessel
Sea Weasel	Crew vessel
Endeavour	Crew vessel
Enterprise	Crew vessel
Meriel D	Crew vessel
Strider	Crew vessel
Distributor	Crew vessel
Supporter	Crew vessel
Voyageur	Crew vessel
Brockelsby	Guard vessel
Bever	Tug
Stevns Arctic	Tug
Meander	Tug
Osprey Boxer	Tug
Shaolbuster	Tug
Red Wolf	Tug
Typhoon	Tug
Blizzard	Tug
Sea Jack	Jack Up
MPI Resolution	Jack Up (DP)
Polar Prince	Cable lay (DP)
Normand Mermaid	Cable lay (DP)
UR101	Cable lay barge
Stanislav Yudin	Heavy lift ship
Maggie M	Multicat
M/S Line	Survey
Arie Dirk	Environmental (Birds)
Forth Joustier	Multicat
Voe Viking	Multicat
Xplorer	Diving Vessel
Oil Express	Diving Support Vessel
Voe Chief	Diving Vessel

NOTES

This document will be issued every Monday and will describe the planned activities for the next 7 days. Normal liaison for offshore operations is between the TOW Marine Coordinator and:

- Captain Rob Brown – Interim Harbour Master Port of Ramsgate; and
- Kaimes Beasley – CNIS Manager Dover MCA

This weekly report will be distributed to those recipients listed on the email address header on a weekly basis and is intended to inform those recipients of TOW's planned activities over the forthcoming week.

For further information or comments please contact:

The Duty Marine Coordinator:

Office: +44 (0) 1843 572130

Mobile: +44 (0) 7825880528

Fax: +44 (0) 1843 572131

Email: marinecoordinator@thanetoffshorewind.com
