

Thanet Offshore Wind Limited


# Weekly Notice of Operations to Stakeholders

---

Date of Notice 06/07/09

Notice No.16

---

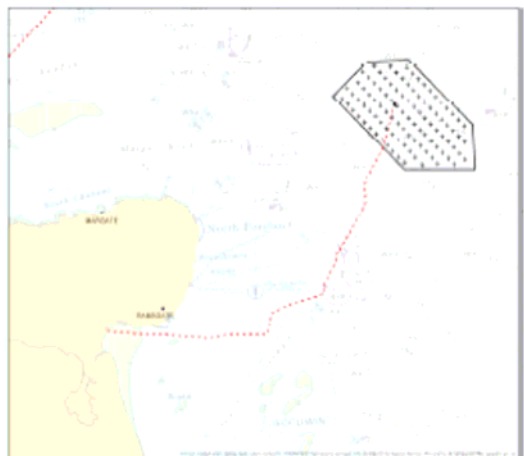

## Distribution

See e-mail address header


**WORK PLANNED FOR PERIOD: FROM 06/07/09 TO 12/07/09**

<b>Description:</b> (subject to weather conditions)
• 06/07/09 – Sea Jack departs Ramsgate to install E06. Resolution on location and installing TP at F14
• 07/07/09 – Sea Jack installs E06 and relocates to E07. Resolution completes TP-F14 and relocates to F11
• 08/07/09 – Sea Jack completes E07 and departs Field to Ramsgate. Resolution Installing TP F11
• 09/07/09 – Sea Jack in Ramsgate and load-out G01 and G04 and returns to field. Resolution completes TP11 and departs field to Vlissingen
• 10/07/09 – Sea Jack installs G01 and moves to G04. Resolution in Vlissingen and load-out TP's C14, C15, D16, D17, D10 and D11
• 11/07/09 – Sea Jack installs G04. Resolution in Vlissingen mobilising monopile cleaner
• 12/07/09 – Sea Jack completes G04 and returns to Ramsgate for F03 & F04 load-out. Resolution departs Vlissingen and returns to field
• Stevns Arctic and Bever tow tugs and field support for Sea Jack.
• Osprey Fighter towing monopile supply barges to / from Ramsgate & Vlissingen.
• Crew boat Meriel D performing Marine Mammal Observations and various crew changes and transfers
• Crew boat Offshore Performer (OP3) assisting crew changes / transfers and monopile cleaning - TP maintenance.
• Guard boat Brocklesby in field for monitoring vessel movements and collision avoidance

**WORK COMPLETED FROM: 28/06/09 TO 06/07/09**

<b>Date</b>	<b>Description</b>
29/06/09	• Complete installation of TP-C09. Monopile G02 installed
30/06/09	• Monopile F01 installed with temporary marker
01/07/09	• Complete installation of TP-F12
02/07/09	• Monopile F02 installed with temporary marker
03/07/09	• Complete installation of TP-D15
04/07/09	• Complete installation of TP-E16. Monopile E14 installed
05/07/09	• Complete Installation of TP-E15

FIELD STATUS REPORT 5<sup>TH</sup> JULY 2009

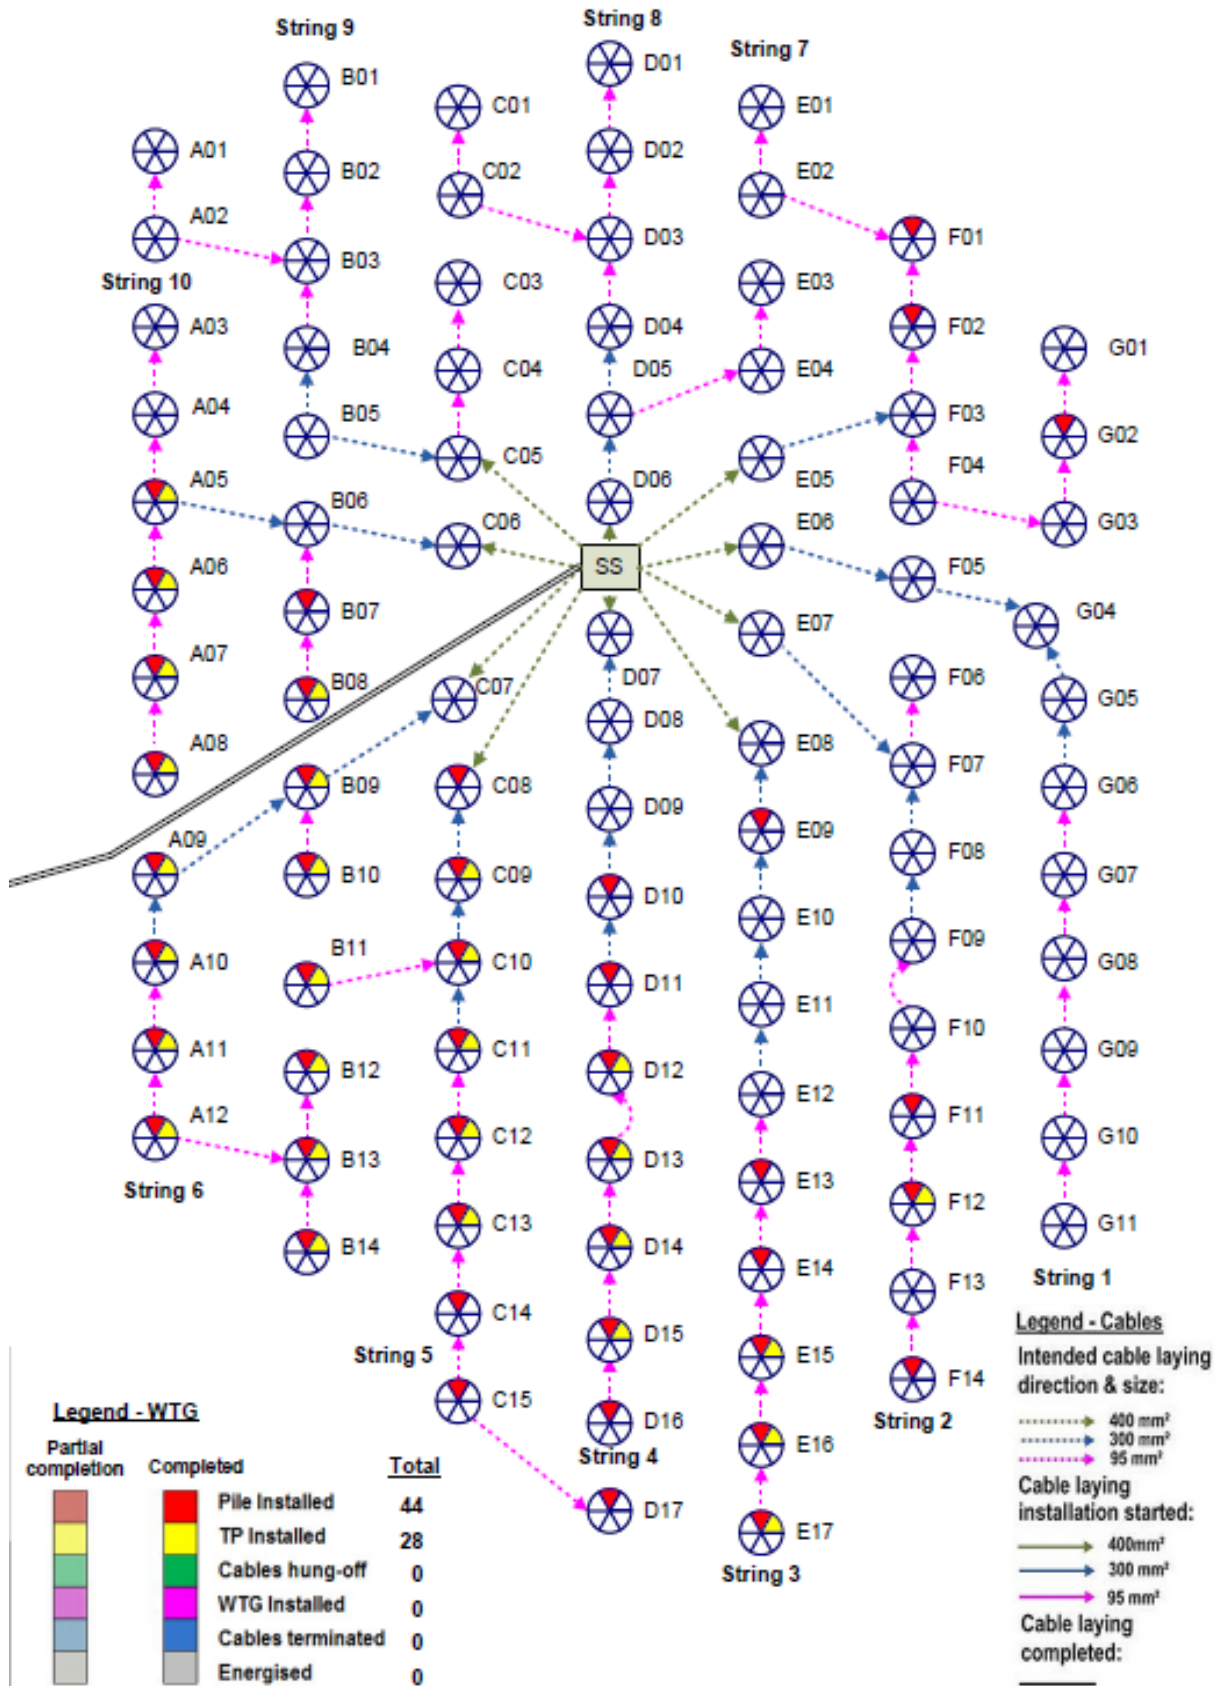

## ON PROJECT VESSEL LIST :

Name	Type
Offshore Performer(OP3)	Crew vessel
Meriel D	Crew vessel
Bever	Tug
Sea Jack	Jack Up
Stevns Arctic	Tug
MPI Resolution	Jack Up (SP)
Brocklesby	Guard vessel
Meander	Tug
Osprey Fighter	Tug

## NOTES

This document will be issued every Monday and will describe the planned activities for the next 7 days. Normal liaison for offshore operations is between the TOW Marine Supervisor and:

- Captain Dominic Evans – Harbour Master Port of Ramsgate; and
- Kaimes Beasley – CNIS Manager Dover MCA

This weekly report will be distributed to those recipients listed on the email address header on a weekly basis and is intended to inform those recipients of TOW's planned activities over the forthcoming week.

For further information or comments please contact:

### **The Duty Marine Coordinator:**

**Office:** +44 (0) 1843 572130

**Mobile:** +44 (0) 7825880528

**Fax:** +44 (0) 1843 572131

**Email:** marinesupervisor@thanetoffshorewind.com
