


Thanet Offshore Wind Limited

Weekly Notice of Operations to Stakeholders

Date of Notice 19/10/09

Notice No.31

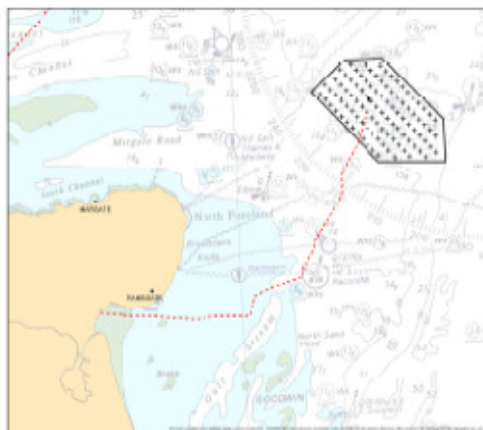

Distribution

See e-mail address header


WORK PLANNED FOR PERIOD: FROM 19/10/09 TO 25/10/09

Description: (subject to weather conditions)
19/10/09 – Resolution on location A03 installing a TP. SeaJack on location B02 installing a MP. Polar Prince laying cable C11 to C12.
20/10/09 – Resolution WOW, Sea Jack WOW, Polar Prince in Sheerness spooling cable to barge UR101.
21/10/09 – Resolution WOW, Sea Jack WOW. Polar prince WOW.
22/10/09 – Resolution on snagging list items. Sea Jack install MP at B03. Polar Prince cable lay C10 to C09 & D16 to D15.
23/10/09 – Resolution install TP on B02. Sea Jack in Ramsgate. Polar Prince cable lay D15 to D14 & D14 to d13. Cable barge UR101 on site cable lay A12 to B13.
24/10/09 – Resolution install TP on B03. Sea Jack install MP on B01.
25/10/09 – Resolution install TP on B01. Sea Jack install MP on D06. Polar Prince cable lay D13 to D12 & D12 to D11.
<ul style="list-style-type: none"> • Tugs Stevns Arctic and Bever tow tugs and field support for Sea Jack. • Tug Osprey Fighter towing 2onopole supply barges to / from Ramsgate & Vlissingen. • Tug Meander assisting Sea Jack and Osprey Fighter as required. • Tug Keverne to assist the non-propelled barge UR101 as required. • Multicat Voe Jarl performing Prelay grapnel run operations in field. • DP Ship Polar Prince cable laying – Inter array cables between turbine foundations. • Crew boat Waterfall performing Marine Mammal Observations and various crew changes and transfers. • Crew boat Offshore Performer (OP3) assisting with crew changes / transfers & TP maintenance. • Crew boat Sea Weasel for crew changes to Polar Princes & barges (Subocean). • Sander performing post laid cable surveys. • Guard boat Brocklesby in field for monitoring vessel movements and collision avoidance.

WORK COMPLETED FROM: 12/10/09 TO 19/10/09

Date	Description
12/10/09	<ul style="list-style-type: none"> Resolution snag items at A01, A07 & A04. Polar Prince install cable B09 to A09.
13/10/09	<ul style="list-style-type: none"> Resolution snag items at A04, B08, E11. Polar Prince install cable C10 to C11.
14/10/09	<ul style="list-style-type: none"> Resolution snag items at e11, F11, D15. Polar Prince install cable B11 C10.
15/10/09	<ul style="list-style-type: none"> Resolution snag items at D15 & C15 then departed for Vlissingen.
16/10/09	<ul style="list-style-type: none"> Waiting on weather.
17/10/09	<ul style="list-style-type: none"> Waiting on weather.
18/10/09	<ul style="list-style-type: none"> Polar Prince, cable preparations

Field Status Report 18th October 2009

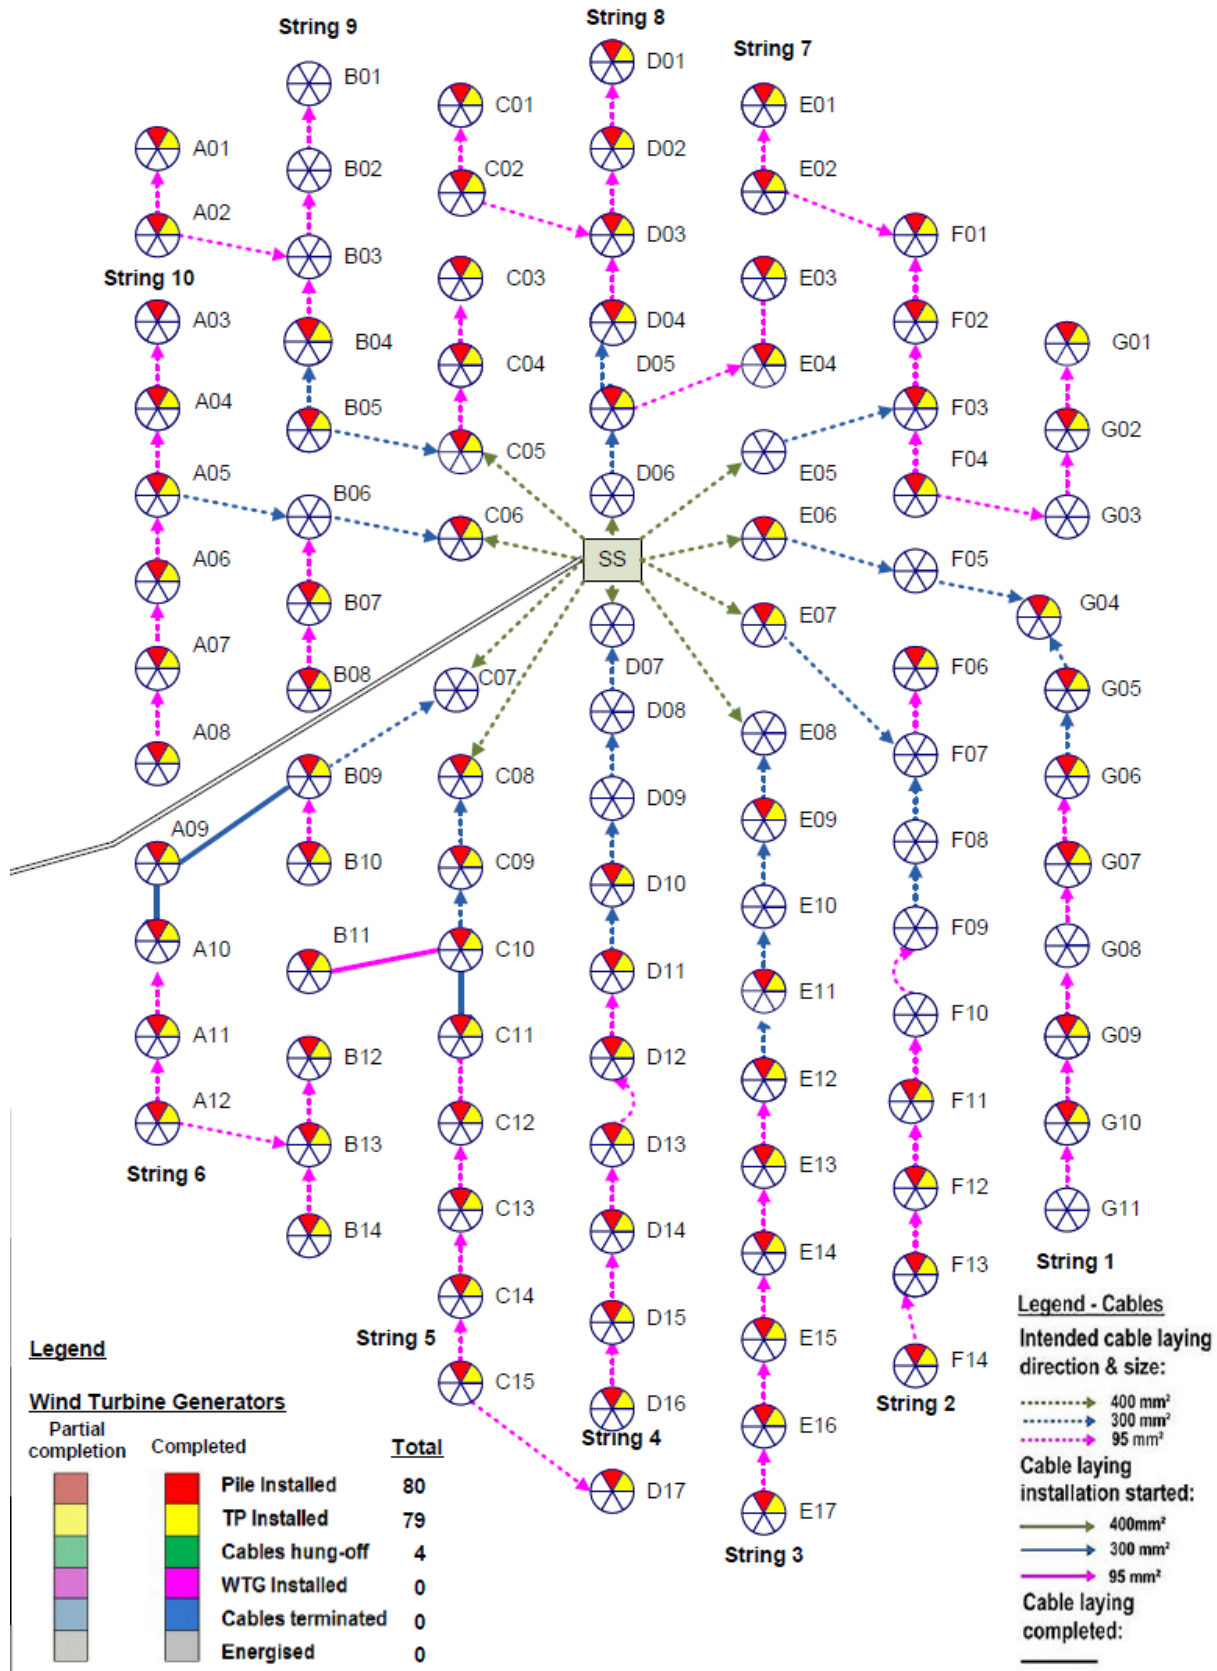

ON PROJECT VESSEL LIST :

Name	Type
Offshore Performer(OP3)	Crew vessel
Waterfall	Crew vessel
Sea Weasel	Crew vessel
Bever	Tug
Sea Jack	Jack Up
Stevns Arctic	Tug
MPI Resolution	Jack Up (DP)
Brocklesby	Guard vessel
Meander	Tug
Osprey Fighter	Tug
Polar Prince	Survey (DP)
Voe Jarl	Multicat
Sander	Survey
Arie Dirk	Environmental (Birds)

NOTES

This document will be issued every Monday and will describe the planned activities for the next 7 days. Normal liaison for offshore operations is between the TOW Marine Coordinator and:

- Captain Rob Brown – Interim Harbour Master Port of Ramsgate; and
- Kaimes Beasley – CNIS Manager Dover MCA

This weekly report will be distributed to those recipients listed on the email address header on a weekly basis and is intended to inform those recipients of TOW's planned activities over the forthcoming week.

For further information or comments please contact:

The Duty Marine Coordinator:

Office: +44 (0) 1843 572130

Mobile: +44 (0) 7825880528

Fax: +44 (0) 1843 572131

Email: marinecoordinator@thanetoffshorewind.com
