


Thanet Offshore Wind Limited

Weekly Notice of Operations to Stakeholders

Date of Notice 08/06/09

Notice No.12

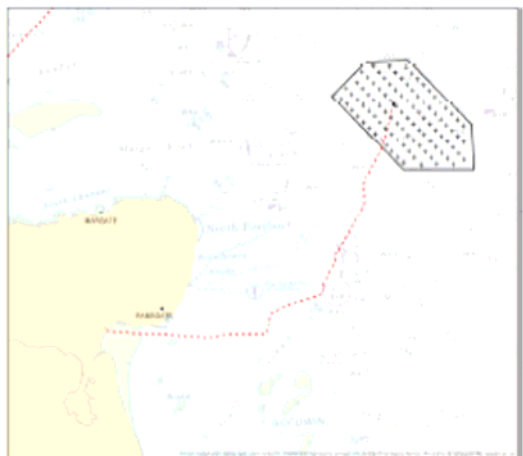

Distribution

See e-mail address header


WORK PLANNED FOR PERIOD: FROM 8/06/09 TO 14/06/09

Description: (subject to weather conditions)
• 07/06/09 – Resolution arrives on site and positions at E17
• 08/06/09 – Sea Jack completes installation of pile at E13 and sails to Ijmuiden.
• 09/06/09 – Resolution completes TP E17 and relocates to B11
• 10/06/09 – Resolution begins installing TP B11
• 11/06/09 – Resolution completes TP B11 and relocates to C11
• 12/06/09 – Resolution begins installing TP C11
• 13/06/09 – Resolution completes TP C11 and relocates to C10
• 14/06/09 – Resolution begins installing TP C10
• Sea Jack assisted in above by tugs Stevns Arctic and Bever and standby in Ijmuiden
• Osprey Fighter remains on standby in Vlissingen
• Tug Meander will depart Ramsgate for dry dock after Sea Jack has completed and cleared the field
• Crew boat Meriel D performing Marine Mammal Observation duties and assist in crew changes from Resolution
• Crew boat Offshore Performer (OP3) monitoring entrance current at Ramsgate for towage operations, assisting crew changes for Sea Jack & Resolution and monopile cleaning and TP maintenance.
• Guard boat Brocklesby in field for monitoring vessel movements and collision avoidance

WORK COMPLETED FROM: 31/05/09 TO 08/06/09

Date	Description
31/05/09	• Installed TP B10
03/06/09	• Installed C14 & D16 with temporary navigation marks.
03/06/09	• Installed TP B12
05/06/09	• Installed TP C12
07/06/09	• Installed D11 with temporary navigation mark
08/06/09	• Installed E13 with temporary navigation mark

FIELD STATUS REPORT 8TH JUNE MAY 2009

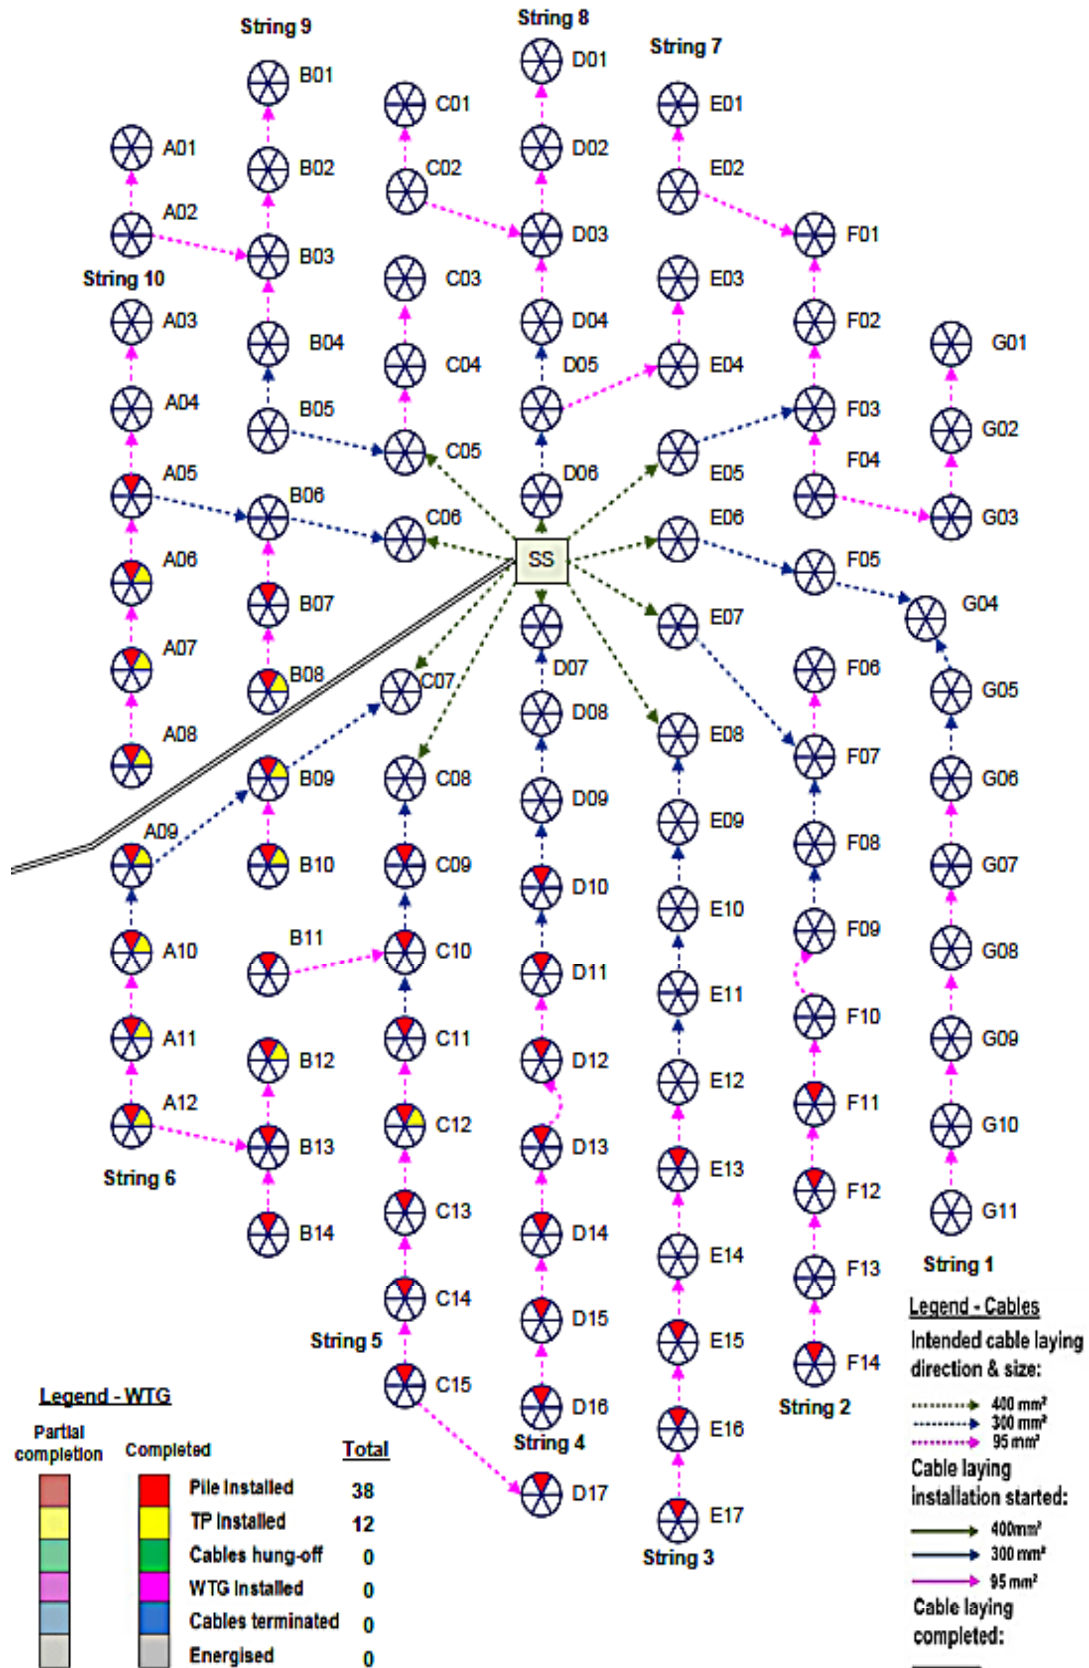

ON PROJECT VESSEL LIST :

Name	Type
Offshore Performer(OP3)	Crew vessel
Meriel D	Crew vessel
Bever	Tug
Sea Jack	Jack Up
Stevns Arctic	Tug
MPI Resolution	Jack Up (SP)
Brocklesby	Guard vessel
Meander	Tug
Osprey Fighter	Tug

NOTES

This document will be issued every Monday and will describe the planned activities for the next 7 days. Normal liaison for offshore operations is between the TOW Marine Supervisor and:

- Captain Dominic Evans – Harbour Master Port of Ramsgate; and
- Kaimes Beasley – CNIS Manager Dover MCA

This weekly report will be distributed to those recipients listed on the email address header on a weekly basis and is intended to inform those recipients of TOW's planned activities over the forthcoming week.

For further information or comments please contact:

The Duty Marine Coordinator:

Office: +44 (0) 1843 572130

Mobile: +44 (0) 7825880528

Fax: +44 (0) 1843 572131

Email: marinesupervisor@thanetoffshorewind.com
